

May 2012 Monthly Report



MACHADO LAKE ECOSYSTEM REHABILITATION PROJECT PLAN SIGNING

Administrative Oversight Committee

Miguel Santana, City Administrative Officer, Chair Andrea A. Alarcón, Board of Public Works Gerry Miller, Chief Legislative Analyst Ronald Nichols, Department of Water and Power Romel Pascual, Office of the Mayor

Citizens Oversight Advisory Committee

Adi Liberman, Chair Dayna Bochco Francine Diamond Mark Gold Tiger Kang Miguel Luna Cynthia McClain-Hill Craig A. Perkins M. Teresa Villegas

PREPARED BY BUREAU OF ENGINEERING PROP O BOND DIVISION





Distribution List

Miguel Santana, City Administrative Officer Andrea A. Alarcón, President Gerry F. Miller, Chief Legislative Analyst Ronald Nichols, General Manager Romel Pascual, Deputy Mayor Adi Liberman, Chair Dayna Bochco Francine Diamond Mark Gold Tiger Kang Miguel Luna Cynthia McClain-Hill Craig A. Perkins M. Teresa Villegas Jerilyn Lopez Mendoza, Vice President John J. Choi, Commissioner Steven T. Nutter, Commissioner Valerie Lynne Shaw, Commissioner Gary Lee Moore, City Engineer John L. Reamer, Jr., Director Nazario Sauceda, Director Enrique C. Zaldivar, Director Victoria Santiago, Director Jon Kirk Mukri, General Manager Kenneth R. Redd, Deputy City Engineer Adel H. Hagekhalil, Assistant Director Edward Jordan, Assistant City Attorney David H. Hirano Rafael E. Prieto Charles E. Modica Michael E. Mullin David Pettijohn Shahram Kharaghani Kendrick K. Okuda

Monthly Progress Report - May 2012

Office of the City Administrative Officer (CAO) Board of Public Works Office of the Chief Legislative Analyst (CLA) Department of Water and Power (DWP) Mavor's Office Citizens Oversight Advisory Committee Citizens Oversight Advisory Committee **Citizens Oversight Advisory Committee** Citizens Oversight Advisory Committee **Board of Public Works Board of Public Works Board of Public Works** Board of Public Works Bureau of Engineering (BOE) Bureau of Contract Administration **Bureau of Street Services** Bureau of Sanitation (BOS) Board of Public Works, Office of Accounting Department of Recreation & Parks (RAP) BOE BOS City Attorney's Office CAO CLA CLA Mayor's Office DWP BOS BOE

Comments or suggestions regarding the Proposition O Monthly Report may be directed to Kendrick K. Okuda, BOE Proposition O Implementation Program Manager, at 213-485-1165 or email at Kendrick.Okuda@lacity.org

This report is available for viewing online at the Bureau of Engineering website: http://eng.lacity.org/projects/prop_o/report2012.htm





TABLE OF CONTENTS

Section

Page

1.0	Execu	utive Su	ummary	
	1.1	Progra	am Summary	4
		1.1.1		4
		1.1.2	Key Issues	
		1.1.3		
	1.2	Bond	Sales	7
	1.3	Projec	ct Status Summary	8
		1.3.1	COAC & AOC Project Funding Recommendations	8
			1.3.1.1 COAC & AOC Project Recommendations	8
		1.3.2	Projects in Implementation	9
		1.3.3		10
			1.3.3.1 Project Budget Summary	10
			1.3.3.2 Program Budget Summary	11
			1.3.3.3 Project Funding Summary	12
2.0	<u>Sche</u>	<u>dule</u>		
	2.1	Projec	ct Schedules	13
	2.2		am Master Schedule	14
3.0	<u>Budg</u>	<u>et</u>		
	3.1	Budge	et vs. Actual Expenditure	15
4.0	<u>Proje</u>	ct Statu	<u>IS</u>	
	4.1	Projec	ct Status Report	19
5.0	<u>Appe</u>	<u>ndix</u>		
	5.1	Map o	of Proposition O Projects Approved for Implementation	29
	5.2	Table	of Catch Basin Retrofits Screen Covers and Inserts by Council Districts	30
	5.3	Counc	cil District Map	31



1.0 EXECUTIVE SUMMARY

1.1 Program Summary

In November 2004, voters of the City of Los Angeles passed the Proposition O - Clean Water Bond, authorizing \$500 million of general obligation bonds for projects to protect public health by cleaning up pollution in the City's rivers, lakes, and beaches. The projects are intended to assist the City of Los Angeles in meeting Federal Clean Water Act requirements. Proposition O - Clean Water Bond will also fund improvements to protect water quality, provide flood protection, increase water conservation, provide habitat protection, and create open space.

This monthly progress report summarizes the status of activities and progress of the Proposition O - Clean Water Bond program, for May 2012.

1.1.1 <u>Citizens Oversight Advisory Committee (COAC)</u>, <u>Administrative Oversight</u> <u>Committee (AOC)</u>, and <u>Other highlights</u>

- The May 16th COAC meeting was canceled.
- The May 31st AOC meeting was canceled.



1.1.2 Key Issues

- Projects with American Recovery and Reinvestment Act (ARRA) funding
 - Mar Vista Recreation Center Storm Water BMP (Mar Vista)
 - Santa Monica Bay Low Flow Diversion Upgrades Pkg. 1 (LFD Pkg.1)
 - Santa Monica Bay Low Flow Diversion Upgrades Pkg. 2 (LFD Pkg.2)
 - Issue: Mar Vista, LFD Pkg. 1, and LFD Pkg. 2 are receiving ARRA funding and need to comply with the ARRA requirements.
 - **Status:** To date, 90% of the ARRA Grant funds have been received. The remaining balance is being held as retention, pending the submittal and approval of final project reports.
 - Action: Bureau of Sanitation will prepare and submit the necessary reports to the grantor.

Albion Dairy Demolition and Remediation Project

- **Issue:** Unforeseen soil contamination was discovered under the foundations of two buildings that were demolished.
- Status: Two underground fuel tanks were removed under the direction of the Los Angeles Fire Department (LAFD) and the LAFD referred environmental regulation of the project to the Los Angeles Regional Water Quality Control Board (LARWQCB). The project team met with Executive Director and members of LARWQCB staff to develop a work plan for additional remediation and monitoring. LARWQCB required additional soil sampling, groundwater monitoring, and soil vapor sampling prior to evaluating and approval of further remediation.
- Action: On May 17, 2012, Prop O staff met with the LARWQCB staff to discuss the work plan and additional remediation proposal.

• Machado Lake Phase 1 (Wilmington Drain) Project

- Issue: This project is on Los Angeles County Flood Control District (LACFCD) Property. LACFCD requirements for this project include increasing the capacity of the Wilmington Drain channel by removing sediment from the channel at LACFCD's cost. The agreement between the City (BOS) and LACFCD has not been finalized; but it is needed to secure the needed funding from LACFCD in order to proceed with construction. The Wilmington Drain channel maintenance agreement between the LACFCD and California Department of Fish and Game (CDFG) need to be resolved.
- Status: LACFCD and the CDFG have a difference of opinion on maintenance of channel. Prop O team is facilitating a resolution on maintenance agreement with CDFG. A meeting has been scheduled, on May 22, 2012, with CDFG, LACFCD and the City to resolve issues regarding Section 2081, California Endangered Species Act (CESA) permit.
- Action: In response to CDFG request, the city prepared report with impacts to Least Bell's Vireo (LBV) use areas resulting from the construction of the Project.

• Santa Monica Bay Low Flow Diversion Upgrades Pkg. 3 Project

- Issue: Excavations to verify utility locations revealed an underground Southern California Edison vault and duct bank. They are in conflict with approximately 900 feet of the new 48 inch sewer pipe that will be constructed under this project.
- Status: A design revision to re-align the sewer away from the conflicting utility has been completed. California Department of Transportation (Caltrans) encroachment permit amendment was issued. The AOC and the Board of Public Works have authorized the deletion of the southerly 900 foot reach of sewer pipe installation. Issue has been solved on this construction contract.
- **Action:** Project team will issue change order to delete the southerly 900 foot reach of sewer pipe installation. Deleted work will be done under a new construction contract.



Key issues cont'd

• South LA Wetlands Park Project

- **Issue:** The daily drop of the wetland water surface elevation appears to exceed expected evaporation rates.
- **Status:** An evaluation of alternatives to identify cause of water elevation drop and to mitigate water losses is on-going.
- Action: Alternatives are being prepared for evaluation.


Westchester Stormwater BMP Project

- **Issue:** Land use agreement between the City (BOS) and Los Angeles World Airport (LAWA) has not been finalized.
- Status: Meeting with Mayor's Office, CLA, City Attorneys Office, BOS, LAWA, and BOE held to resolve this issue.
- Action: City Attorney, LAWA, and BOS are working to document and finalize resolution of land use issues.

1.1.3 Project Community Meetings Schedule

The following is a list of Proposition O project meetings with the public that occurred in May and are planned for the month of June.

		COMMUNIT	Y MEETINGS	
Date	Time	Project	Group	Location
5/23/12	11:00 AM	Santa Monica Bay Low Flow Diversion Upgrades Package 3 and Temescal Canyon Park Stormwater BMP Phase 1	PCH Taskforce Quarterly Meeting	Caltrans, District 7 100 S. Main Street Los Angeles, CA 90012 Room 1-040A



1.2 Bond Sales

The following table is a summary of the bond sales that fund Proposition O.

PROPOSITION O	BOND SALE SUI		¢500.000.000
General Obligation Bonds Approved by Voters			\$500,000,000
Total Bond Sales to Date			\$439,500,000
Fund 16F July 13, 2005 City Council Approved Bond Sale (Ord. 176839 CF 05-1408)		\$37,000,000	
Bond Interest Earnings (As of November 2011)	\$3,056,910		
Fund 16M July 21, 2006 City Council Approved Bond Sale (Ord. 177733 CF 06-0600-S37)		\$8,000,000	
Bond Interest Earnings (As of November 2011)	\$867,352		
Fund 16Q July 22, 2008 City Council Approved Bond Sale (Ord. 180090 CF 08-1706)		\$101,000,000	
Bond Interest Earnings (As of November 2011)	\$5,559,580		
Fund 16T July 21, 2009 City Council Approved Bond Sale (Ord. 180808 CF 09-1674)		\$176,500,000	
Bond Interest Earnings (As of November 2011)	\$7,831,469		
Fund 16V July 28, 2011 City Council Approved Bond Sale (Ord. 181755 CF 11-0841)		\$117,000,000	
Bond Interest Earnings (As of November 2011)	<u>\$ 932,800</u>		
Total Bond Interest Earnings to Date	\$18,230,111		
General Obligation Bonds Remaining to be S	-1.1		\$60,500,00

1.3 Project Status Summary

1.3.1 COAC & AOC Funding Recommendations (Pending Mayor Approval)

The following table summarizes the projects approved and recommended by COAC and AOC for funding. The projects will be presented to the City Council and Mayor for approval.

	PROJECTS RECOMMENDED FOR FUNDING BY COAC AND AOC											
Project Title	Applicant	Prop O Funding Request	Prop O Set Aside Funds Request	Funds From Other Sources (if applicable)	Total Project Funding Needed		O Funding mendations	Month/Year Recommended by COAC & AOC				
						COAC	AOC					
N/A	N/A	\$0	\$0	\$0	\$0	\$0	\$0	N/A				
				TOTALS								
		\$0	\$0	\$0	\$0	\$0	\$0					

1.3.1.1 COAC & AOC Project Recommendations (Pending Funding Availability)

The following table summarizes the projects approved by COAC and AOC, pending availability

PROJECTS RECOMMENDED BY COAC AND AOC										
Project Title	Applicant	Prop O Funding Request	Prop O Set Aside Funds Request	Funds From Other Sources (if applicable)	Total Project Funding Needed	Month/Year Recommended by COAC & AOC				
Aliso Creek & Limekiln Creek Restoration	Mountains Recreation and Conservation Authority	\$7,842,042*	\$0	\$0	\$7,842,042	July 2007				
Boyle Heights Joint Use Community Center	City of LA, Council District 14	\$2,291,000*	\$0	\$528,000	\$2,819,000	July 2007				
			TOTALS							
		\$10,133,042	\$0	\$528,000	\$10,661,042					

* No Proposition O funding is available to fund this project at this time.



1.3.2 Projects in Implementation (Approved by City Council & Mayor)

The following table lists the projects approved for Proposition O funding by the City Council and the Mayor.

PROJEC	CTS IN IMPLEMEN			
Project Title	Prop O Funding Approved	Prop O Set Aside	Total Project	Potential Funds From Other Sources*
Projects in Pre-Design	Approved	Approved	Budget	Other Sources
Penmar Water Quality Improvement Phase II	\$2,830,200	\$0	\$2,830,200	\$0
emescal Canyon Park Stormwater BMP Phase II	\$3,698,565	\$0 \$0	\$3,698,564	\$0
and Acquisition Projects	ψ0,000,000	ΨΟ	¥3,030,304	ψυ
aylor Yard River Park – Parcel G2 Land Acquisition	\$0	\$12,440,000	TBD	TBD
Projects in Design	ψυ	\$12,440,000	IBD	IDD
Glenoaks/Sunland Stormwater Capture	\$508,696	\$0	\$508,696	\$0
Strathern Wetlands Park	\$7,800,000	\$0 \$0	\$22,000,000	\$14,200,000
Vestchester Stormwater BMP		\$0 \$0	\$22,000,000	\$14,200,000
	\$32,722,000	Ф О	\$32,722,000	ΦU
Projects in Bid & Award	¢000.000	* 0	¢4.075.000	¢ 440.000
Elmer Avenue Phase II: Elmer Paseo	\$829,000	\$0	\$1,275,000	\$446,000
Achado Lake Ecosystem Rehabilitation	\$99,523,897	\$0	\$99,523,897	\$956,997
Aachado Lake Phase I (Wilmington Drain)	\$21,049,911	\$0	\$21,049,911	\$4,397,500*
Projects in Construction	#0.070 (00	*	0 0.050.100	
Ibion Dairy Park – Demolition & Remediation	\$3,956,400	\$0	\$3,956,400	\$3,577,476
Catch Basin Opening Screen Covers Phase III	\$44,500,000	\$0	\$44,500,000	\$0
cho Park Lake Rehabilitation	\$84,263,313	\$0	\$84,263,313	\$599,875
Penmar Water Quality Improvement Phase I	\$20,754,800	\$0	\$20,754,800	\$0
Rosecrans Recreation Center Stormwater Enhancements	\$4,829,119	\$0	\$6,754,033	\$1,924,914
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 3	\$20,634,036	\$0	\$20,634,036	\$7,000,000
South Los Angeles Wetlands Park (includes Site Readiness)	\$16,678,202	\$0	\$26,374,067	\$13,001,866*
Femescal Canyon Park Stormwater BMP Phase I	\$14,947,435	\$0	\$14,947,436	\$0
Projects in Post Construction	-			
lansen Dam Wetlands Restoration	\$2,220,702	\$0	\$2,517,702	\$297,000
los Angeles Zoo Parking Lot	\$13,904,243	\$0	\$13,904,243	\$0
Iar Vista Recreation Center Stormwater BMP	\$4,556,186	\$0	\$4,556,186	\$2,077,838*
Peck Park Canyon Enhancement	\$6,190,000	\$0	\$8,231,118	\$2,041,118*
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 2	\$3,380,111	\$0	\$3,380,111	**
Vestside Park Rainwater Irrigation	\$6,904,589	\$0	\$8,304,589	\$3,192,038*
Projects Completed				
Albion Dairy Park – Land Acquisition	\$17,560,000	\$0	TBD	TBD
Catch Basin Inserts and Coverings Phase I	\$14,702,886	\$0	\$14,702,886	\$600,000*
Catch Basin Opening Screen Covers Phase II	\$9,362,404	\$0	\$9,362,404	\$0
Cesar Chavez Ground Water Improvement (a.k.a Sheldon Arleta)	\$3,040,000	\$0	\$9,841,230	\$6,801,230
Grand Blvd. Tree Wells	\$780,282	\$0	\$780,282	\$350,000*
mperial Highway Sunken Median Stormwater BMP	\$2,723,403	\$0	\$2,723,403	\$0
nner Cabrillo Beach Bacterial Water Quality Improvement	\$8,000,000	\$0	\$16,000,000	\$8,000,000
a Cienega/Fairfax Stormwater BMP (CANCELED)	\$668,159	\$0	\$668,159	\$0
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 1	\$6,814,377	\$0	\$6,814,377	\$5,131,497**
Dros Green Street	\$197,600	\$0	\$784,251	\$586,651
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 4	\$6,290,504	\$0	\$6,290,504	**
Strathern Pit Multiuse - Land Acquisition	\$10,000,000	\$0	\$28,000,000	\$18,000,000
Vestminster Dog Park Stormwater BMP	\$1,438,755	\$0	\$1,438,755	\$0
	TOTALS		,	· -
	\$498,259,775	\$12,440,000	\$544,092,553	\$78,982,000



1.3.3 Project and Program Budget Summary

1.3.3.1 Total Project Budget Summary

The following table is a summary of the Proposition O project funding.

PROJECT BUDGET SUMMARY							
Description	Prop O Funding	Prop O Set Aside	Potential Funds From Other Sources*	Total Project Budget			
Projects In Planning– Prop O Funding Request	\$0	\$0	\$0	\$0			
Projects Recommended by AOC	\$0	\$0	\$0	\$0			
Projects In Implementation	\$498,259,775	\$12,440,000	\$78,982,000	\$544,092,553			
		тот	ALS				
	\$498,259,775	\$12,440,000	\$78,982,000	\$544,092,553			
Prop O Total Project Obligation	\$510,6	99,775					

*Estimated grant funds/reimbursements that may be available

1.3.3.2 Program Budget Summary

The table on the following pages gives an updated program budget summary for Proposition O.

1.3.3.3 Project Funding Summary


The table on the following pages gives an updated project funding summary for Proposition O.

Prop O - Program Budget Summary

		uncil / Mayor	Approved		Cost		op O Budget
Project Title		Approved	Set-Asides	Future Needs	Reductions		& Funding
Albion Dairy Park - Demolition & Remediation	\$	3,956,400				\$	3,956,400
Albion Dairy Park - Land Acquisition - COMPLETED	\$	17,560,000				\$	17,560,000
Aliso Wash - Limekiln Creek Confluence Restoration	\$	-				\$	-
Boyle Heights Joint Use Community Center Improvements	\$	-				\$	-
Catch Basin Inserts and Coverings Phase I - COMPLETED	\$	17,000,000			\$ (2,297,114)		14,702,886
Catch Basin Opening Screen Covers Phase II - COMPLETED	\$	10,000,000			\$ (637,596)	\$	9,362,404
Catch Basin Opening Screen Covers Phase III Cesar Chavez Ground Water Improvement	\$ \$	44,500,000 3,040,000				\$ \$	44,500,000
Echo Park Lake Rehabilitation	۰ \$	84,263,313				ф \$	84,263,313
Elmer Avenue Phase II: Elmer Paseo	\$	829,000				\$	829,000
Glenoaks/Sunland Stormwater Capture	\$	508,696				\$	508,696
Grand Blvd. Tree Wells - COMPLETED	\$	1,075,927			\$ (295,645)	\$	780,282
Hansen Dam Wetlands Restoration	\$	2,220,702				\$	2,220,702
Imperial Highway Sunken Median Stormwater BMP	\$	2,723,403				\$	2,723,403
Inner Cabrillo Beach Bacterial Water Quality Improvement La Cienega/Fairfax Stormwater BMP - CANCELED	\$ \$	8,000,000 7,667,887		-	\$ (6,999,728)	\$ \$	<u>8,000,000</u> 668,159
Los Angeles Zoo Parking Lot	э \$	13.904.243			\$ (0,999,720)	э \$	13,904,243
Machado Lake-Phase I (Wilmington Drain)	\$	21,049,911				\$	21,049,911
Machado Lake Ecosystem Rehabilitation	\$	99,523,897				\$	99,523,897
Mar Vista Recreation Center Stormwater BMP	\$	4,556,186		<u> </u>	<u> </u>	\$	4,556,186
Oros Green Street - COMPLETED	\$	386,000			\$ (188,400)	\$	197,600
Peck Park Canyon Enhancement	\$	6,190,000				\$	6,190,000
Penmar Water Quality Improvement Phase I	\$	20,754,800				\$	20,754,800
Penmar Water Quality Improvement Phase II	\$	2,830,200				\$	2,830,200
Rosecrans Recreation Center Stormwater Enhancements Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 1	\$ \$	4,829,119 6,814,377				\$ \$	4,829,119
Santa Monica Bay Low Flow Diversion Opgrades, Pkg. 1 Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 2	\$ \$	3.380.111				⇒ \$	<u>6,814,377</u> 3,380,111
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 2	φ \$	20,634,036				ф \$	20,634,036
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 4	\$	6,290,504				\$	6,290,504
South Los Angeles Wetlands Park (includes Site Readiness)	\$	16,678,202				\$	16,678,202
Strathern Pit Multiuse - Land Acquisition	\$	10,000,000				\$	10,000,000
Strathern Wetlands Park	\$	7,800,000				\$	7,800,000
Taylor Yard River Park - Parcel G2 Land Acquisition			\$ 12,440,000			\$	12,440,000
Temescal Canyon Park Stormwater Phase I	\$	14,947,435				\$	14,947,435
Temescal Canyon Park Stormwater Phase II	\$	3,698,565				\$	3,698,565
Westchester Stormwater BMP Westminster Dog Park Stormwater BMP	\$ \$	<u>32,722,000</u> 1,438,755				\$ \$	<u>32,722,000</u> 1,438,755
Westhinster Dog Park Stormwater Dor Westside Park Rainwater Irrigation	φ \$	6,904,589				φ \$	6,904,589
Total - Project Budget			\$ 12,440,000	\$ -	\$ (10,418,483)	•	
City Staff - Program Related Budget (as of June 30, 2011)	Ψ.	500,070,250	\$ 12,440,000	Ψ	\$ (10,410,403)	Ψ	310,033,773
				\$ 491,450		•	1,079,173
Office of Accounting	\$	587,723		φ 491,450		\$	
	\$	587,723		\$ 491,430		\$ \$	-
Office of Accounting Bureau of Contract Administration Bureau of Engineering	\$	2,003,796		\$ 2,504,606		\$ \$	
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation	\$ \$	2,003,796 4,081,839		\$ 2,504,606 \$ 2,586,746		\$ \$ \$	6,668,585
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation Related Costs	\$ \$ \$	2,003,796 4,081,839 2,333,524		\$ 2,504,606 \$ 2,586,746 \$ 1,746,497		• • • • •	6,668,585 4,080,021
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation Related Costs Subtotal	\$ \$ \$	2,003,796 4,081,839		\$ 2,504,606 \$ 2,586,746		\$ \$ \$	6,668,585 4,080,021
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011)	\$ \$ \$ 1	2,003,796 4,081,839 2,333,524 9,006,882		\$ 2,504,606 \$ 2,586,746 \$ 1,746,497	¢ (136)	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	6,668,585 4,080,021 16,336,18 1
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation	\$ \$ \$ \$ \$	2,003,796 4,081,839 2,333,524 9,006,882 600,000		\$ 2,504,606 \$ 2,586,746 \$ 1,746,497	\$ (136)	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	6,668,585 4,080,021 16,336,18 1 599,864
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011)	\$ \$ \$ \$ \$ \$	2,003,796 4,081,839 2,333,524 9,006,882		\$ 2,504,606 \$ 2,586,746 \$ 1,746,497	\$ (136) \$ (136)	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	6,668,585 4,080,021 16,336,181 599,864 360,000
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,003,796 4,081,839 2,333,524 9,006,882 600,000 360,000 960,000	\$ 12.440.000	\$ 2,504,606 \$ 2,586,746 \$ 1,746,497 \$ 7,329,299	\$ (136)	\$\$\$\$\$ \$\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	6,668,585 4,080,021 16,336,181 599,864 360,000 959,86 4
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Total - Prop O Budget	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,003,796 4,081,839 2,333,524 9,006,882 600,000 360,000 960,000 518,645,140	\$ 12,440,000	\$ 2,504,606 \$ 2,586,746 \$ 1,746,497 \$ 7,329,299		\$\$\$\$\$ \$\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	6,668,585 4,080,02 16,336,18 599,864 360,000 959,86 4
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Total - Prop O Budget FUND	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,003,796 4,081,839 2,333,524 9,006,882 600,000 360,000 960,000	\$ 12,440,000	\$ 2,504,606 \$ 2,586,746 \$ 1,746,497 \$ 7,329,299	\$ (136)	\$\$\$\$\$ \$\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	6,668,585 4,080,021 16,336,181 599,864 360,000 959,86 4
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Total - Prop O Budget FUND Funding Sources (as of September, 30, 2011)	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,003,796 4,081,839 2,333,524 9,006,882 600,000 360,000 960,000 518,645,140 SOURCES	\$ 12,440,000	\$ 2,504,606 \$ 2,586,746 \$ 1,746,497 \$ 7,329,299	\$ (136)	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	6,668,585 4,080,021 16,336,181 599,864 360,000 959,864 527,995,320
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Total - Prop O Budget FUND	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,003,796 4,081,839 2,333,524 9,006,882 600,000 360,000 960,000 518,645,140	\$ 12,440,000	\$ 2,504,606 \$ 2,586,746 \$ 1,746,497 \$ 7,329,299	\$ (136)	\$\$\$\$\$ \$\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	6,668,585 4,080,02 ⁻ 16,336,18 ⁻¹ 599,864 360,000 959,864 527,995,820 37,000,000
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Total - Prop O Budget FUND Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - First Sale Interest Bond Proceeds - Second Sale	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,003,796 4,081,839 2,333,524 9,006,882 600,000 360,000 960,000 518,645,140 SOURCES 37,000,000	\$ 12,440,000	\$ 2,504,606 \$ 2,586,746 \$ 1,746,497 \$ 7,329,299	\$ (136)	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	6,668,585 4,080,02 ⁻ 16,336,18 ⁻¹ 599,864 360,000 959,864 527,995,820 37,000,000 3,042,656
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Total - Prop O Budget FUND Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - First Sale Interest	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,003,796 4,081,839 2,333,524 9,006,882 600,000 360,000 960,000 518,645,140 SOURCES 37,000,000 3,042,656	\$ 12,440,000	\$ 2,504,606 \$ 2,586,746 \$ 1,746,497 \$ 7,329,299	\$ (136)	\$\$ \$\$<	6,668,583 4,080,02 16,336,18 599,864 360,000 959,864 527,995,820 37,000,000 3,042,656 8,000,000
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Total - Prop O Budget FUND Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - Second Sale Bond Proceeds - Third Sale	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,003,796 4,081,839 2,333,524 9,006,882 600,000 360,000 960,000 518,645,140 SOURCES 37,000,000 3,042,656 8,000,000 854,249 101,000,000	\$ 12,440,000	\$ 2,504,606 \$ 2,586,746 \$ 1,746,497 \$ 7,329,299	\$ (136)	· · · · · · · · · · · · · · · · · · ·	6,668,583 4,080,02 16,336,18 599,864 360,000 959,864 527,995,820 37,000,000 3,042,656 8,000,000 854,243 101,000,000
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Total - Prop O Budget FUND Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - Second Sale Bond Proceeds - Second Sale Bond Proceeds - Third Sale Interest Bond Proceeds - Third Sale Interest Bond Proceeds - Third Sale Bond Proceeds - Third Sale Interest Bond Proceeds - Third Sale Bond Proceeds - Third Sale Bond Proceeds - Third Sale Interest Bond Proceeds - Third Sale Bond Proceeds - Third Sale Interest Bond Proceeds - Third Sale Bond Proceeds - Third Sale	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,003,796 4,081,839 2,333,524 9,006,882 600,000 360,000 518,645,140 SOURCES 37,000,000 3,042,656 8,000,000 854,249 101,000,000 5,142,889	\$ 12,440,000	\$ 2,504,606 \$ 2,586,746 \$ 1,746,497 \$ 7,329,299	\$ (136)	\$\$\$\$\$ \$ \$\$ \$ \$\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	6,668,583 4,080,02 16,336,18 599,864 360,000 959,864 527,995,820 37,000,000 3,042,656 8,000,000 854,244 101,000,000 5,142,885
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Total - Prop O Budget FUND Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - First Sale Interest Bond Proceeds - Second Sale Interest Bond Proceeds - Third Sale Bond Proceeds - Third Sale Bond Proceeds - Third Sale Bond Proceeds - First Sale Subtotal Bond Proceeds - Third Sale Bond Proceeds - Third Sale Bond Proceeds - Fourth Sale	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,003,796 4,081,839 2,333,524 9,006,882 600,000 360,000 960,000 518,645,140 SOURCES 37,000,000 3,042,656 8,000,000 854,249 101,000,000 5,142,889 176,500,000	\$ 12,440,000	\$ 2,504,606 \$ 2,586,746 \$ 1,746,497 \$ 7,329,299	\$ (136)	· ·	6,668,583 4,080,02 16,336,18 599,864 360,000 959,864 527,995,320 37,000,000 3,042,656 8,000,000 854,249 101,000,000 5,142,889 176,500,000
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Total - Prop O Budget FUND Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - First Sale Interest Bond Proceeds - Second Sale Interest Bond Proceeds - Third Sale Interest Bond Proceeds - Third Sale Interest Bond Proceeds - First Sale Bond Proceeds - Third Sale Interest Bond Proceeds - First Sale Bond Proceeds - First Sale Bond Proceeds - Third Sale Interest Bond Proceeds - First Sale Bond Proceeds - Fourth Sale Bond Proceeds - Fourth Sale Interest Bond Pr	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,003,796 4,081,839 2,333,524 9,006,882 600,000 360,000 960,000 518,645,140 SOURCES 37,000,000 3,042,656 8,000,000 854,249 101,000,000 5,142,889 176,500,000 5,858,814	\$ 12,440,000	\$ 2,504,606 \$ 2,586,746 \$ 1,746,497 \$ 7,329,299	\$ (136)	· · · · · · · · · · · · · · · · · · ·	6,668,583 4,080,02 16,336,18 599,864 360,000 959,864 527,995,820 37,000,000 3,042,656 8,000,000 854,244 101,000,000 5,142,888 176,500,000 5,858,814
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Total - Prop O Budget FUND Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - First Sale Interest Bond Proceeds - Third Sale Interest Bond Proceeds - Third Sale Bond Proceeds - First Sale Bond Proceeds - Third Sale Bond Proceeds - Third Sale Interest Bond Proceeds - First Sale Bond Proceeds - First Sale Bond Proceeds - Third Sale Bond Proceeds - Third Sale Bond Proceeds - First Sale Bond Proceeds - First Sale Bond Proceeds - First Sale Bond Proceeds - Third Sale Bond Proceeds - First Sale	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,003,796 4,081,839 2,333,524 9,006,882 600,000 360,000 960,000 518,645,140 SOURCES 37,000,000 3,042,656 8,000,000 854,249 101,000,000 5,142,889 176,500,000	\$ 12,440,000	\$ 2,504,606 \$ 2,586,746 \$ 1,746,497 \$ 7,329,299	\$ (136)	· · · · · · · · · · · · · · · · · · ·	6,668,583 4,080,02 16,336,18 599,864 360,000 959,864 527,995,820 37,000,000 3,042,656 8,000,000 854,244 101,000,000 5,142,888 176,500,000 5,858,814
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Total - Prop O Budget FUND Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - First Sale Interest Bond Proceeds - Second Sale Interest Bond Proceeds - Third Sale Bond Proceeds - Third Sale Bond Proceeds - Fourth Sale Interest Bond Proceeds - First Sale Interest Bond Proceeds - Fourth Sale Interest Bond Proceeds - Fourth Sale Interest Bond Proceeds - First Sale Interest Bond Procee	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,003,796 4,081,839 2,333,524 9,006,882 600,000 360,000 960,000 518,645,140 SOURCES 37,000,000 3,042,656 8,000,000 854,249 101,000,000 5,142,889 176,500,000 5,858,814	\$ 12,440,000	\$ 2,504,606 \$ 2,586,746 \$ 1,746,497 \$ 7,329,299 \$ 7,329,299	\$ (136)	····································	6,668,583 4,080,02 ⁻ 16,336,18 ⁻ 599,864 360,000 959,864 527,995,82 37,000,000 3,042,656 8,000,000 854,249 101,000,000 5,142,889 176,500,000 5,858,814 117,000,000
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Total - Prop O Budget FUND Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - First Sale Interest Bond Proceeds - Third Sale Interest Bond Proceeds - Third Sale Bond Proceeds - First Sale Bond Proceeds - Third Sale Bond Proceeds - Third Sale Interest Bond Proceeds - First Sale Bond Proceeds - First Sale Bond Proceeds - Third Sale Bond Proceeds - Third Sale Bond Proceeds - First Sale Bond Proceeds - First Sale Bond Proceeds - First Sale Bond Proceeds - Third Sale Bond Proceeds - First Sale	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,003,796 4,081,839 2,333,524 9,006,882 600,000 360,000 960,000 518,645,140 SOURCES 37,000,000 3,042,656 8,000,000 854,249 101,000,000 5,142,889 176,500,000 5,858,814	\$ 12,440,000	\$ 2,504,606 \$ 2,586,746 \$ 1,746,497 \$ 7,329,299	\$ (136)	· · · · · · · · · · · · · · · · · · ·	6,668,58 4,080,02 16,336,18 599,86 360,000 959,86 527,995,82 37,000,000 3,042,650 8,000,000 5,142,88 176,500,000 5,858,81 117,000,000
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Total - Prop O Budget FUND Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - First Sale Interest Bond Proceeds - Second Sale Interest Bond Proceeds - Third Sale Bond Proceeds - Fourth Sale Interest Bond Proceeds - Firth Sale Interest Bond Proceeds - Furth Sale Interest Bond Proceeds - Furth Sale Interest Bond Proceeds - Furth Sale Bond Proceeds - Firth Sale Interest Bond Proceeds - Firth Sale Interest Bond Proceeds - Furth Sale Bond Proceeds - Furth Sale Bond Proceeds - Furth Sale Bond Proceeds - Firth Sale Interest Bond Proceeds - Furth Sale Bond Proceeds - Furth Sale Bond Proceeds - Firth Sale Interest Bond Proceeds - Firth Sale Interest Bond Proceeds - Firth Sale Interest Bond Proceeds - Firth Sale Bond Proceeds - Firth Sale	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,003,796 4,081,839 2,333,524 9,006,882 600,000 360,000 960,000 518,645,140 SOURCES 37,000,000 3,042,656 8,000,000 854,249 101,000,000 5,142,889 176,500,000 5,858,814 117,000,000	\$ 12,440,000 \$ 12,440,000 \$ (100,000)	\$ 2,504,606 \$ 2,586,746 \$ 1,746,497 \$ 7,329,299 \$ 7,329,299	\$ (136)	· · · · · · · · · · · · · · · · · · ·	6,668,583 4,080,02 16,336,18 599,86 4 360,000 959,86 4 527,995,82 4 517,955,82 4 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,82 517,955,855,855 517,955,9
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Total - Prop O Budget FUND Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - First Sale Interest Bond Proceeds - Second Sale Bond Proceeds - Third Sale Interest Bond Proceeds - Fourth Sale Interest Bond Proceeds - Fourth Sale Interest Bond Proceeds - Fourth Sale Interest Bond Proceeds - First Sale Bond Proceeds - Fourth Sale Bond Proceeds - First Sale Interest Bond Proceeds - Firth Sale Interest Bond Proceeds - Furth Sale Interest Bond Proceeds - Firth Sale Interest Bond Proceeds	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,003,796 4,081,839 2,333,524 9,006,882 600,000 360,000 960,000 518,645,140 SOURCES 37,000,000 3,042,656 8,000,000 854,249 101,000,000 5,142,889 176,500,000 5,858,814 117,000,000		\$ 2,504,606 \$ 2,586,746 \$ 1,746,497 \$ 7,329,299 \$ 7,329,299	\$ (136)	· · · · · · · · · · · · · · · · · · ·	6,668,585 4,080,021 16,336,181 599,864 599,864 527,995,820 37,000,000 3,042,656 8,000,000 5,142,885 101,000,000 5,142,885 101,000,000 5,142,885 101,000,000 5,142,885 101,000,000 13,412,918 (100,000
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Total - Prop O Budget FUND Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - First Sale Interest Bond Proceeds - Second Sale Interest Bond Proceeds - Fourth Sale Bond Proceeds - Fourth Sale Bond Proceeds - First Sale Bond Proceeds - Fourth Sale Interest Bond Proceeds - Fourth Sale Bond Proceeds - First Sale Bond Proceeds - First Sale Bond Proceeds - Fourth Sale Bond Proceeds - Fourth Sale Bond Proceeds - First Sale Bond Proceeds - First Sale Bond Proceeds - Future Sales Bond Proceeds - Secured Grants Received Less Set-Aside for Future Arbitrage Payments	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,003,796 4,081,839 2,333,524 9,006,882 600,000 360,000 960,000 518,645,140 SOURCES 37,000,000 3,042,656 8,000,000 854,249 101,000,000 5,142,889 176,500,000 5,858,814 117,000,000	\$ (100,000)	\$ 2,504,606 \$ 2,586,746 \$ 1,746,497 \$ 7,329,299 \$ 7,329,299 \$ 7,329,299 \$ 7,329,299 \$ 7,329,299 \$ 60,500,000	\$ (136) \$ (10,418,619) 	· · · · · · · · · · · · · · · · · · ·	6,668,585 4,080,02 16,336,18 599,86 4 599,86 4 527,995,82 (527,995,82 (537,00 (5,142,88 (101,000,000 (5,142,88 (101,000,000 (5,142,85 (101,000,000 (13,412,918 ((100,000)(7,000,000 (5,000,000 (
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Total - Prop O Budget FUND Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - First Sale Interest Bond Proceeds - Second Sale Bond Proceeds - Third Sale Interest Bond Proceeds - Fourth Sale Interest Bond Proceeds - Fourth Sale Interest Bond Proceeds - First Sale Interest Bond Proceeds - Fourth Sale Interest Bond Proceeds - First Sale Interest Bond Proceeds - Secured Grants Received Less Set-Aside for Future Arbitrage Payments Sewer Construction and Maintenance (SCM)	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,003,796 4,081,839 2,333,524 9,006,882 600,000 360,000 960,000 518,645,140 SOURCES 37,000,000 3,042,656 8,000,000 854,249 101,000,000 5,142,889 176,500,000 5,858,814 117,000,000	\$ (100,000)	\$ 2,504,606 \$ 2,586,746 \$ 1,746,497 \$ 7,329,299 \$ 7,329,299 \$ 7,329,299 \$ 60,500,000 \$ 60,500,000 \$ 7,000,000.00 \$ 7,000,000.00	\$ (10,418,619) \$ (10,418,619) 		6,668,583 4,080,02 ⁻ 16,336,18 ⁻ 599,86 4 360,000 959,86 4 527,995,32 37,000,000 3,042,656 8,000,000 8,54,245 101,000,000 5,142,888 176,500,000 5,858,814 117,000,000 5,858,814 (100,000 7,000,000 535,211,52
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Total - Prop O Budget FUND Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - First Sale Interest Bond Proceeds - Second Sale Bond Proceeds - Third Sale Interest Bond Proceeds - Fourth Sale Interest Bond Proceeds - Fourth Sale Interest Bond Proceeds - First Sale Interest Bond Proceeds - First Sale Bond Proceeds - Secured Grants Received Less Set-Aside for Future Arbitrage Payments Sewer Construction and Maintenance (SCM)	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,003,796 4,081,839 2,333,524 9,006,882 600,000 360,000 960,000 518,645,140 SOURCES 37,000,000 3,042,656 8,000,000 854,249 101,000,000 5,142,889 176,500,000 5,858,814 117,000,000	\$ (100,000)	\$ 2,504,606 \$ 2,586,746 \$ 1,746,497 \$ 7,329,299 \$ 7,000,000 \$ 7,00	\$ (10,418,619) \$ (10,418,619) 	•• ••<	6,668,585 4,080,027 16,336,187 599,864 360,000 959,864 527,995,820 37,000,000 3,042,656 8,000,000 854,245 101,000,000 5,142,885 176,500,000 5,858,814 117,000,000 5,958,814 117,000,000 5,958,814 117,000,000 5,958,814 117,000,000 5,958,814 117,000,000 5,958,814 117,000,000 5,958,814 117,000,000 5,958,814 117,000,000 5,958,814 117,000,000 5,958,814 117,000,000 5,958,814 117,000,000 5,958,814 117,000,000 5,958,814 117,000,000 5,958,814 117,000,000 5,958,814 117,958,814 117,958,814 117,958,958,958,958,958,958,958,958,958,958
Office of Accounting Bureau of Contract Administration Bureau of Engineering Bureau of Sanitation Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Total - Prop O Budget FUND Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - First Sale Interest Bond Proceeds - Second Sale Interest Bond Proceeds - Third Sale Bond Proceeds - Third Sale Bond Proceeds - First Sale Bond Proceeds - Secured Grants Received Less Set-Aside for Future Arbitrage Payments Sewer Construction and Maintenance (SCM)	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,003,796 4,081,839 2,333,524 9,006,882 600,000 360,000 960,000 518,645,140 SOURCES 37,000,000 3,042,656 8,000,000 854,249 101,000,000 5,142,889 176,500,000 5,858,814 117,000,000	\$ (100,000)	\$ 2,504,606 \$ 2,586,746 \$ 1,746,497 \$ 7,329,299 \$ 7,000,000 \$ 7,00	\$ (10,418,619) \$ (10,418,619) 	•• ••<	37,000,000 3,042,656 8,000,000 854,249 101,000,000 5,142,889 176,500,000 5,858,814 117,000,000 13,412,918 (100,000 7,000,000 535,211,520

Project Funding Summary

				op O Funding		ther Direct		tential		
Project Title		Budget	(wi	th set asides)		Funding		Irsements	Source	Status
Albion Dairy Park - Demolition & Remediation	\$	3,956,400	\$	3,956,400	\$ \$	- 556,524	\$ \$	3,000,000	Demolition escrow account Sprint Nextel and Swiss II lease payment	N/A Lease payment of \$556,524 received
Abon Dairy Faix - Demonitor & Kenediation	Ψ	3,330,400	Ψ	3,330,400	э \$	330,324	\$	20,952	City Clerk	Rental reimbursement of \$20,952 approved
Albion Dairy Park - Land Acquisition - COMPLETED	\$	-	\$	17,560,000	\$	-	\$		N/A	N/A
Catch Basin Inserts and Coverings Phase I - COMPLETED	\$	14,702,886	\$	14,702,886	\$	-	\$	600,000		Grant reimbursement of \$600,000 received; grant
	÷	11,102,000	Ŷ	11,702,000	Ŷ		Ŷ	000,000	Prop 40	completed
Catch Basin Opening Screen Covers Phase II - COMPLETED	\$	9,362,404	\$	9,362,404	\$	-	\$	-	N/A	N/A
Catch Basin Opening Screen Covers Phase III	\$	44,500,000	\$	44,500,000	\$	-	\$	-	N/A	N/A
					\$	5,250,000		-	DWP	Secured
Cesar Chavez Ground Water Improvement	\$	9,841,230	\$	3,040,000	\$	750,000		-	CIWMB	Secured Secured
					э \$	387,230 414,000			UDAG CIEP	Secured
Echo Park Lake Rehabilitation	\$	84,263,313	\$	84,263,313	\$	599,875		-	Prop K	Secured
							\$	294,395	State of CA Natural Resources Agency	Secured
Elmer Avenue Phase II: Elmer Paseo	\$	1,275,000	\$	829,000	\$	446,000	\$	127,411	State of CA Santa Monica Mountains	On avera d
							\$	25,000	Conservancy Bureau of Reclamation	Secured Funding in negotiation
Glenoaks/Sunland Stormwater Capture	\$	508,696	\$	508,696	\$	-	\$	-	N/A	N/A
Grand Blvd. Tree Wells - COMPLETED	\$	780,282	\$	780,282	\$	_	\$	350,000		Grant reimbursement of \$350,000 received; grant
	*		•		· ·	207.000	-	500,000	Prop 50-SMBRP	completed
Hansen Dam Wetlands Restoration Imperial Highway Sunken Median Stormwater BMP	\$	2,517,702 2,723,403		2,220,702 2,723,403		297,000	\$ \$	-	Caltrans - FTIP N/A	Secured by MRCA for Design N/A
Inner Cabrillo Beach Bacterial Water Quality Improvement	\$	16,000,000		8,000,000			\$	-	Port of Los Angeles	Secured
La Cienega Fairfax Stormwater BMP - CANCELED	\$	668,159	\$	668,159	\$		\$	-	N/A	Project canceled
Los Angeles Zoo Parking Lot	\$	13,904,243	\$	13,904,243	\$	-	\$	-	N/A	N/A
Machado Lake-Phase I (Wilmington Drain)	\$	21,049,911	\$	21,049,911	\$ TBD	-	\$ \$	4,387,500	Prop 50-IRWMP LA County Flood Control District	Secured Final Agreement Pending
Machado Lake-Fhase I (Willington Drain)	φ	21,049,911	φ	21,049,911	\$, 10.000			Lawsuit Settlement	Secured
					\$		\$	-	Prop K	Secured
Machado Lake Ecosystem Rehabilitation	\$	99,523,897	\$	99,523,897	\$	296,997				
					•				Coastal Conservancy	Grant reimbursement of \$296,997 paid; grant completed
							\$	1,777,838	American Recovery & Reinvestment Act (ARRA)	Grant reimbursement of \$1,600,054 received
Mar Vista Recreation Center Stormwater BMP	\$	4,556,186	\$	4,556,186	\$	-	^		() (() ()	Grant reimbursement of \$300,000 received; grant
							\$	300,000	Prop 50-SMBRP	completed
Oros Green Street - COMPLETED	\$	784,251	\$	197,600	\$		\$	-	Prop 13 & CWA 319th	Secured
Peck Park Canyon Enhancement	\$	8,231,118	\$	6,190,000	\$ ¢	1,921,118 120,000		-	Prop 50 Rec & Trails Grant	\$1,586,193 in grant funding authorized for payment \$120,000 in grant funding received; grant completed
Penmar Water Quality Improvement (Phase I & II)	\$	23,585,000	\$	23,585,000	\$		\$	-	N/A	N/A
Rosecrans Recreation Center Stormwater Enhancements	\$	6,754,033	\$	4,829,119	\$	568,690		-	Prop K	Secured
	Ŷ	0,101,000	Ŷ	1,020,110	\$	1,356,224	\$	-	TBD	Prop K to find funding or down scope project
					\$	-	\$	4,364,420	American Recovery & Reinvestment Act (ARRA)	Grant reimbursement of \$3,924,995 received; ARRA funding for Pkg. 2 is bundled with Pkg. 1
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 1	\$	6,814,377	\$	6,814,377	¢		¢	707.077	() uno ()	Grant reimbursement of \$767,077 received; grant
					\$	-	\$	767,077	Prop 50-CBI	completed
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 2	\$	3,380,111	\$	3,380,111	\$	-	\$	-	American Recovery & Reinvestment Act	ADDA funding for Disp. 0 is hundled with Disp. 4
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 3	\$	20,634,036	\$	20,634,036	\$		\$	7,000,000	(ARRA) SCM Fund	ARRA funding for Pkg. 2 is bundled with Pkg. 1 Secured
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 4	\$	6,290,504		6,290,504		-	\$		Prop 50-CBI	Prop 50-CBI funding for Pkg. 4 is bundled with Pkg. 1
······································	Ť	.,,	l .	.,,	\$			3,300,000		Grant reimbursement of \$1,316,250 received. \$1,789,379
					φ	-	φ	3,300,000	Prop 50-IRWMP	authorized for payment
					\$	-	\$	2,011,937	Prop 12 (P7H) for Land Acquisition	Grant reimbursement of \$2,011,937 received; grant completed
					\$	1,282,721			Prop 12 (RZH) - for Land Acquisition Prop 40 (RZH)	Grant funding of \$916,188 paid
					\$	3,739,707	\$		Collection System Settlement Agreement -	
South Los Angeles Wetlands Park (includes Site Readiness)	\$	26,374,067	\$	16,678,202	Ψ			-	Supplemental Environmental Project	Funding of \$2,717,394 paid
	Ť		Ť		\$	1 1	\$ ¢	-	Prop K - for Land Acquisition Prop K	Secured Grant funding of \$500,000 paid, grant completed
					Ð	500,000		-	MTA - max potential reimbursement for	Grant running or \$500,000 paid, grant completed
					\$	-	\$	900,000	remediation	Reimbursement of \$761.829 received
					\$	67,501	\$	-	MTA - lease payment	Lease payment of \$67,501 received
					\$	-	\$	200,000		Grant reimbursement of \$199,977 received & grant
Strathern Dit Multiuse - Land Acquisition	\$	28 000 000	¢	10,000,000			\$,	EPA - Brownfields grant LA County Flood Control District	completed Secured
Strathern Pit Multiuse - Land Acquisition Strathern Wetlands Park	\$	28,000,000 22,000,000		7,800,000		18,000,000	φ	-	LA County Flood Control District	Secured
Taylor Yard River Park - Parcel G2 Land Acquisition	TB		\$	12,440,000			TBD		TBD	TBD
Temescal Canyon Park Stormwater BMP (Phase I & II)	\$	18,646,000		18,646,000	\$	-	\$	-	N/A	N/A
Westchester Stormwater BMP	\$	32,722,000		32,722,000			\$	-	N/A	N/A
Westminster Dog Park Stormwater BMP	\$	1,438,755	\$	1,438,755		-	\$	-	N/A	N/A Grant reimbursement of \$ 2,000,000 received; grant
Mantaida Darla Daissantas Inisatis	~	0.004.555	¢	0.001.505	\$	-	\$	2,000,000	Prop 50-SMBRP	completed
Westside Park Rainwater Irrigation	\$	8,304,589	\$	6,904,589	\$	900,000	\$	-	Quimby	Secured
					\$	292,038	\$	-	Prop K	Secured
		TOTALS								
	\$	544,092,553	\$	510,699,775	\$	62,202,276	\$ 3	81,426,530		1




2.0 SCHEDULE

2.1 Project Schedules

The following table summarizes the schedule status for projects in the Program Schedule Update and are grouped by project phase.

Description	Sch	nedule Sta	atus
Description	Ahead	On	Behind
Projects in Pre-Design			
Penmar Water Quality Improvement Phase II		\checkmark	
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 3 Phase II		\checkmark	
Temescal Canyon Park Stormwater BMP Phase II		\checkmark	
Land Acquisition Projects			
Taylor Yard River Park-Parcel G2 Land Acquisition*	I	NACTIV	E
Projects in Design			
Glenoaks/Sunland Stormwater Capture		\checkmark	
Strathern Wetlands Park		\checkmark	
Westchester Stormwater BMP		NACTIV	E
Projects in Bid & Award			
Elmer Avenue Phase II: Elmer Paseo		\checkmark	
Machado Lake Ecosystem Rehabilitation		\checkmark	
Machado Lake Phase I (Wilmington Drain)		\checkmark	
Projects in Construction			
Albion Dairy Park – Demolition & Remediation		~	
Catch Basin Opening Screen Covers Phase III*			√*
Echo Park Lake Rehabilitation		\checkmark	
Penmar Water Quality Improvement Phase I		\checkmark	
Rosecrans Recreation Center Stormwater Enhancements*		√*	
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 3		~	
South Los Angeles Wetlands Park			✓
Temescal Canyon Park Stormwater BMP Phase I		\checkmark	
Projects in Post Construction			
Hansen Dam Wetlands Restoration			
Los Angeles Zoo Parking Lot			
Mar Vista Recreation Center Stormwater BMP			
Peck Park Canyon Enhancement			
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 2			
Westside Park Rainwater Irrigation			
Projects Completed			
Albion Dairy Park – Land Acquisition*			
Catch Basin Inserts and Coverings Phase I			
Catch Basin Opening Screen Covers Phase II			
Cesar Chavez Ground Water Improvement* (a.k.a. Sheldon Arleta)			
Grand Blvd. Tree Wells			
Imperial Highway Sunken Median Stormwater BMP			
Inner Cabrillo Beach Bacterial Water Quality Improvement*			
Oros Green Street			
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 1			
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 4			
Strathern Pit Multiuse – Land Acquisition*			
Westminster Dog Park Stormwater BMP			
*Schedule not controlled by Prop O			

*Schedule not controlled by Prop O

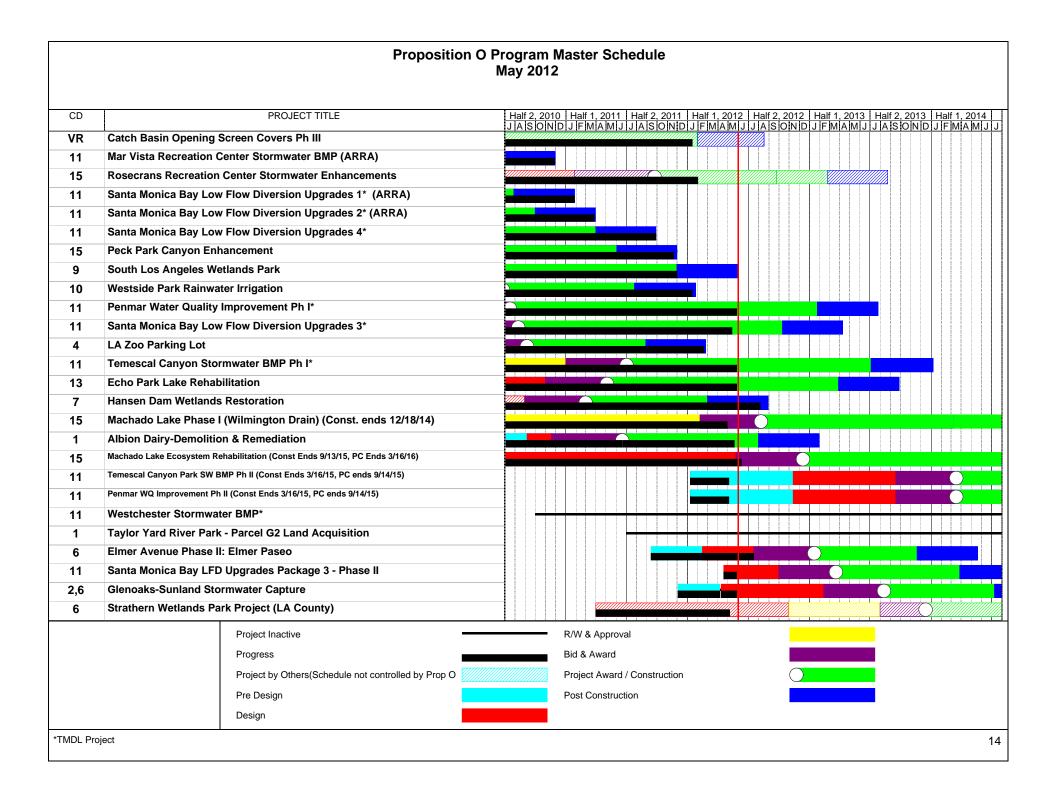



3.0 PROP O PROGRAM BUDGET

3.1 Budget vs. Actual Expenditure

Project		Prop O Budget	Prop O Appropriation	Prop O Expenditures for May	Prop O Total Expenditures
Albion Dairy Park Demolition &					
Remediation	Land Acquisition	\$0		\$0	\$0
Funding Category 3	Pre-Design/Design	\$485,313		\$8,744	\$418,075
	Construction Cost	\$3,140,000		\$149,610	\$2,133,404
	Construction Management	\$331,087		\$24,326	\$200,562
	Sub-total	\$3,956,400	\$4,056,400	\$182,680	\$2,752,047
Albion Dairy Park Land Acquisition	Land Acquisition	\$17,560,000		\$0	\$17,468,154
Funding Category 2	Pre-Design/Design	\$0		\$0	\$47,604
	Construction Cost	\$0		\$0	\$0
	Construction Management	\$0		\$0	\$0
	Sub-total	\$17,560,000	\$17,515,758	\$0	\$17,515,758
Catch Basin Inserts and Coverings					
Ph I	Land Acquisition	\$0		\$0	\$0
Funding Category 1	Pre-Design/Design Cost	\$0		\$0	\$0
	Construction Cost	\$14,607,953		\$0 ©	\$14,607,953
	Construction Management	\$94,933		\$0	\$0
	Sub-total	\$14,702,886	\$14,607,953	\$0	\$14,607,953
Catch Basin Opening Screen Covers Ph II	Land Acquisition	\$0		\$0	\$0
Funding Category 1	Pre-Design/Design Cost	\$0 \$0		\$0 \$0	\$0
running outegory r	Construction Cost	\$9,246,965		\$0 \$0	\$9,246,965
	Construction Management	\$115,439		\$0 \$0	\$0,240,50
	Sub-total	\$9,362,404	\$9,246,965	\$0	\$9,246,965
Catch Basin Opening Screen Covers					
Ph III	Land Acquisition	\$0		\$0	\$0
Funding Category 1 & 4	Pre-Design/Design	\$250,000		\$0	\$0
	Construction Cost	\$42,025,000		\$0	\$37,983,482
	Construction Management	\$2,225,000		\$0	\$68,126
	Sub-total	\$44,500,000	\$41,258,368	\$0	\$38,051,608
Cesar Chavez Ground Water					
Improvement	Land Acquisition	\$212		\$0	\$0
Funding Category 2	Pre-Design/Design Cost	\$663,238		\$0	\$0
	Construction Cost Construction Management	\$1,805,050 \$571,500		\$0 \$0	\$1,815,625 \$0
	Sub-total	\$3,040,000	\$1,815,625	\$0	\$1,815,62
Echo Park Lake Rehabilitation	Land Acquisition	\$0		\$0	\$0
Funding Category 1, 2, 3, & 4	Pre-Design/Design	\$10,997,899		\$1,345	\$6,060,793
	Construction Cost Construction Management	\$64,693,522 \$8,571,892		\$1,028,951 \$51,700	\$8,474,497
	Sub-total		\$59,413,140	\$1,081,996	\$238,692 \$14,773,98 2
	oub-total	404,203,513	\$55,415,146	\$1,001,330	φ1 4 ,775,502
Elmer Avenue Phase II: Elmer Paseo	Land Acquisition	\$0		\$0	\$0
Funding Category 3	Pre-Design/Design	\$206,000		\$0	\$66,546
	Construction Cost	\$510,100		\$0	\$0
	Construction Management	\$112,900		\$0	\$0
Glenoak/Sunland Stormwater Capture	Sub-total	\$829,000	\$829,000	\$0	\$66,546
· · · · ·	Land Acquisition	\$0		\$0	\$0
Funding Category 3	Pre-Design/Design	\$106,436		\$0	\$C
	Construction Cost	\$340,000		\$0	\$0
	Construction Management	\$62,260		\$0	\$0
	Sub-total	\$508,696	\$508,696	\$0	\$0

Proposition O - Clean	Water Bond		Monthly P	rogress Report - May	2012
Project		Prop O Budget	Prop O Appropriation	Prop O Expenditures for May	Prop O Total Expenditures
Grand Blvd. Tree Wells	Land Acquisition	\$0		\$0	\$0
Funding Category 1	Pre-Design/Design Cost	\$270,308		\$0	\$196,02 ⁻
	Construction Cost	\$382,444		\$0	\$382,444
	Construction Management	\$127,530 \$780,282	¢579.465	\$0 \$0	\$0
	Sub-total	. ,	\$578,465		\$576,403
Hansen Dam Wetland Restoration	Land Acquisition Pre-Design/Design	\$0 \$205 835		\$0 \$0	\$0 \$0
unung outegory s	Construction Cost	\$395,835 \$1,583,400		\$0 \$28,748	\$1,265,50 ²
	Construction Management	\$241,467		\$2,860	\$55,454
	Sub-total	\$2,220,702	\$1,923,702	\$31,608	\$1,320,955
mperial Hwy Sunken Median					
Stormwater BMP	Land Acquisition	\$0		\$0	\$C
Funding Category 1	Pre-Design/Design	\$334,200		\$0	\$315,288
	Construction Cost	\$2,217,703		\$0	\$764,536
	Construction Management	\$171,500		\$0	\$12,724
	Sub-total	\$2,723,403	\$1,251,144	\$0	\$1,092,548
nner Cabrillo Beach Bacterial Water Quality Improvement	Land Acquisition	N/A		N/A	N1/1
Funding Category 1	Pre-Design/Design	\$347,826		\$0	N/A \$0
	Construction Cost	\$6,956,522		\$0 \$0	\$6,906,550
	Construction Management	\$695,652		\$0	\$0
	Sub-total	\$8,000,000	\$6,906,550	\$0	\$6,906,550
La Cienega/Fairfax Stormwater BMP					
Canceled)	Land Acquisition	\$0		\$0	\$0
Funding Category 1	Pre-Design/Design	\$668,159		\$0	\$621,752
	Construction Cost Construction Management	\$0 \$0		\$0	\$0
	Sub-total	\$0 \$668,159	\$621,752	\$0 \$0	\$0 \$621,752
		\$000,135	\$021,732	ψŪ	φ021,732
LA Zoo Parking Lot	Land Acquisition	\$0		\$0	\$0
Funding Category 1 & 3	Pre-Design/Design Construction Cost	\$1,743,743		\$0	\$861,586
	Construction Management	\$11,129,500 \$1.031.000		\$0 \$0	\$4,479,213 \$351,238
	Sub-total	\$13,904,243	\$6,129,609	\$0	\$5,692,037
Machado Lake - Phase I (Wilmington					
Drain)	Land Acquisition	\$0		\$0	\$0
Funding Category 1 & 3	Pre-Design/Design	\$3,250,959		\$10,650	\$3,265,844
	Construction Cost	\$15,751,285		\$0	\$0
	Construction Management	\$2,047,667		\$0	\$0
	Sub-total	\$21,049,911	\$21,049,911	\$10,650	\$3,265,844
Machado Lake Ecosystem	Land Acquisition	¢o		\$ 0	¢0
Rehabilitation Funding Category 1 & 3	Pre-Design/Design	\$0 \$12,989,683		\$0 \$2,137	\$0 \$7,440,748
	Construction Cost	\$76,409,901		\$0	\$0
	Construction Management	\$10,124,313		\$0	\$0
	Sub-total	\$99,523,897	\$95,249,121	\$2,137	\$7,440,748
Mar Vista Recreation Center					
Mar Vista Recreation Center Stormwater BMP	Land Acquisition	\$0		\$0	\$0
Stormwater BMP	Land Acquisition Pre-Design/Design	\$0 \$753,655		\$0 \$0	
Stormwater BMP	Land Acquisition Pre-Design/Design Construction Cost	\$753,655 \$3,425,704		\$0 \$0	\$734,160 \$2,405,822
Stormwater BMP	Land Acquisition Pre-Design/Design Construction Cost Construction Management	\$753,655 \$3,425,704 \$376,827		\$0 \$0 \$0	\$734,160 \$2,405,822 \$282,513
Stormwater BMP Funding Category 1	Land Acquisition Pre-Design/Design Construction Cost Construction Management Sub-total	\$753,655 \$3,425,704 \$376,827	\$4,467,642	\$0 \$0 \$0 \$0	\$734,160 \$2,405,822 \$282,513
Stormwater BMP Funding Category 1 Dros Green Street	Land Acquisition Pre-Design/Design Construction Cost Construction Management Sub-total Land Acquisition	\$753,655 \$3,425,704 \$376,827 \$4,556,186 \$0	\$4,467,642	\$0 \$0 \$0 \$0 \$0 \$0	\$734,160 \$2,405,822 \$282,513 \$3,422,495 \$0
Stormwater BMP Funding Category 1 Dros Green Street	Land Acquisition Pre-Design/Design Construction Cost Construction Management Sub-total Land Acquisition Pre-Design/Design	\$753,655 \$3,425,704 \$376,827 \$4,556,186 \$0 \$0	\$4,467,642	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$734,160 \$2,405,822 \$282,513 \$3,422,495 \$0 \$0 \$0 \$0
	Land Acquisition Pre-Design/Design Construction Cost Construction Management Sub-total Land Acquisition	\$753,655 \$3,425,704 \$376,827 \$4,556,186 \$0	\$4,467,642	\$0 \$0 \$0 \$0 \$0 \$0	\$734,160 \$2,405,822 \$282,513 \$3,422,495 \$0

			Prop O	Prop O	Prop O Total
Project		Prop O Budget	Appropriation	Expenditures for May	Expenditures
Peck Park Canyon Enhancement	Land Acquisition	\$0		\$0	\$0
Funding Category 3	Pre-Design/Design	\$477,551		\$0	\$1,059,98
	Construction Cost	\$5,475,338		\$0	\$2,698,12
	Construction Management	\$237,111		\$0	\$474,929
	Sub-total	\$6,190,000	\$6,190,000	\$0	\$4,233,038
Penmar Water Quality Improvement					
Phase I	Land Acquisition	\$0		\$0	\$0
Funding Category 2 & 4	Pre-Design/Design	\$2,395,140		\$0	\$1,867,326
	Construction Cost Construction Management	\$16,808,000 \$1,551,660		\$1,013,013 \$23,190	\$6,908,815 \$266,008
	Sub-total		\$20,754,800	\$1,036,203	\$9,042,14
Denman Water Oselits Immerianes		<i> </i>	<i> </i>	÷ :,••••,=•••	<i>•••••••••••••••••••••••••••••••••••••</i>
Penmar Water Quality Improvement Phase II	Land Acquisition	\$0		\$0	\$0
Funding Category 4	Pre-Design/Design	\$326,600		\$0 \$0	\$0
	Construction Cost	\$2,292,000		\$0 \$0	\$0
	Construction Management	\$211,600		\$0	\$0
	Sub-total	\$2,830,200	\$2,630,200	\$0	\$0
Rosecrans Recreation Center					
Stormwater Enhancements	Land Acquisition	\$0		\$0	\$0
Funding Category 3 & 4	Pre-Design/Design	\$767,095		\$0	\$8,035
	Construction Cost	\$3,722,692		\$103,788	\$669,890
	Construction Management	\$339,332		\$0	\$0
	Sub-total	\$4,829,119	\$4,829,119	\$103,788	\$677,925
Santa Monica Bay Low Flow Diversi	on Land Acquisition				
Upgrades P 1		\$0		\$0	\$0
Funding Category 1	Pre-Design/Design Construction Cost	\$1,097,819 \$4,040,401		\$0 \$0.155	\$577,522
	Construction Management	\$4,949,401 \$767,157		\$9,155 \$0	\$3,634,780 \$471,423
	Sub-total		\$6,562,066	\$9,155	\$4,683,72
0		¢0,011,011	\$0,00 <u>-</u> ,000		¢ 1,000,1 _
Santa Monica Bay Low Flow Diversion Upgrades P 2	on Land Acquisition	\$0		\$0	\$0
Funding Category 1	Pre-Design/Design	\$544,547		\$0	\$396,202
	Construction Cost	\$2,455,034		\$0	\$1,176,789
	Construction Management	\$380,530		\$0	\$184,576
	Sub-total	\$3,380,111	\$2,257,710	\$0	\$1,757,566
Santa Monica Bay Low Flow Diversi					
Upgrades P 3	Land Acquisition	\$2,000,000		\$0	\$440,680
Funding Category 1	Pre-Design/Design	\$3,324,213		\$0	\$1,712,133
	Construction Cost Construction Management	\$13,255,258 \$2,054,565		\$147,793 \$57,752	\$5,998,416 \$577,108
	Sub-total		\$12,780,718	\$205,545	\$8,728,337
Santa Monica Bay Low Flow Diversi	on				
Upgrades P 4	Land Acquisition	\$0		\$0	\$0
Funding Category 1	Pre-Design/Design	\$1,013,421		\$0	\$574,057
	Construction Cost	\$4,568,903		\$0	\$2,457,047
	Construction Management	\$708,180		\$0	\$363,829
	Sub-total	\$6,290,504	\$5,003,055	\$0	\$3,394,927
South Los Angeles Wetlands Park (includes Site Readiness)	Land Acquisition	\$2,011,937		\$0	\$0
Funding Category 3	Pre-Design/Design Cost	\$2,011,937 \$1,638,000		\$0 \$0	\$2,977,256
	Construction Cost	\$1,838,000 \$11,722,602		\$0 \$0	\$2,977,250
		÷,. ==,002			
	Construction Management	\$1,305,663		\$19,587	\$755,475

CT-052 7.00

			Dren O	Prop O	Dress O Tetal
Project		Prop O Budget	Prop O Appropriation	Expenditures for May	Prop O Total Expenditures
Strathern Pit Multiuse -Land					
Acquisition	Land Acquisition	\$10,000,000		\$0	\$
Funding Category 2	Pre-Design/Design	\$0		\$0	\$
	Construction Cost	\$0		\$0	\$
	Construction Management	\$0		\$0	\$
	Sub-total	\$10,000,000	\$10,000,000	\$0	\$
Strathern Wetlands Park	Land Acquisition	\$0		\$0	\$
Funding Category 2	Pre-Design/Design	\$0		\$0	\$
	Construction Cost	\$7,800,000		\$0	\$
	Construction Management	\$0		\$0	\$
	Sub-total	\$7,800,000	\$7,800,000	\$0	\$
Taylor Yard River Park - Parcel G2 Land	Land Acquisition	\$12,440,000		\$0	\$
Acquisition	Pre-Design/Design	\$0		\$0	\$
Funding Category 3 & 4	Construction Cost	\$0		\$0	\$
	Construction Management	\$0		\$0	\$
	Sub-total	\$12,440,000	\$0	\$0	\$
Temescal Canyon Park Stormwater	Land Acquisition	\$0		\$0	\$
BMP Phase I	Pre-Design/Design	\$1,725,352		\$2,352	\$2,343,49
Funding Category 3 & 4	Construction Cost	\$12,104,809		\$161,253	\$1,387,18
	Construction Management	\$1,117,274		\$138,924	\$227,13
	Sub-total	\$14,947,435	\$14,974,353	\$302,529	\$3,957,81
Temescal Canyon Park Stormwater BMP Phase II	Land Acquisition	\$0		\$0	\$
Funding Category 3 & 4	Pre-Design/Design	\$0 \$426,918		\$0 \$0	÷
	Construction Cost	\$2,995,191		\$0 \$0	\$
	Construction Management	\$276,456		\$0 \$0	\$
	Sub-total	\$3,698,565	\$3,671,647	\$0	\$
Westchester Stormwater BMP	Land Acquisition	\$0		\$0	\$
Funding Category 1, 2, & 4	Pre-Design/Design	\$3,776,050		\$0	\$2,167,80
	Construction Cost	\$26,500,000		\$0	\$
	Construction Management	\$2,445,950		\$0	\$
	Sub-total	\$32,722,000	\$4,200,200	\$0	\$2,167,80
Westminster Dog Park Stormwater					
BMP	Land Acquisition	\$0		\$0	\$
Funding Category 4	Pre-Design/Design	\$169,577		\$0	\$224,00
	Construction Cost	\$1,159,000		\$0	\$254,96
	Construction Management	\$110,178 \$1,438,755	\$559.640	\$0	\$46,34
	Sub-total	.,,,	\$558,649	\$0	\$525,31
Westside Park Rainwater Irrigation	Land Acquisition Pre-Design/Design	\$0 \$747.045		\$0	\$
Project Funding Category 1	Construction Cost	\$747,945 \$5,756,644		\$222 \$0	\$785,04 \$2,617,17
	Construction Management	\$400,000		\$0 \$1,454	\$240,76
	Sub-total	\$6,904,589	\$4,302,563	\$1,676	\$3,642,98
PROJECTS SUBTOTAL		\$510,699,775	\$410,817,263	\$2,987,554	\$179,330,16
Consultant Cost – Program Related Bu	udget				
Program Development Full Proposal Development		\$599,684 \$360,000	\$599,684 \$360,000	\$0 \$0	\$599,86 \$360,00
		\$360,000	\$360,000	<u>۵</u> 0	\$360,00
City Staff - Program Related Budget*					
Office of Accounting		\$895,696	\$670,265	\$0	\$430,97
Bureau of Engineering Bureau of Contract Administratior		\$4,057,743	\$10,441,634 \$3,088,428	\$0 \$0	\$6,636,62 \$1,346,80
Bureau of Contract Administration Bureau of Sanitation		\$5,344,625	\$3,988,428 \$7,431,598	\$0 \$0	\$1,346,80 \$5,779,22
Indirect Cost		\$3,629,458	\$7,431,598 \$7,000,123	\$0 \$0	\$5,779,22 \$4,573,62
Arbitrage			¢.,000,120		
Fund 16F (1st Bond Sale)		\$7,340	\$7,340	\$0	\$7,34
PROGRAM TOTAL		\$525,594,321	\$441,316,335	\$2,987,554	\$199,064,62

*Appropriations and expenditures represent Program and Project related City Staff Cost "No Program related Budget



4.1 Project Status Report

A brief status report for each project is provided on the following pages. The report identifies key project information, the planned scope of work, progress date, updated construction costs and percentage complete for all Proposition O projects.

The Percentage Complete at the far right hand column of the diagram uses a color-coding system to designate the current phase of each project.

Turquoise	Pre-Design
Yellow	Right of Way Acquisition/ Land Acquisition
Red	Design
Violet	Bid and Award
Green	Construction
Blue	Post Construction

Progress for each project is tracked by a color-coded pie chart. The color-coding system shows work completed in the darker shade of each color and the lighter shade denotes work to be completed. For example, if a project is in design the pie chart begins as light red. As progress is made, a darker red will indicate the approximate percentage of design work completed to date.



PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION	COST	PERCENT COMPLETE
Albion Dairy Park - Demolition				Notice to Proceed:	7/8/2011	
& Remediation	CD 1 - Ed P. Reyes	Demolition of the buildings and	Demolition of above-ground	Contract Duration:	350 days	
1739 N. Albion Street	Designer: Malcolm Pirnie	improvements of an industrial	structures is complete. Regional	City Engineer's Est. (Class A):	\$2,468,100	
T		facility, remediation and abatement of all hazardous	Water Quality Control Board required additional soil	Contract Award		
A de la contra de la	Contractor: National Demolition	materials and soils onsite, and	sampling, groundwater	Amount: Contract Award +	\$1,269,555	
	Proj. Mgr.: Iftekhar Ahmed	the importation of clean soil to	monitoring, and soil vapor	Contingency (20%)	\$1,523,466	
	Contact #: 213-485-5875	leave the property in a level, graded condition.	sampling prior to evaluating and approval of further remediation	CO's to date (8, 85%):	\$1,080,468	
A Real		9.4404 00.141.011	plan leading to completion of	Award Amount +		222/
Carde -			project.	CO's Issued Master Sch. Constr.	\$2,350,023	Land Design Bid & Const Post Const
	Photo of Project Site	Funding: Prop O		Completion Date:	JUL 2012 Design	Acquire Award
Albion Dairy Park - Land						
Acquisition		Acquire a parcel of land adjacent	The Purchase and Sale	Prop O Acquisition		
1739 N. Albion Street	CD 1 - Ed P. Reyes	to the LA River as part of LA	Agreement was executed on	Cost:	\$17,474,154	
8 / + 1	Designer: N/A	River Revitalization Master Plan.	10/2/09. Escrow closed on	Orig. Const. Contr.:	N/A	
T	Contractor: N/A		10/23/09. Park land acquisition	CO's to date:	N/A	
	Proj. Mgr.: Kendrick Okuda					
	Contact #: 213-485-1165			Rev. Constr. Contr.:	N/A	
and the second				Payment to date:	\$17,474,154	100%
2000	Photo of Project Site	Funding: Prop O		Master Sch. Constr. Completion Date:	Pre Design N/A	Land Design Bid & Const Post Const Acquire Award
Cabrito Paseo Walkway/Bike				Completion Date.	N/A	
Path				Est. Prop O Constr.		
	CD 6 - Tony Cárdenas	Implement stormwater best management practices	Project is on hold due to funding issues. The Los Angeles	Cost:	\$1,007,558	
btwn Marson St. and Raymer St.	Designer: TBD	including: installation of	Neighborhood Land Trust	Orig. Const. Contr.:	N/A	
1	Contractor: TBD	bioswales, trash capture	(LANLT) is unable to secure	CO's to date:	N/A	
	Proj. Mgr.: Iftekhar Ahmed	devices, tree wells to aid in filtration, and a "\$MART"	additional \$3 million in funds			
	Contact #: 213-485-5875		LANET requested to withdraw	Rev. Constr. Contr.:	N/A	
	Contact #. 213-465-5675		their request for project funding.			
+ + + + + + +		Funding: Prop-Q, Kaiser	う └ └ └ ノ 丿	Payment to date: Master Sch. Constr.	N/A Pre	Land Design Bid & Const Post Cons
$\rightarrow \rightarrow \rightarrow \rightarrow \rightarrow \rightarrow \rightarrow$	Proposed Project Site Plan	Foundation, & LANLT		Completion Date:	Design N/A	Acquire Award
Catch Basin Inserts and						
Covers Phase I		leatell 0.000 incerts and 0.000		Prop O Constr.		
Citavida	CD: All	Install 8,000 inserts and 6,000 screens in the high trash	This project is complete.	Cost:	\$14,900,000	
Citywide	Designer: Bureau of Sanitation	generation areas, in the City, to				
	Contractor: Various	achieve 20% trash reduction in the Ballona Creek and Les				
	Proj. Mgr.: Alfredo Magallanes	the Ballona Creek and Los Angeles River Watersheds.				
	Contact #: 213-485-3958					
				Payment to date:	\$14,202,869	100%
				Construction	Pre Design	Land Design Bid & Const Post Const Acquire Award
	Photo of Catch Basin Insert	Funding: Prop O & Prop 40		Completion Date:	SEP 2007	


PROJECT STATUS REPORT

PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION C	OST	PERCENT COMPLETE
Catch Basin Opening Screen Covers Phase II Citywide	CD: All Designer: Bureau of Sanitation Contractor: Various Proj. Mgr.: Alfredo Magallanes Contact #: 213-485-3958	Install approximately 6,400 screens in medium trash generation areas, in the City, to increase trash reduction from 20% (accomplished in Phase 1) to 30% trash reduction in Ballona Creek and A River D Watersheos.	This project is complete.	Prop O Constr. Cost: Payment to date: Construction Completion Date:	\$9,400,000 \$9,246,965 OCT 2007	100%
Catch Basin Opening Screen Covers Phase III Citywide	CD: All Designer: Bureau of Sanitation Contractor: West Coast Construction Proj. Mgr.: Alfredo Magallanes Contact #: 213-485-3958	Retrofit of approximately 24,219 catch basins with opening screen covers and 2,600 inserts. Includes City-owned catch basins not covered in Phases I & II, as well as all State and County catch basins within the City.	A new procurement and installation services contract will install 2,600 catch basin inserts throughout the City to comply with trash TMDL.	Notice to Proceed: Contract Duration: City Engineer's Est. (Class A): Contract Award Amount: Contract Award + Contingency (10%) CO's to date (#, %): Award Amount + CO's Issued	\$42,025,000 \$42,025,000 \$0 \$0 \$37,595,224	98%
	Photo of Catch Basin Screen Cover	Funding: Prop O		Master Sch. Constr. Completion Date:	FEB 2012	Land Design Bid & Const Post Const Acquire Award
Cesar Chavez Ground Water Improvement 12455 Wicks Street	CD 6 - Tony Cárdenas Designer: Kleinfelder/Geosyntec Contractor: Environmental Construction Proj. Mgr.: Fang Chang Contact #: 213-978-1896	Retrofit existing gas collection system, install new flare & restore capacity in adjacent Tujunga Spreading Grounds through renovation of closed collector system.	The board report to the Board of Public Works (BPW) to accept the construction contract is being prepared.	Prop O Constr. Cost: Orig. Const. Contr.: CO's to date: Rev. Constr. Contr.: Payment to date: Construction	\$1,805,050 \$7,471,676 \$727,278 \$8,198,954 \$7,131,597 Pre Design	100%
Echo Park Lake Rehabilitation 751 Echo Park Avenue	Photo of Project Site CD 13 - Eric Garcetti	Grant, UDA Grant, & CIEP In-lake improvements, in-lake vegetation (wetlands) and	Construction activities include dewatering and grading of the	Completion Date: Notice to Proceed: Contract Duration: City Engineer's Est.	OCT 2009 7/11/2011 600 Days	
	Designer:Black & VeatchContractor:Ford E.C.Proj. Mgr.:Kendrick OkudaContact #:213-485-1165	habitat improvements, and parkland structural best management practices (swales), lake re-circulation system, lake aeration system, relocate fountain pump house.	lake bottom, the State's Division of Safety of Dams (DSOD) submerged berm and pump house. Construction of the sewer connection on Glendale Blvd. took approx. 3 weeks and was completed on 5/25/2012.	(Class Å): Contract Award Amount: Contract Award + Contingency (10%) CO's to date (17, 2%): Award Amount + CO's Issued	\$49,580,000 \$24,485,000 \$26,933,500 \$446,849 \$24,931,849	56%
	Photo of Existing Lake	Funding: Prop O & Prop K		Master Sch. Constr. Completion Date:	MAR 2013 Design	Land Design Bid & Const Post Const Acquire Award

PROJECT STATUS REPORT


PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION C	OST	PERCENT COMPLETE
Elmer Avenue Phase II:						
Elmer Paseo	CD 6 - Tony Cárdenas	Convert a paved 20' x 270' alley	Project is in the bid and award	Est. Prop O Constr. Cost:	¢000.000	
7702 North Elmer Avenue	Designer: Tetra Tech	into a pocket park with water	phase.		\$829,000	
		quality improvements, including a pervious pedestrian pathway		Orig. Const. Contr.: CO's to date:	N/A	
A CONTRACTOR OF A CONTRACTOR O	Contractor: TBD	and a vegetated swale.			N/A	
	Proj. Mgr.: Iftekhar Ahmed Contact #: 213-485-5875	Sedimentation removal devices will also be installed.		Rev. Constr. Contr.:	N//A	
16	Contact #. 213-405-5675			Payment to date:	N/A \$0	1%
				Master Sch. Constr.	۵U Pre	Land Design Bid & Const Post Const
	Photo of Existing Paseo	Funding: Prop O		Completion Date:	JUL 2013	n Acquire Award
Glenoaks-Sunland						
Stormwater Capture	CD 6 Tany Cárdanaa	This project will install infiltration	This project is in the design	Est. Prop O Constr.		
Intersection of Sunland & Glenoaks	CD 6 - Tony Cárdenas	wells and other storm water Best	phase.	Cost:	\$475,000	
	- Barbad of Calification	Management Practices (BMPs)		Orig. Const. Contr.:	N/A	
	Contractor: Hollywood Beautification Tean	subject intersection during storm		CO's to date:	N/A	
	Proj. Mgr.: Iftekhar Ahmed	events.		David Caracter Constru		
	Contact #: 213-485-5875			Rev. Constr. Contr.:	N/A	450/
a second a	Photo of Flooding at Subject			Payment to date: Master Sch. Constr.	\$0 Pre	15% Land Design Bid & Const Post Const
	Intersection	Funding: Prop O		Completion Date:	NOV 2013	n Acquire Award
Grand Blvd. Tree Wells				Notice to Proceed:	7/7/2008	
	CD 11 - Bill Rosendahl	Install seven stormwater	This project is complete.	Contract Duration:	100 days	
Intersection Grand & Riviera	Designer: PSOMAS	bioretention filters in a high- density residential and		City Engineer's Est. (Class A):	\$428,900	
Riterri at Righer Biverdin that Bypes	Contractor: Andrew Papac & Sons	commercial corridor in the		Contract Award Amount:	\$401,797	
	Contractor. Andrew Papac & Sons	Venice area to treat runoff from		Contract Award +	5401,797	
" A CO-	Proj. Mgr.: Andy Flores			Contingency (24.8%)	\$501,797	
See Water life				CO's to date		
('First Real')	Contact #: 213-485-4496			(5, -15%): Award Amount +	-\$19,353	
Bendman Parking Lat		$(\cup) (\cup) ($		CO's Issued	\$382,444	Land Design Bid & Const Post Const
	Conceptual Drawing of Tree Well	Funding: Prop O & Prop 50		Constrution Completion Date:	DEC 2009	Acquire Award
Hansen Dam Wetlands		· · ·		Notice to Proceed:	2/3/2011	
Restoration	CD 7 - Richard Alarcón	Stormwater runoff from three	Project is in the post-	Contract Duration:	240 days	
Osborne Street @ Foothill Blvd.	Designer: MRCA	existing parking lots will be sent	construction phase.	City Engineer's Est. (Class A):		
	-	through newly constructed sediment forebays for removal of		Contract Award	\$1,159,000	
	Contractor: Lee Construction	trash & sediments prior to		Amount: Contract Award +	\$955,257	
Lower Parking Area	Proj. Mgr.: Iftekhar Ahmed	wetlands discharge.		Contingency (10%)	\$1,050,257	
Ares 9	Contact #: 213-485-5875			CO's to date (28, 43%):	\$412,668	
Perking Area				Award Amount + CO's Issued	\$1,334,496	85%
		Funding: Prop O & Caltrans-		Master Sch. Constr.	φ1,00 1 ,490 Pre	Land Design Bid & Const Post Const
	Proposed Project Layout	FTIP		Completion Date:	FEB 2012	Acquire Award

PROJECT STATUS REPORT

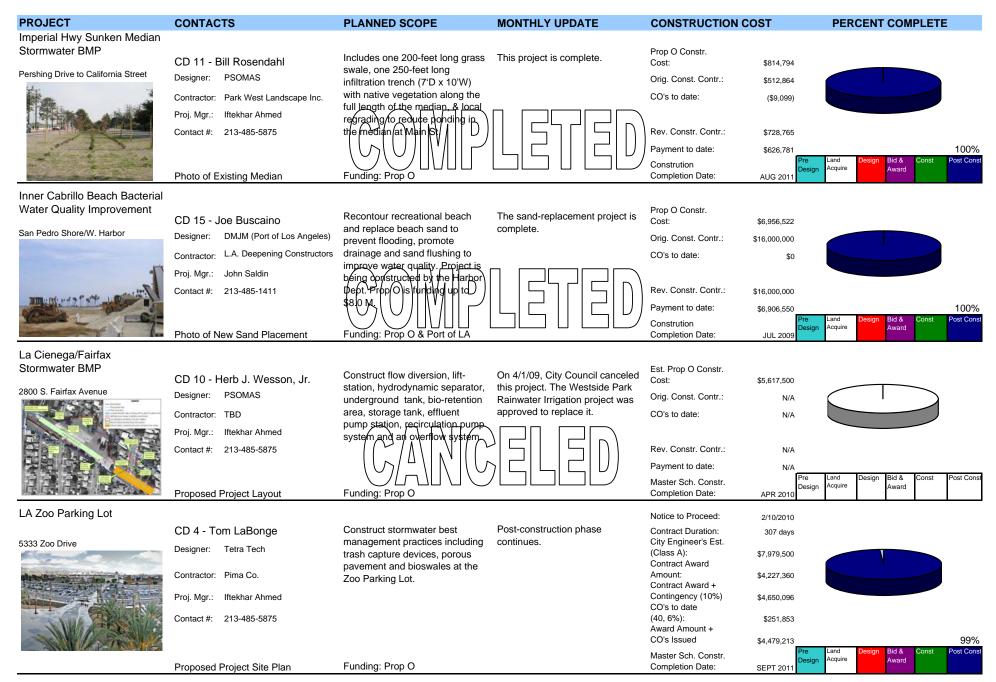




PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION CO	DST PERCENT COMPLETE
Machado Lake-Phase I (Wilmington Drain)	CD 15 - Joe Buscaino	Install trash netting systems,	The City is updating the plans	Est. Prop O Constr.	
PCH & Vermont Avenue	CD 15 - JOE BUSCAINO Designer: CDM Smith	install smart irrigation in	and specifications with	Cost: Sort:	\$15,751,285
	Contractor: TBD	landscaped areas, use biofilters or similar vegetated BMPs, and	environmental permit requirements. Team continues	CO's to date:	N/A N/A
	Proj. Mgr.: Kendrick Okuda	recontour and align the channel.	efforts to finalize the design in order to move into the bid and		
The second second	Contact #: 213-485-1165		award phase.	Rev. Constr. Contr.:	N/A
				Payment to date:	N/A44%
	Photo of Existing Conditions	Funding: Prop O & Prop 50		Master Sch. Constr. Completion Date:	DEC 2014 Pre Land Design Bid & Const Post Const DEC 2014 Acquire Award
Machado Lake Ecosystem					
Rehabilitation	CD 15 - Joe Buscaino	In-lake rehabilitation techniques,	Design plan signed by the City	Est. Prop O Constr.	
PCH & Vermont Avenue	Designer: CDM Smith	riparian system enhancements,	Engineer. City completed permit	Cost: Orig. Const. Contr.:	\$76,409,901
A THE NUMBER	Contractor: TBD	and treatment best management practices.	applications for The US Army Corps of Engineers 401 and 404	CO's to date:	N/A
A Strill maker	Proj. Mgr.: Kendrick Okuda		Permits, Regional Water Quality		
A CONTRACTOR OF THE OWNER	Contact #: 213-485-1165		Control Board, and The California Dept of Fish and Game Permits.	Rev. Constr. Contr.:	N/A
				Payment to date:	N/A1%
	Photo of Existing Lake	Funding: Prop O & Prop K		Master Sch. Constr. Completion Date:	Pre Land Design Bid & Const Post Const Design Acquire Award
Mar Vista Recreation Center				•	
Stormwater BMP	CD 11 - Bill Rosendahl	Construction of a stormwater lift	Project continues in the post	Notice to Proceed: Contract Duration:	5/4/2009
11430 W. Woodbine	Designer: PSOMAS	station, hydrodynamic separator,	construction phase. Bureau of	City Engineer's Est.	365 days
	Designer. ToomAo	underground detention tank, chlorination facility, final effluent	Sanitation and the Bureau of Engineering continue implement	(Class A): Contract Award	\$2,979,900
	Contractor: LA Engineering Inc.	pump station, recirculation pump,	optimization of the system.	Amount: Contract Award +	\$2,340,120
	Proj. Mgr.: Andy Flores	and overflow piping at Mar Vista Park.		Contingency (19%) CO's to date	\$2,790,120
	Contact #: 213-485-4496			(18, 3%):	\$65,702
				Award Amount + CO's Issued	\$2,405,822 99%
	Proposed Project Site Plan	Funding: Prop O, Prop 50 & ARRA		Master Sch. Constr. Completion Date:	NOV 2010 Pre Land Design Bid & Const Post Const Award
Oros Green Street				•	
	CD 13 - Eric Garcetti	Construct five curb side	This project is complete.	Prop O Constr. Cost:	\$300,000
between Blake Avenue & LA River	Designer: North East Trees (NET)	"stormwater gardens" in street parkway and a large infiltration		Orig. Const. Contr.:	N/A
	Contractor: Street Services	gallery beneath Steelhead Park.		CO's to date:	\$0
	Proj. Mgr.: Dean Harding			Rev. Constr. Contr.:	\$300.000
	Contact #: 213-473-4242			Payment to date:	\$0
- Aller - Aller				Construction Completion Date:	AUG 2007 100%
	Photo of New Sidewalk & Stormwater			Construction	Pre Land Design Bid & Const Post Const
	Gardens	CWA		Completion Date:	MAY 2010 Acquire Award



PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION	COST	PERCENT COMPLETE
Peck Park Canyon				Notice to Proceed:	5/3/2010	
Enhancement	CD 15 - Joe Buscaino	Install vegetated bio-swales,	Conducting Mitigation Measures	Contract Duration:	593 days	
560 N. Western Avenue	Designer: Tetra Tech	catch basins, armoring and re-	establishment and Best Management Practices (BMP)	City Engineer's Est. (Class A): Contract Award	\$4,000,641	
	Contractor: C.S. Legacy Construction, Inc.	vegetation for bank stabilization, and a step pool channel in Peck	optimization.	Amount:	\$3,636,946	
	Proj. Mgr.: John Saldin	Park.		Contract Award + Contingency (10%) CO's to date	\$4,000,640	
	Contact #: 213-485-1411			(32, 8%): Award Amount +	\$301,760	
				CO's Issued	\$3,938,706	99 ⁴ Pre Land Design Bid & Const Post Co
	Proposed Project Layout	Funding: Prop O, Prop 50 & Rec and Trails Grant		Master Sch. Constr. Completion Date:	MAY 2011	Pre Land Design Bid & Const Post Co Design Acquire Award
Penmar Water Quality				Notice to Proceed:	12/12/2010	
Improvement Phase I	CD 11 - Bill Rosendahl	Capture & treat dry/wet weather	Project construction phase	Contract Duration:	600 days	
1216 E. Rose Ave	Designer: Brown & Caldwell	runoff. Dry weather runoff to be diverted to sanitary sewer for	continues. Ongoing construction activities include construction of	City Engineer's Est. (Class A):	\$13,878,500	
	Contractor: Pacific Hydrotech	treatment. Wet weather runoff to be diverted to the underground	the underground tank at Penmar Park, the pump station at	Contract Award Amount: Contract Award +	\$11,360,700	
THE REAL PROPERTY OF THE PARTY	Proj. Mgr.: Andy Flores	storage tank for discharge to sanitary sewer.	Frederick Street.	Contingency (10%)	\$12,500,700	
	Contact #: 213-485-4496			CO's to date (27, 2%): Award Amount +	\$184,547	
				CO's Issued	\$11,545,247	74%
				Master Sch. Constr.		Pre Land Design Bid & Const Post Col Design Acquire Award
	Proposed Project Layout	Funding: Prop O		Completion Date:	JAN 2013	
Penmar Water Quality						
Improvement Phase II		Install a water treatment system	A task order solicitation was	Est. Prop O Constr.		
1216 E. Rose Ave	CD 11 - Bill Rosendahl	for the purpose of reusing	advertised for the pre-design of	Cost:	\$2,292,000	
	Designer: TBD	collected stormwater.	this project, along with the Temescal Canyon Park	Orig. Const. Contr.:	N/A	
A CONTRACTOR OF	Contractor: TBD		Stormwater BMP Phase II	CO's to date:	N/A	
HIRAD MANE BANALON MARKAN	Proj. Mgr.: Katie Clark		Project, on 5/14/2012. Proposals			
PRETATION PRETATION PRETATION	Contact #: 213-847-0395		are due on 6/15/2012.	Rev. Constr. Contr.:	N/A	
- Contractor				Payment to date:	N/A	38% Pre Land Design Bid & Const Post Con
AND AND	Proposed Project Layout	Funding: Prop O		Master Sch. Constr. Completion Date:	MAR 2015	Design Acquire Award
Rosecrans Rec. Center				Notice to Proceed:		
Stormwater Enhancements	CD 15 - Joe Buscaino	Install "SMART" irrigation system,	Project is in the construction	Contract Duration:	1/17/2011 640 days	
15000 S. Vermont Avenue	Designer: Withers & Sandgren	bioswales, vegetated retention basins, infiltration basins,	phase.	City Engineer's Est. (Class A):	\$3,500,000	
	Contractor: Horizon Construction Intl.	synthetic soccer field,		Contract Award Amount:	\$3,195,540	
Storage and Storag	Proj. Mgr.: Ray Araujo	decomposed granite pathway, and landscaping.		Contract Award + Contingency (10%)	\$3,515,094	
Mining and Annual				CO's to date		
And Tables and the second seco	Contact #: 213-473-9717			(#, 1%): Award Amount +	\$42,400	
Recorder				CO's Issued	\$3,237,940	25% Pre Land Design Bid & Const Post Co



PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION COST	PERCENT COMPLETE
Santa Monica Bay Low Flow				Notice to Proceed: 7	7/6/2009
Diversion Upgrades Pkg 1	CD 11 - Bill Rosendahl	Upgrade Marquez, Bay Club,	Project is complete.		66 days
PCH Several Locations	Designer: PSOMAS	Thornton, Venice Pavilion, and Imperial Low Flow Diversion		City Engineer's Est. (Class A): \$4.	949,401
		systems/to divert both summer		Contract Award	
	Contractor: LA Engineering, Inc.	/and winter-dry-weather tows, in		Amount: \$3, Contract Award +	024,545
	Proj. Mgr.: Andy Flores	order to comply with the bacteria			328,998
AREA I	Contact #: 213-485-4496	regulations.		CO's to date (26, 6%): \$	190,854
				Award Amount + CO's Issued \$3.	100%
		Funding: Prop O, Prop 50 &		Master Sch. Constr.	215,399 100% Pre Land Design Bid & Const Post Const
	Photo of Marquez Ave. LFD	ARRA			JL 2010 Acquire Award
Santa Monica Bay Low Flow				Notice to Proceed: 7/2	27/2009
Diversion Upgrades Pkg 2	CD 11 - Bill Rosendahl	Upgrade the existing Temescal	Project continues in the post	Contract Duration:	21/2000
At Temescal Canyon Park	Designer: PSOMAS	Canyon Low Flow Diversion	construction phase. Bureau of	City Engineer's Est. (Class A): \$1,	807,900
A Property		System to comply with the bacteria TMDL winter dry	Sanitation and the Bureau of Engineering continue implement	Contract Award	
	Contractor: LA Engineering, Inc.	weather regulations.	optimization of the system.		207,440
	Proj. Mgr.: Andy Flores			Contract Award + Contingency (9.9%) \$1,;	327,440
	Contact #: 213-485-4496			CO's to date (11, 3%):	\$40.074
	Contact #. 213-463-4496			Award Amount +	\$42,074
					249,514 99% Pre Land Design Bid & Const Post Const
	Proposed Improvements at Temescal Cyn LFD	Funding: Prop O & ARRA		Master Sch. Constr. Completion Date: 00	CT 2010 Design Acquire Acquire Award
Santa Monica Bay Low Flow	- ,				
Diversion Upgrades Pkg 3	CD 11 - Bill Rosendahl	Construct a relief sewer (CIRS)	The northern sewer reach along		20/2010 60 days
Along PCH	Designer: PSOMAS	to the Coastal Interceptor Sewer	PCH has been completed. Work	City Engineer's Est.	ou days
	Designer. 1 SOWAS	in order to comply with the	will continue in the beach parking	(Class A): \$13,3 Contract Award	255,258
	Contractor: Blois Construction	bacteria TMDL winter dry- weather regulations.	lots through June 30, 2012.	Amount: \$8,	468,451
	Proj. Mgr.: Andy Flores			Contract Award + Contingency (15%) \$9,7	740,902
				CO's to date	
	Contact #: 213-485-4496			(24, 9%): \$ Award Amount +	721,364
				CO's Issued \$9,	189,815 83% Pre Land Design Bid & Const Post Const
				Master Sch. Constr.	Pre Land Design Bid & Const Post Const Design Acquire Award
	Photo of Relief Sewer Location	Funding: Prop O & SCM		Completion Date: 00	CT 2012
Santa Monica Bay Low Flow				Notice to Proceed: 9/2	23/2009
Diversion Upgrades Pkg 4	CD 11 - Bill Rosendahl	This project will upgrade the existing Low Flow Diversion	The project is complete.	Contract Duration: 36 City Engineer's Est.	5 DAYS
Will Rogers Beach Parking Lot	Designer: PSOMAS	System at Santa Monica Canyon			798,800
	Contractor: Griffith Company	and Palisades Park Low Flow		Contract Award Amount: \$2.	279,000
		Diversion System. Upgrades		Contract Award +	2/3,000
	Proj. Mgr.: Andy Flores	include pump and electrical upgrades and automatic control irdm Venice Pump Plant.		Contingency (10%) \$2,8 CO's to date	507,000
	Contact #: 213-485-4496	frdm Vehice Pump Plant.		(10, 8%): \$	178,640
and the second s				Award Amount + CO's Issued \$2.	457,640 100%
	I	$\bigcirc \bigcirc $		Master Sch. Constr.	Pre Land Design Bid & Const Post Const
	Photo of Channel at Diversion Site	Funding: Prop O & Prop 50		Completion Date: AF	PR 2011



PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION CO	OST P	ERCENT COMPLETE
South Los Angeles Wetlands Park	CD 9 - Jan Perry	Construct a wetlands park at 54th St. and Avalon Blvd to improve	The Park area is complete. The Grand Opening was held on Feb.	Notice to Proceed: Contract Duration: City Engineer's Est.	4/9/2010 683 days	
54th St & Avalon Boulevard	Designer: PSOMAS	area stormwater quality, and provide recreational space for the	9th. Change order work continues for the pump station.	(Class A): Contract Award	\$10,354,300	
	Contractor: Ford E.C.	surrounding community.	The daily drop of the wetland water surface elevation continues	Amount: Contract Award +	\$6,370,000	
A A A A A A A A A A A A A A A A A A A	Proj. Mgr.: John Saldin		to exceed expected evapotransporation rates. An	Contingency (10%) CO's to date	\$7,297,000	
STALL AND STALL	Contact #: 213-485-1411	Funding: Prop O, Prop K, Prop	evaluation of alternatives to reduce water elevation loss is	(50, 11%): Award Amount + CO's Issued	\$669,999 \$7,029,379	100%
	Rendering of Proposed Project	12, Prop 50, Prop 40, CSSA(SEP), Brownfields Grant, & MTA	ongoing.	Master Sch. Constr. Completion Date:	DEC 2011	e Land Design Bid & Const Post Const Isign Acquire Design Award
Strathern Pit Multiuse - Land						
Acquisition	CD 6 - Tony Cárdenas	Acquire the land necessary to convert a 30-acre gravel pit site	This project is complete.	Est. Prop O Acquisition Cost:	\$10,000,000	
8175 & 8216 Fair Avenue	Designer: LA County	into a multipurpose facility dedicated to stormwater retention		Orig. Const. Contr.:	N/A	
	Contractor: N/A Proj. Mgr.: Andy Flores	and reuse		CO's to date:	N/A	
Answer for the second	Contact #: 213-485-4496	(((((((((((((((((((Rev. Constr. Contr.:	N/A	
Here And				Payment to date: Expected Acquisition	N/A Pre	100% e Land Design Bid & Const Post Const
* * market	Proposed Project Site Plan	Funding: Prop O & LA County		Date:	TBD De	sign Acquire Award
Strathern Wetlands Park				Est. Prop O		
9175 8 9216 Eair Avonua	CD 6 - Tony Cárdenas	The Strathern Pit Multiuse Project will convert a 30-acre	Los Angeles County Public Works has acquired the land and	Construction Cost:	\$7,800,000	
8175 & 8216 Fair Avenue	Designer: LA County	landfill to a wetlands park facility to provide enhanced water	the project continues in the design phase. City submitted it's	Orig. Const. Contr.: CO's to date:	N/A	
	Contractor: N/A Proj. Mgr.: Andy Flores	quality, flood protection, habitat creation, groundwater recharge,	30% design review comment to LA County on 5/24/12.		N/A	
Annual fut	Contact #: 213-485-4496	recreational and water reuse.	LA County on 3/24/12.	Rev. Constr. Contr.:	N/A	
Arban and a second a				Payment to date:	N/A	68% Land Design Bid & Const Post Const
2 2 a	Proposed Project Site Plan	Funding: Prop O & LA County		Master Sch. Constr. Completion Date:	JUL 2019	sign Acquire Award
Taylor Yard River Park -						
Parcel G2 Land Acquisition	CD 1 - Ed P. Reyes	Acquire a parcel of land adjacent to the LA River as part of	Land acquisition is in negotiation.	Est. Prop O Acquisition Cost:	\$12,440,000	
2850 Kerr Street	Designer: N/A	Revitalization Master Plan. \$25M in Prop O funds must be		Orig. Const. Contr.:	N/A	
ALL DE CONTRACTOR	Contractor: N/A Proj. Mgr.: Kendrick Okuda	augmented. CD 1 leads purchase		CO's to date:	N/A	
A Share a	Contact #: 213-485-1165	negotiations (coordination with Trust for Public Land).		Rev. Constr. Contr.:	N/A	
				Payment to date:	N/A	e Land Design Bid & Const Post Const
and the shall be	Photo of G2 Parcel & LA River	Funding: Prop O & TBD		Expected Acquisition Date:	TBD	sign Acquire Award

PROJECT STATUS REPORT

PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION COS	T PERCENT COMPLETE
Temescal Canyon Park Stormwater BMP Ph I				Notice to Proceed:	8/17/2011
	CD 11 - Bill Rosendahl	Divert stormwater from an	Excavation for the underground	Contract Duration: City Engineer's Est.	540 days
15900 Pacific Coast Highway	Designer: AECOM	existing storm drain to Temescal Canyon Park for treatment by a	storm water storage tank continues. Work on the storm	, 0	8,008,800
	Contractor: LA Engineering, Inc.	hydrodynamic separator, underground detention tank and	drain diversion structure in the middle of Temescal Canyon		7,019,800
	Proj. Mgr.: Iftekhar Ahmed	diversion to a sanitary sewer for treatment at treatment plant.	Road has begun.		7,721,780
	Contact #: 213-485-5875			(3, 0%): Award Amount +	\$0
1 States					7,019,800 45%
	Proposed Project Layout	Funding: Prop O		Master Sch. Constr. Completion Date:	JUL 2013
Temescal Canyon Park					
Stormwater BMP Ph II	CD 11 - Bill Rosendahl	Phase II of the Temescal Canyon	A task order solicitation was	Est. Prop O Constr. Cost: \$	2,995,191
15900 Pacific Coast Highway	Designer: TBD	Park Stormwater BMP Project proposes the construction of an	advertised for the pre-design of this project, along with the	Orig. Const. Contr.:	N/A
E SULLESS	Contractor: TBD	onsite stormwater treatment /	Penmar Water Quality	CO's to date:	N/A
1074- State 6415	Proj. Mgr.: Katie Clark	disinfection system. The treated stormwater is to be used for	Improvements Phase II Project, on 5/14/2012. Proposals are due		
	Contact #: 213-847-0395	landscape irrigation.	on 6/15/2012.	Rev. Constr. Contr.:	N/A
				Payment to date:	N/A 38%
and the second	Proposed Project Layout	Funding: Prop O		Master Sch. Constr. Completion Date:	Pre Land Design Bid & Const Post Const Acquire Acquire Award
Westchester Stormwater					
BMP		Capture and treat stormwater	Bureau of Sanitation (BOS) staff	Est. Prop O Constr.	
Los Angeles World Airport	CD 11 - Bill Rosendahl Designer: AECOM	runoff from three existing	continues to work with LAWA to		6,500,000
	Contractor: TBD	stormdrains through the project BMP elements, including Trash	finalize the lease agreement of the project site.	Orig. Const. Contr.: CO's to date:	N/A N/A
	Proj. Mgr.: Salem Garawi	Net System, Underground Detention Tank and Underground			
	Contact #: 213-847-0345	Infiltration Facility.		Rev. Constr. Contr.:	N/A
				Payment to date:	N/A
 Section of the section of the section	Proposed Project Layout	Funding: Prop O		Master Sch. Constr. Completion Date:	Pre Land Bid & Const Post Const Design Acquire Award OCT 2014
Westminster Dog Park					<u></u>
Stormwater BMP		Includes installation of a modular	This project is complete.	Prop O Constr.	
1203 South Main Street	CD 11 - Bill Rosendahl	constructed wetland	This project is complete.		\$385,330
	Designer: PSOMAS	(bioremediation filter), so that on- site runoff will be captured and			\$285,330
	Contractor: Fleming Environmental, Inc. Proj. Mgr.: Salem Garawi	treated prior to discharging into		CO's to date:	(\$30,370)
	Proj. Mgr.: Salem Garawi Contact #: 213-847-0345	the storm drain system.	בקרןבןע,	Rev. Constr. Contr.:	\$254,960
					\$254,585 100%
				Master Sch. Constr.	Pre Land Design Bid & Const Post Const Design Acquire Award
	Photo of Existing Dog Park	Funding: Prop O		Completion Date:	FEB 2010

PROJECT STATUS REPORT

PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION CO	DST	PERCENT	COMPL	ETE		
Westside Park Rainwater				Notice to Proceed:	6/3/2010					
Irrigation	CD 10 - Herb J. Wesson, Jr.	Treat pollutants from on-site and	Project is in the post-construction	Contract Duration:	270 days					
2785 Clyde Avenue	Designer: PSOMAS	off-site stormwater by installing a p stormwater lift station, a subsurface irrigation system, and a dry creek with a perforated pipe for collecting and returning excess irrigation water to the existing stormdrain.	· · ·	City Engineer's Est. (Class A): Contract Award	\$2,766,900					
	Contractor: PPC Construction, Inc.			Amount: Contract Award +	\$2,675,963					
	Proj. Mgr.: Iftekhar Ahmed			Contingency (10%) CO's to date	\$2,943,559					
	Contact #: 213-485-5875			(37, 22%):	\$600,216					
				Award Amount + CO's Issued	\$3,276,179					95%
		Funding: Prop O, Prop 50, Prop		Construction		Pre Land Design Acquire	Design	Bid & O Award	Const	Post Const
	Photo of Completed Park	K, Quimby		Completion Date:	AUG 2011	Doolgii		/ mara		



5.0 APPENDIX

5.1 Map of Proposition O Projects Approved for Implementation

See attached

5.2 Catch Basin Retrofits Screen Covers and Inserts by Council Districts

CATCH BASIN RETROFITS						
Council	Inserts			Screen Covers		
District	Phase I	Phase III		Phase I & II	Phase III	
	(COMPLETED)			(COMPLETED)		
	Installed	Planned	Installed	Installed	Planned	Installed*
1	1,174	200	0	960	960	960
2	0	10	0	505	1,436	1,436
3	0	10	0	1,230	1,790	1,790
4	580	500	0	890	1,454	1,454
5	98	20	0	1,186	2,673	2,673
6	0	0	0	380	1,162	1,162
7	0	0	0	960	1,306	1,306
8	1,370	50	0	1,526	1,611	1,611
9	1,300	500	0	1,936	1,040	1,040
10	809	100	0	1,200	1,716	1,716
11	71	10	0	399	2,581	2,581
12	0	20	0	985	2,294	2,294
13	570	320	0	790	941	941
14	1,480	220	0	1,125	1,642	1,642
15	168	40	0	228	1,581	1,581
TOTALS	7,620	2,000	0	14,300	24,219	24,219

Proposition O Projects Approved for Implementation

