

September 2012 Monthly Report



Bio-Retention basin at parking lot of Peck Park Canyon Project

Administrative Oversight Committee

Miguel Santana, City Administrative Officer, Chair Andrea A. Alarcón, Board of Public Works Gerry Miller, Chief Legislative Analyst Ronald Nichols, Department of Water and Power Romel Pascual, Office of the Mayor

Citizens Oversight Advisory Committee

Adi Liberman, Chair Francine Diamond Mark Gold Tiger Kang Miguel Luna Cynthia McClain-Hill Craig A. Perkins M. Teresa Villegas

PREPARED BY BUREAU OF ENGINEERING PROP O BOND DIVISION





Distribution List

Miguel Santana, City Administrative Officer Andrea A. Alarcón, President Gerry F. Miller, Chief Legislative Analyst Ronald Nichols, General Manager Romel Pascual, Deputy Mayor Adi Liberman, Chair Dayna Bochco Francine Diamond Mark Gold Tiger Kang Miguel Luna Cynthia McClain-Hill Craig A. Perkins M. Teresa Villegas Jerilyn Lopez Mendoza, Vice President Capri W. Maddox Steven T. Nutter, Commissioner Valerie Lynne Shaw, Commissioner Gary Lee Moore, City Engineer John L. Reamer, Jr., Director Nazario Sauceda, Director Enrique C. Zaldivar, Director Victoria Santiago, Director Jon Kirk Mukri, General Manager Kenneth R. Redd, Deputy City Engineer Adel H. Hagekhalil, Assistant Director Edward Jordan, Assistant City Attorney David H. Hirano Rafael E. Prieto Charles E. Modica Michael E. Mullin David Pettijohn Shahram Kharaghani Kendrick K. Okuda

Office of the City Administrative Officer (CAO) Board of Public Works Office of the Chief Legislative Analyst (CLA) Department of Water and Power (DWP) Mavor's Office Citizens Oversight Advisory Committee Citizens Oversight Advisory Committee **Citizens Oversight Advisory Committee** Citizens Oversight Advisory Committee **Board of Public Works Board of Public Works** Board of Public Works **Board of Public Works** Bureau of Engineering (BOE) Bureau of Contract Administration **Bureau of Street Services** Bureau of Sanitation (BOS) Board of Public Works, Office of Accounting Department of Recreation & Parks (RAP) BOE BOS City Attorney's Office CAO CLA CLA Mayor's Office DWP BOS BOE

Comments or suggestions regarding the Proposition O Monthly Report may be directed to Kendrick K. Okuda, BOE Proposition O Implementation Program Manager, at 213-485-1165 or email at <u>Kendrick.Okuda@lacity.org</u>

This report is available for viewing online at the Bureau of Engineering website: <u>http://eng.lacity.org/projects/prop_o/report2012.htm</u>




TABLE OF CONTENTS

Section

Page

1.0	Execu	utive Su	mmary		
	1.1	Progra	ım Summa	iry	4
		1.1.1	COAC, A	OC, and Other Highlights	4
		1.1.2		es	5
		1.1.3		ommunity Meetings Schedule	6
	1.2	Bond	Sales		7
	1.3	Projec	t Status Su	ummary	8
		1.3.1	COAC &	AOC Project Funding Recommendations	8
			1.3.1.1	COAC & AOC Project Recommendations	8
		1.3.2	Projects i	n Implementation	9
		1.3.3		nd Program Budget Summary	10
			1.3.3.1	Project Budget Summary	10
			1.3.3.2	Program Budget Summary	11
			1.3.3.3	Project Funding Summary	12
2.0	<u>Schee</u>	<u>dule</u>			
	2.1	Projec	t Schedule	9S	13
	2.2	Progra	m Master	Schedule	14
3.0	<u>Budg</u>	<u>et</u>			
	3.1	Budge	t vs. Actua	al Expenditure	15
4.0	<u>Proje</u>	ct Statu	<u>s</u>		
	4.1	Projec	t Status Re	eport	19
5.0	<u>Apper</u>	<u>ndix</u>			
	5.1	Map o	f Propositio	on O Projects Approved for Implementation	31
	5.2	Table	of Catch B	asin Retrofits Screen Covers and Inserts by Council Districts	30
	5.3	Counc	il District M	Лар	32



1.0 EXECUTIVE SUMMARY

1.1 Program Summary

In November 2004, voters of the City of Los Angeles passed the Proposition O - Clean Water Bond, authorizing \$500 million of general obligation bonds for projects to protect public health by cleaning up pollution in the City's rivers, lakes, and beaches. The projects are intended to assist the City of Los Angeles in meeting Federal Clean Water Act requirements. Proposition O - Clean Water Bond will also fund improvements to protect water quality, provide flood protection, increase water conservation, provide habitat protection, and create open space.

This monthly progress report summarizes the status of activities and progress of the Proposition O - Clean Water Bond program, for September 2012.

1.1.1 <u>Citizens Oversight Advisory Committee (COAC)</u>, <u>Administrative Oversight</u> <u>Committee (AOC)</u>, and <u>Other highlights</u>

- At the September 19, 2012 meeting the COAC heard a report on the Master Schedule update and the South Los Angeles Wetlands project. The COAC that the Vermont Corridor project be placed on a future COAC agenda. The COAC President advised that Dayna Bochco was no longer a member of the COAC.
- On September 27, 2012 the AOC met and authorized BOE to expend \$1.2 million of the \$3.0 Million reimbursement from the state for the Albion Demolition & remediation project, for the purpose of completing project site remediation. The AOC also concurred with BOE recommendation to use the remaining unexpended funds from the South Los Angeles Wetlands Park construction budget in an amount not to exceed \$350,000, for the purpose of installing a redundant wetlands liner.



1.1.2 Key Issues

Albion Dairy Demolition and Remediation Project

- **Issue:** Unforeseen soil contamination was discovered under the foundations of two buildings that were demolished.
- Status: Two underground fuel tanks were removed under the direction of the Los Angeles Fire Department (LAFD) and the LAFD referred environmental regulation of the project to the Los Angeles Regional Water Quality Control Board (LARWQCB). The project team met with Executive Director and members of LARWQCB staff to develop a work plan for additional remediation and monitoring. LARWQCB required additional soil sampling, groundwater monitoring, and soil vapor sampling prior to evaluating and approval of further remediation.
- Action: The City has submitted the Environmental Site Characterization report to the LARWQCB. On September 27, 2012 LARWQCB approved the Environmental Site Characterization report while requiring additional soil remediation.

• Machado Lake Phase 1 (Wilmington Drain) Project

- Issue: This project is on Los Angeles County Flood Control District (LACFCD) Property. LACFCD requirements for this project include increasing the capacity of the Wilmington Drain channel by removing sediment from the channel at LACFCD's cost. The agreement between the City (BOS) and LACFCD has not been finalized; but it is needed to secure the needed funding from LACFCD in order to proceed with construction. The Wilmington Drain channel maintenance agreement between the LACFCD and California Department of Fish and Game (CDFG) need to be resolved.
- Status: LACFCD and the CDFG have a difference of opinion on maintenance of channel. Prop O team is facilitating a resolution on maintenance agreement with CDFG. On May 22, 2012, Prop O team met with CDFG, LACFCD and the City to resolve issues regarding Section 2081, California Endangered Species Act (CESA) permit.
- Action: In response to CDFG request, the city prepared report with impacts to Least Bell's Vireo (LBV) use areas resulting from the construction of the Project. City is waiting for CDFG review of the report and issuance of CESA permit.

• South LA Wetlands Park Project

- **Issue:** The daily drop of the wetland water surface elevation appears to exceed expected evaporation rates.
- **Status:** An evaluation of alternatives to identify cause of water elevation drop and to mitigate water losses is on-going.
- Action: The preferred alternative to mitigate excessive water loss is installation of plastic liner.

Westchester Stormwater BMP Project

- Issue: Land use agreement between the City (BOS) and Los Angeles World Airport (LAWA) has not been finalized.
- **Status:** Meeting with Mayor's Office, CLA, City Attorneys Office, BOS, LAWA, and BOE held to resolve this issue.
- Action: City Attorney, LAWA, and BOS are working to document and finalize resolution of land use issues.



1.1.3 Project Community Meetings Schedule

The following is a list of Proposition O project meetings with the public that occurred in September and are planned for the month of October.

	COMMUNITY MEETINGS										
Date	Time	Project	Group	Location							
9/4/12	10:00 AM	Santa Monica Bay Low Flow Diversion Upgrades Package 3 and Temescal Canyon Park Stormwater BMP Phase 1	PCH Taskforce Quarterly Meeting	23519 W. Civic Center Way, Malibu, CA 90265							



1.2 Bond Sales

The following table is a summary of the bond sales that fund Proposition O.

General Obligation Bonds Approved by Voters	3		\$500,000,000
Total Bond Sales to Date			\$439,500,000
Fund 16F July 13, 2005 City Council Approved Bond Sale (Ord. 176839 CF 05-1408)		\$37,000,000	
Bond Interest Earnings (As of Sept. 2012)	\$3,061,458		
Fund 16M July 21, 2006 City Council Approved Bond Sale (Ord. 177733 CF 06-0600-S37)		\$8,000,000	
Bond Interest Earnings (As of Sept. 2012)	\$871,511		
Fund 16Q July 22, 2008 City Council Approved Bond Sale (Ord. 180090 CF 08-1706)		\$101,000,000	
Bond Interest Earnings (As of Sept. 2012)	\$5,678,538		
Fund 16T July 21, 2009 City Council Approved Bond Sale (Ord. 180808 CF 09-1674)		\$176,500,000	
Bond Interest Earnings (As of Sept. 2012)	\$8,351,753		
Fund 16V July 28, 2011 City Council Approved Bond Sale (Ord. 181755 CF 11-0841)		\$117,000,000	
Bond Interest Earnings (As of Sept. 2012)	<u>\$ 1,419,235</u>		
Total Bond Interest Earnings to Date	\$19,382,495		

1.3 Project Status Summary

1.3.1 COAC & AOC Funding Recommendations (Pending Mayor Approval)

The following table summarizes the projects approved and recommended by COAC and AOC for funding. The projects will be presented to the City Council and Mayor for approval.

	PROJECTS RECOMMENDED FOR FUNDING BY COAC AND AOC													
Project Title	Applicant	Prop O Funding Request	Prop O Set Aside Funds Request	Funds From Other Sources (if applicable)	Total Project Funding Needed	Prop O Funding Recommendations		Month/Year Recommended by COAC & AOC						
						COAC	AOC							
N/A	N/A	\$0	\$0	\$0	\$0	\$0	\$0	N/A						
				TOTALS										
		\$0	\$0	\$0	\$0	\$0	\$0							

1.3.1.1 COAC & AOC Project Recommendations (Pending Funding Availability)

The following table summarizes the projects approved by COAC and AOC, pending availability

PROJECTS RECOMMENDED BY COAC AND AOC													
Project Title	Applicant	Prop O Funding Request	Prop O Set Aside Funds Request	Funds From Other Sources (if applicable)	Total Project Funding Needed	Month/Year Recommended by COAC & AOC							
Aliso Creek & Limekiln Creek Restoration	Mountains Recreation and Conservation Authority	\$7,842,042*	\$0	\$0	\$7,842,042	July 2007							
Boyle Heights JointCity of LA,Use CommunityCouncil DistrictCenter14		\$2,291,000*	\$0	\$528,000	\$2,819,000	July 2007							
			TOTALS										
		\$10,133,042	\$0	\$528,000	\$10,661,042								

* No Proposition O funding is available to fund this project at this time.



1.3.2 Projects in Implementation (Approved by City Council & Mayor)

The following table lists the projects approved for Proposition O funding by the City Council and the Mayor.

PROJEC	TS IN IMPLEMEN			
Project Title	Prop O Funding Approved	Prop O Set Aside Approved	Total Project Budget	Potential Funds From Other Sources*
Projects in Pre-Design	Approveu	Approveu	Buuget	Other Sources
Penmar Water Quality Improvement Phase II	\$2,830,200	\$0	\$2,830,200	\$0
emescal Canyon Park Stormwater BMP Phase II	\$3,698,565	\$0 \$0	\$3,698,564	\$0
and Acquisition Projects	ψ3,030,303	ΨΟ	ψ 0,000,00 4	ψυ
aylor Yard River Park – Parcel G2 Land Acquisition	\$0	\$12,440,000	TBD	TBD
Projects in Design	ψυ	ψ12, 44 0,000	TDD	100
Glenoaks/Sunland Stormwater Capture	\$508,696	\$0	\$508,696	\$0
Strathern Wetlands Park	\$7,800,000	\$0 \$0	\$22,000,000	\$0
Vestchester Stormwater BMP	\$32,722,000	\$0	\$22,000,000	\$14,200,000
	\$32,722,000	φŪ	\$32,722,000	ΦΟ
Projects in Bid & Award	#000.000	\$ 0	¢4.075.000	¢ 4 4 0 0 0 0
Elmer Avenue Phase II: Elmer Paseo	\$829,000	\$0	\$1,275,000	\$446,000
Achado Lake Ecosystem Rehabilitation	\$99,523,897	\$0	\$99,523,897	\$956,997
Aachado Lake Phase I (Wilmington Drain)	\$21,049,911	\$0	\$21,049,911	\$4,397,500*
Projects in Construction	#0.050.400	*	#0.050.100	¢0 577 (76
Ibion Dairy Park – Demolition & Remediation	\$3,956,400	\$0	\$3,956,400	\$3,577,476
Catch Basin Opening Screen Covers Phase III	\$44,500,000	\$0	\$44,500,000	\$0
cho Park Lake Rehabilitation	\$84,263,313	\$0	\$84,263,313	\$599,875
Penmar Water Quality Improvement Phase I	\$20,754,800	\$0	\$20,754,800	\$0
Rosecrans Recreation Center Stormwater Enhancements	\$4,829,119	\$0	\$6,754,033	\$1,924,914
anta Monica Bay Low Flow Diversion Upgrades Pkg. 3	\$20,634,036	\$0	\$20,634,036	\$7,000,000
emescal Canyon Park Stormwater BMP Phase I	\$14,947,435	\$0	\$14,947,436	\$0
Projects in Post Construction	-	1		
lansen Dam Wetlands Restoration	\$2,220,702	\$0	\$2,517,702	\$297,000
Iar Vista Recreation Center Stormwater BMP	\$4,556,186	\$0	\$4,556,186	\$2,077,838*
eck Park Canyon Enhancement	\$6,190,000	\$0	\$8,231,118	\$2,041,118*
outh Los Angeles Wetlands Park (includes Site Readiness)	\$16,678,202	\$0	\$26,374,067	\$13,001,866*
Projects Completed				
Ibion Dairy Park – Land Acquisition	\$17,560,000	\$0	TBD	TBD
Catch Basin Inserts and Coverings Phase I	\$14,702,886	\$0	\$14,702,886	\$600,000*
atch Basin Opening Screen Covers Phase II	\$9,362,404	\$0	\$9,362,404	\$0
cesar Chavez Ground Water Improvement (a.k.a Sheldon Arleta)	\$3,040,000	\$0	\$9,841,230	\$6,801,230
Grand Blvd. Tree Wells	\$780,282	\$0	\$780,282	\$350,000*
nperial Highway Sunken Median Stormwater BMP	\$2,723,403	\$0	\$2,723,403	\$0
nner Cabrillo Beach Bacterial Water Quality Improvement	\$8,000,000	\$0	\$16,000,000	\$8,000,000
a Cienega/Fairfax Stormwater BMP (CANCELED)	\$668,159	\$0	\$668,159	\$0
os Angeles Zoo Parking Lot	\$13,904,243	\$0	\$13,904,243	\$0
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 1	\$6,814,377	\$0	\$6,814,377	\$5,131,497**
anta Monica Bay Low Flow Diversion Upgrades Pkg. 2	\$3,380,111	\$0	\$3,380,111	**
Dros Green Street	\$197,600	\$0	\$784,251	\$586,651
anta Monica Bay Low Flow Diversion Upgrades Pkg. 4	\$6,290,504	\$0	\$6,290,504	**
Strathern Pit Multiuse - Land Acquisition	\$10,000,000	\$0	\$28,000,000	\$18,000,000
Vestminster Dog Park Stormwater BMP	\$1,438,755	\$0	\$1,438,755	\$0
Vestside Park Rainwater Irrigation	\$6,904,589	\$0	\$8,304,589	\$3,192,038*
	TOTALS	÷ •	+ - , ,	· · · · · · · · · · · · · · · ·
	\$498,259,775	\$12,440,000	\$544,092,553	\$78,982,000



1.3.3 Project and Program Budget Summary

1.3.3.1 Total Project Budget Summary

The following table is a summary of the Proposition O project funding.

	PROJECT BUDGET SUMMARY											
Description	Prop O Funding	Prop O Set Aside	Potential Funds From Other Sources*	Total Project Budget								
Projects In Planning– Prop O Funding Request	\$0	\$0	\$0	\$0								
Projects Recommended by AOC	\$0	\$0	\$0	\$0								
Projects In Implementation	\$498,259,775	\$12,440,000	\$78,982,000	\$544,092,553								
		тот	ALS									
	\$498,259,775	\$12,440,000	\$78,982,000	\$544,092,553								
Prop O Total Project Obligation	\$510,6	99,775										

*Estimated grant funds/reimbursements that may be available

1.3.3.2 Program Budget Summary

The table on the following pages gives an updated program budget summary for Proposition O.

1.3.3.3 Project Funding Summary

The table on the following pages gives an updated project funding summary for Proposition O.

Prop O - Program Budget Summary

Project Title		ncil / Mayor oproved	Approved Set-Asides	Future Needs	Cost Reductions	Prop O Bu & Fundi
Albion Dairy Park - Demolition & Remediation	\$	3,956,400				\$ 3,956
Albion Dairy Park - Land Acquisition - COMPLETED		3,956,400				\$ 3,950
Aliso Wash - Limekiln Creek Confluence Restoration	\$	-				\$ 17,500
Boyle Heights Joint Use Community Center Improvements	\$	-				\$
Catch Basin Inserts and Coverings Phase I - COMPLETED	- · ·	17,000,000			\$ (2,297,114)	\$ 14,702
Catch Basin Opening Screen Covers Phase II - COMPLETED		10,000,000			\$ (637,596)	\$ 9,362
Catch Basin Opening Screen Covers Phase III		44,500,000				\$ 44,500
Cesar Chavez Ground Water Improvement	\$	3,040,000				\$ 3,040
Echo Park Lake Rehabilitation		84,263,313				\$ 84,263
Elmer Avenue Phase II: Elmer Paseo Glenoaks/Sunland Stormwater Capture	\$ \$	829,000 508.696				\$ 829 \$ 508
Grand Blvd. Tree Wells - COMPLETED	\$	1,075,927			\$ (295,645)	\$ 780
Hansen Dam Wetlands Restoration	\$	2,220,702			φ (200,010)	\$ 2,220
mperial Highway Sunken Median Stormwater BMP	\$	2,723,403				\$ 2,723
nner Cabrillo Beach Bacterial Water Quality Improvement	\$	8,000,000				\$ 8,000
a Cienega/Fairfax Stormwater BMP - CANCELED	\$	7,667,887			\$ (6,999,728)	\$ 668
os Angeles Zoo Parking Lot		13,904,243				\$ 13,904
Machado Lake-Phase I (Wilmington Drain)		21,049,911				\$ 21,049
Machado Lake Ecosystem Rehabilitation		99,523,897				\$ 99,523
Mar Vista Recreation Center Stormwater BMP	\$	4,556,186			¢ (400.400)	\$ 4,556
Dros Green Street - COMPLETED Peck Park Canyon Enhancement	\$ \$	386,000			\$ (188,400)	\$ 197 \$ 6.190
Perk Park Canyon Ennancement Penmar Water Quality Improvement Phase I		6,190,000 20,754,800				\$ 6,190 \$ 20,754
Penmar Water Quality Improvement Phase I	\$	2,830,200				\$ 2,830
Rosecrans Recreation Center Stormwater Enhancements	\$	4,829,119				\$ 4,829
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 1	\$	6,814,377				\$ 6,814
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 2	\$	3,380,111				\$ 3,380
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 3	\$ 2	20,634,036				\$ 20,634
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 4	\$	6,290,504				\$ 6,290
South Los Angeles Wetlands Park (includes Site Readiness)		16,678,202				\$ 16,678
Strathern Pit Multiuse - Land Acquisition		10,000,000				\$ 10,000
Strathern Wetlands Park	\$	7,800,000				\$ 7,800
Taylor Yard River Park - Parcel G2 Land Acquisition	^	11017 105	\$ 12,440,000			\$ 12,440
Temescal Canyon Park Stormwater Phase I Temescal Canyon Park Stormwater Phase II	\$ \$	14,947,435				\$ 14,947 \$ 3,698
Westchester Stormwater BMP		3,698,565 32,722,000				\$ 3,698 \$ 32,722
Westminster Dog Park Stormwater BMP	\$	1,438,755				\$ 1,438
Westside Park Rainwater Irrigation	\$	6,904,589				\$ 6,904
Total - Project Budget			\$ 12,440,000	\$ -	\$ (10,418,483)	
City Staff - Program Related Budget (as of June 30, 2011)		00,010,200	φ 12,110,000	Ŷ	φ (10,110,100)	φ 010,000
Office of Accounting	\$	587,723		\$ 491,450		\$ 1,079
Bureau of Contract Administration						\$
Bureau of Engineering	\$	2,003,796		\$ 2,504,606		\$ 4,508
Duran au of Consideration	\$	4,081,839		\$ 2,586,746		\$ 6,668
Bureau of Sanitation				. , ,		
Related Costs	\$	2,333,524		\$ 1,746,497		\$ 4,080
Related Costs Subtotal	\$			\$ 1,746,497 \$ 7,329,299		
Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011)	\$ I \$	2,333,524 9,006,882		. , ,	1	\$ 4,080 \$ 16,330
Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation	\$ I \$	2,333,524 9,006,882 600,000		. , ,	\$ (136)	\$ 4,080 \$ 16,330 \$ 599
Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development	\$ I \$ \$	2,333,524 9,006,882 600,000 360,000		. , ,		\$ 4,080 \$ 16,330 \$ 599 \$ 360
Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal	\$ I \$ \$ I \$	2,333,524 9,006,882 600,000 360,000 960,000		\$ 7,329,299	\$ (136)	\$ 4,080 \$ 16,330 \$ 599 \$ 360 \$ 959
Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Total - Prop O Budget	\$ \$ \$ \$ \$ t \$ 5	2,333,524 9,006,882 600,000 360,000 960,000 18,645,140	\$ 12,440,000	\$ 7,329,299	\$ (136)	\$ 4,080 \$ 16,330 \$ 599 \$ 360 \$ 959
Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Total - Prop O Budget FUND	\$ \$ \$ \$ \$ t \$ 5	2,333,524 9,006,882 600,000 360,000 960,000	\$ 12,440,000	\$ 7,329,299	\$ (136)	\$ 4,080 \$ 16,330 \$ 599 \$ 360 \$ 959
Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Full Proposal Development Subtotal Total - Prop O Budget FUNDI FUNDI FUNDI FUNDI	\$ \$ \$ \$ \$ 1 \$ 1 \$ 1 \$ 1 \$ 1 \$	2,333,524 9,006,882 600,000 360,000 960,000 18,645,140 DURCES	\$ 12,440,000	\$ 7,329,299	\$ (136)	\$ 4,080 \$ 16,330 \$ 599 \$ 360 \$ 959 \$ 959 \$ 360 \$ 959 \$ 360 \$ 959 \$ 527,99
Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Full Proposal Development Subtotal Total - Prop O Budget FUND Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale	\$ 	2,333,524 9,006,882 600,000 360,000 960,000 18,645,140 DURCES 37,000,000	\$ 12,440,000	\$ 7,329,299	\$ (136)	\$ 4,080 \$ 16,330 \$ 599 \$ 366 \$ 959 \$ 366 \$ 959 \$ 367,000 \$ 37,000
Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Full Proposal Development Subtotal Total - Prop O Budget FUND Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - First Sale Bond Proceeds - First Sale Interest	\$ 	2,333,524 9,006,882 600,000 360,000 960,000 18,645,140 DURCES 37,000,000 3,042,656	\$ 12,440,000	\$ 7,329,299	\$ (136)	\$ 4,080 \$ 16,330 \$ 599 \$ 366 \$ 959 \$ 366 \$ 959 \$ 366 \$ 366 \$ 366 \$ 366 \$ 37,000 \$ 37,000 \$ 3,042
Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Full Proposal Development Subtotal Total - Prop O Budget FUND Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - First Sale Bond Proceeds - First Sale Bond Proceeds - Second Sale	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,333,524 9,006,882 600,000 360,000 960,000 18,645,140 DURCES 37,000,000 3,042,656 8,000,000	\$ 12,440,000	\$ 7,329,299	\$ (136)	\$ 4,080 \$ 16,330 \$ 599 \$ 366 \$ 955 \$ 527,999 \$ 37,000 \$ 37,000 \$ 3,042 \$ 8,000
Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Full Proposal Development Subtotal Total - Prop O Budget FUND Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - First Sale Bond Proceeds - Second Sale Bond Proceeds - Second Sale Bond Proceeds - Second Sale Bond Proceeds - Second Sale	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,333,524 9,006,882 600,000 360,000 960,000 18,645,140 DURCES 37,000,000 3,042,656 8,000,000 854,249	\$ 12,440,000	\$ 7,329,299	\$ (136)	\$ 4,080 \$ 16,330 \$ 599 \$ 360 \$ 955 \$ 527,999 \$ 37,000 \$ 3,042 \$ 8,000 \$ 854
Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Full Proposal Development Subtotal Total - Prop O Budget FUNDI Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - First Sale Bond Proceeds - Second Sale Bond Proceeds - Second Sale Bond Proceeds - Second Sale Bond Proceeds - Third Sale	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,333,524 9,006,882 600,000 360,000 960,000 18,645,140 DURCES 37,000,000 3,042,656 8,000,000 854,249 01,000,000	\$ 12,440,000	\$ 7,329,299	\$ (136)	\$ 4,080 \$ 16,330 \$ 599 \$ 360 \$ 955 \$ 527,999 \$ 37,000 \$ 37,000 \$ 37,000 \$ 37,000 \$ 37,000 \$ 37,000 \$ 3,042 \$ 8,000 \$ 854 \$ 101,000
Subtotal Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Full Proposal Development Subtotal Total - Prop O Budget FUNDI Bond Proceeds - First Sale Bond Proceeds - First Sale Interest Bond Proceeds - Second Sale Interest Bond Proceeds - Second Sale Interest Bond Proceeds - Third Sale Bond Proceeds - Third Sale Bond Proceeds - Third Sale	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,333,524 9,006,882 600,000 360,000 960,000 18,645,140 DURCES 37,000,000 3,042,656 8,000,000 854,249 01,000,000 5,142,889	\$ 12,440,000	\$ 7,329,299	\$ (136)	\$ 4,080 \$ 16,330 \$ 599 \$ 360 \$ 360 \$ 37,000 \$ 37,000 \$ 3,042 \$ 8,000 \$ 8,000 \$ 8,000 \$ 101,000 \$ 5,142
Subtotal Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Full Proposal Development Subtotal Total - Prop O Budget FUNDI Gunding Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - First Sale Bond Proceeds - First Sale Interest Bond Proceeds - Second Sale Bond Proceeds - Second Sale Bond Proceeds - Third Sale	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,333,524 9,006,882 600,000 360,000 960,000 18,645,140 DURCES 37,000,000 3,042,656 8,000,000 854,249 01,000,000	\$ 12,440,000	\$ 7,329,299	\$ (136)	\$ 4,080 \$ 16,330 \$ 599 \$ 360 \$ 360 \$ 360 \$ 37,000 \$ 3,042 \$ 3,042
Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation FUI Full Proposal Development Subtotal Subtotal Total - Prop O Budget FUNDI Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - First Sale Interest Bond Proceeds - Second Sale Bond Proceeds - Second Sale Bond Proceeds - Third Sale Bond Proceeds - Third Sale Bond Proceeds - Third Sale Bond Proceeds - Third Sale Bond Proceeds - Third Sale	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,333,524 9,006,882 600,000 360,000 960,000 18,645,140 DURCES 37,000,000 3,042,656 8,000,000 854,249 01,000,000 5,142,889 76,500,000	\$ 12,440,000	\$ 7,329,299	\$ (136)	\$ 4,080 \$ 16,330 \$ 599 \$ 360 \$ 360 \$ 955 \$ 527,99 \$ 527,99 \$ 37,000 \$ 3,042 \$ 8,000 \$ 8,000 \$ 8,000 \$ 3,042 \$ 101,000 \$ 104,000 \$ 104,000 \$ 104,000 \$ 3,042 \$ 104,000 \$ 104,0000 \$ 104,0000 \$ 104,0000 \$ 104,0000 \$ 104,0000 \$ 104,0000 \$ 104,00000 \$ 104,0000 \$ 104,0000 \$ 104,0000 \$
Subtotal Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation FUI Full Proposal Development Subtotal Subtotal Total - Prop O Budget FUNDI FUNDI FUNDI FUNDI FUNDI Bond Proceeds - First Sale Bond Proceeds - First Sale Interest Bond Proceeds - Second Sale Bond Proceeds - Second Sale Bond Proceeds - Third Sale Bond Proceeds - Third Sale Bond Proceeds - Third Sale Bond Proceeds - Third Sale Bond Proceeds - Fourth Sale Bond Proceeds - Fourth Sale	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,333,524 9,006,882 600,000 360,000 960,000 18,645,140 DURCES 37,000,000 3,042,656 8,000,000 854,249 01,000,000 5,142,889 76,500,000 5,858,814	\$ 12,440,000	\$ 7,329,299	\$ (136)	\$ 4,080 \$ 16,330 \$ 599 \$ 360 \$ 360 \$ 37,000 \$ 37,000 \$ 37,000 \$ 3,042 \$ 8,000 \$ 3,042 \$ 4,080 \$ 37,000 \$ 3,042 \$ 101,000 \$ 5,142 \$ 176,500 \$ 5,858
Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Total - Prop O Budget Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - First Sale Interest Bond Proceeds - Second Sale Bond Proceeds - Third Sale Bond Proceeds - Third Sale Bond Proceeds - Fourth Sale	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,333,524 9,006,882 600,000 360,000 960,000 18,645,140 DURCES 37,000,000 3,042,656 8,000,000 854,249 01,000,000 5,142,889 76,500,000 5,858,814	\$ 12,440,000 \$ 12,440,000	\$ 7,329,299	\$ (136)	\$ 4,080 \$ 16,330 \$ 599 \$ 366 \$ 959 \$ 366 \$ 959 \$ 366 \$ 366 \$ 959 \$ 37,000 \$ 3,042 \$ 8,000 \$ 3,042 \$ 8,000 \$ 101,000 \$ 5,142 \$ 176,506 \$ 176,556 \$ 117,000 \$ 3,856 \$ 117,000 \$ 3,856 \$ 107,000 \$ 3,856 \$ 107,000 \$ 3,856 \$ 107,000 \$ 3,856 \$ 107,000 \$ 3,856 \$ 107,000 \$ 3,856 \$ 107,000 \$ 3,856 \$ 5,856 \$
Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Total - Prop O Budget Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - First Sale Interest Bond Proceeds - Second Sale Bond Proceeds - Second Sale Bond Proceeds - Third Sale Bond Proceeds - Third Sale Bond Proceeds - Fourth Sale Bond Proceeds - Futth Sale Interest Bond Proceeds - Futth Sale Bond Proceeds - Futthe Sales Bond Proceeds - Futthe Sales Bond Proceeds - Secured Grants Received <	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,333,524 9,006,882 600,000 360,000 960,000 18,645,140 DURCES 37,000,000 3,042,656 8,000,000 854,249 01,000,000 5,142,889 76,500,000 5,858,814		\$ 7,329,299 \$ 7,329,299 \$ 7,329,299	\$ (136)	\$ 4,080 \$ 16,330 \$ 599 \$ 366 \$ 959 \$ 366 \$ 366 \$ 366 \$ 37,000 \$ 3,042 \$ 4,050 \$ 3,042 \$ 101,000 \$ 5,142 \$ 107,000 \$ 5,556 \$ 101,000 \$ 117,000 \$ 113,412 \$ 113,
Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Total - Prop O Budget Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale FUND Bond Proceeds - First Sale Bond Proceeds - Second Sale Bond Proceeds - Second Sale Interest Bond Proceeds - Second Sale Bond Proceeds - Third Sale Bond Proceeds - Third Sale Bond Proceeds - Fourth Sale Interest Bond Proceeds - Fourth Sale Bond Proceeds - Fourth Sale Bond Proceeds - Fourth Sale Bond Proceeds - Fourth Sale Interest Bond Proceeds - Futh Sale Bond Proceeds - Futh Sale Interest Bond Proceeds - Futh Sale Bond Proceeds - Futh Sale Interest Bond Proceeds - Futh Sale Bond Proceeds - Futh Sale Bond Proceeds - Futh Sale Bond Proceeds - Futh Sale Bond Proceeds - Futh Sale Bond Proceeds - Futh Sale Bond Proceeds - Futh Sale Bond Proceeds - Futh Sale Bond Proceeds - Futh Sale Bond Proceeds - Futh Sale Bond Proceeds - Futh Sale Bond Pro	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,333,524 9,006,882 600,000 360,000 960,000 18,645,140 DURCES 37,000,000 3,042,656 8,000,000 5,42,49 01,000,000 5,142,889 76,500,000 5,858,814 17,000,000	\$ 12,440,000 (100,000) (100,000)	\$ 7,329,299 \$ 7,329,299 \$ 7,329,299 \$ 60,500,000 \$ 60,500,000	\$ (136)	\$ 4,080 \$ 16,330 \$ 599 \$ 366 \$ 959 \$ 366 \$ 366 \$ 366 \$ 37,000 \$ 3,042 \$ 4,080 \$ 37,000 \$ 3,042 \$ 3,042 \$ 4,080 \$ 3,042 \$ 4,080 \$ 3,042 \$ 4,080 \$ 3,042 \$ 4,080 \$ 3,042 \$ 3,04
Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Subtotal Total - Prop O Budget FUND Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - First Sale Bond Proceeds - First Sale Interest Bond Proceeds - Second Sale Bond Proceeds - Second Sale Bond Proceeds - Second Sale Bond Proceeds - Second Sale Interest Bond Proceeds - Third Sale Bond Proceeds - Fourth Sale Bond Proceeds - Futh Sale Bond Proceeds - Futh Sale Bond Proceeds - Futh Sale Future Sales <td>\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$</td> <td>2,333,524 9,006,882 600,000 360,000 960,000 18,645,140 DURCES 37,000,000 3,042,656 8,000,000 5,142,889 76,500,000 5,858,814 17,000,000</td> <td>\$ (100,000)</td> <td>\$ 7,329,299 \$ 7,329,299 \$ 7,329,299 \$ 60,500,000 \$ 60,500,000 \$ 7,000,000.00</td> <td>\$ (136) \$ (10,418,619) </td> <td>\$ 4,080 \$ 16,330 \$ 599 \$ 366 \$ 959 \$ 366 \$ 959 \$ 366 \$ 37,000 \$ 37,000 \$ 37,000 \$ 37,000 \$ 37,000 \$ 37,000 \$ 3,042 \$ 8,000 \$ 3,042 \$ 4,080 \$ 37,000 \$ 3,042 \$ 4,080 \$ 3,042 \$ 4,080 \$ 3,042 \$ 4,080 \$ 3,042 \$ 3,042</td>	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,333,524 9,006,882 600,000 360,000 960,000 18,645,140 DURCES 37,000,000 3,042,656 8,000,000 5,142,889 76,500,000 5,858,814 17,000,000	\$ (100,000)	\$ 7,329,299 \$ 7,329,299 \$ 7,329,299 \$ 60,500,000 \$ 60,500,000 \$ 7,000,000.00	\$ (136) \$ (10,418,619) 	\$ 4,080 \$ 16,330 \$ 599 \$ 366 \$ 959 \$ 366 \$ 959 \$ 366 \$ 37,000 \$ 37,000 \$ 37,000 \$ 37,000 \$ 37,000 \$ 37,000 \$ 3,042 \$ 8,000 \$ 3,042 \$ 4,080 \$ 37,000 \$ 3,042 \$ 4,080 \$ 3,042 \$ 4,080 \$ 3,042 \$ 4,080 \$ 3,042 \$ 3,042
Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Total - Prop O Budget Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale FUND Bond Proceeds - First Sale Bond Proceeds - Second Sale Bond Proceeds - Second Sale Interest Bond Proceeds - Second Sale Bond Proceeds - Third Sale Bond Proceeds - Third Sale Bond Proceeds - Fourth Sale Interest Bond Proceeds - Fourth Sale Bond Proceeds - Fourth Sale Bond Proceeds - Fourth Sale Bond Proceeds - Fourth Sale Interest Bond Proceeds - Fourth Sale Bond Proceeds - Futh Sale Interest Bond Proceeds - Futh Sale Bond Proceeds - Futh Sale Interest Bond Proceeds - Futh Sale Bond Proceeds - Futh Sale Bond Proceeds - Futh Sale Bond Proceeds - Futh Sale Bond Proceeds - Futh Sale Bond Proceeds - Futh Sale Bond Proceeds - Futh Sale Bond Proceeds - Futh Sale Bond Proceeds - Futh Sale Bond Proceeds - Futh Sale Bond Proceeds - Futh Sale Bond P	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,333,524 9,006,882 600,000 360,000 960,000 18,645,140 DURCES 37,000,000 3,042,656 8,000,000 5,142,889 76,500,000 5,858,814 17,000,000	\$ (100,000)	\$ 7,329,299 \$ 7,329,299 \$ 7,329,299 \$ 60,500,000 \$ 60,500,000	\$ (136) \$ (10,418,619) 	\$ 4,080 \$ 16,330 \$ 599 \$ 366 \$ 959 \$ 366 \$ 366 \$ 366 \$ 37,000 \$ 3,042 \$ 4,080 \$ 37,000 \$ 3,042 \$ 3,042 \$ 4,080 \$ 3,042 \$ 4,080 \$ 3,042 \$ 4,080 \$ 3,042 \$ 4,080 \$ 3,042 \$ 3,04
Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Subtotal Total - Prop O Budget FUND Guint Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - First Sale Interest Bond Proceeds - Second Sale Bond Proceeds - Second Sale Bond Proceeds - Second Sale Bond Proceeds - Third Sale Bond Proceeds - Third Sale Bond Proceeds - Third Sale Bond Proceeds - Fourth Sale Bond Proceeds - Futh Sale<	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,333,524 9,006,882 600,000 360,000 960,000 18,645,140 DURCES 37,000,000 3,042,656 8,000,000 5,142,889 76,500,000 5,858,814 17,000,000	\$ (100,000)	\$ 7,329,299 \$ 7,329,299 \$ 7,329,299 \$ 60,500,000 \$ 60,500,000 \$ 7,000,000.00 \$ 7,000,000.00	\$ (136) \$ (10,418,619) 	\$ 4,080 \$ 16,330 \$ 599 \$ 366 \$ 959 \$ 37,000 \$ 37,000 \$ 37,000 \$ 37,000 \$ 37,000 \$ 37,000 \$ 3,042 \$ 4,000 \$ 5,142 \$ 101,000 \$ 5,850 \$ 117,000 \$ 5,850 \$ 117,000 \$ 13,412 \$ (100 \$ 7,000 \$ 3,042 \$ 10,000 \$ 5,850 \$ 13,412 \$ (100 \$ 7,000 \$ 5,352 \$ 3,000 \$ 5,850 \$ 5,850 \$ 5,850 \$ 13,412 \$ (100 \$ 7,000 \$ 5,352 \$ 5,3552 \$ 5,3552
Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Subtotal Total - Prop O Budget FUND Guint Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - First Sale Interest Bond Proceeds - Second Sale Bond Proceeds - Second Sale Bond Proceeds - Second Sale Interest Bond Proceeds - Third Sale Bond Proceeds - Third Sale Bond Proceeds - Fourth Sale Bond Proceeds - Futh Sale Bond Proceeds -	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,333,524 9,006,882 600,000 360,000 960,000 18,645,140 DURCES 37,000,000 3,042,656 8,000,000 5,142,889 76,500,000 5,858,814 17,000,000	\$ (100,000) \$ (100,000)	\$ 7,329,299 \$ 7,329,299 \$ 7,329,299 \$ 60,500,000 \$ 60,500,000 \$ 67,500,000 Tota	\$ (136) \$ (10,418,619)	\$ 4,080 \$ 16,330 \$ 599 \$ 366 \$ 959 \$ 367 \$ 37,000 \$ 37,000 \$ 37,000 \$ 37,000 \$ 3,042 \$ 8,000 \$ 3,042 \$ 4,000 \$ 3,042 \$ 3,042 \$ 4,000 \$ 3,042 \$ 101,000 \$ 5,856 \$ 117,000 \$ 5,856 \$ 117,000 \$ 5,857 \$ 117,000 \$ 117,000 \$ 5,857 \$ 117,000 \$ 5,857 \$ 117,000 \$ 117,000 \$ 5,857 \$ 117,000 \$ 1
Related Costs Subtotal Consultants - Program Related Budget (as of as of June 30, 2011) Program Development/Implementation Full Proposal Development Subtotal Subtotal Total - Prop O Budget FUND Funding Sources (as of September, 30, 2011) Bond Proceeds - First Sale Bond Proceeds - First Sale Interest Bond Proceeds - Second Sale Bond Proceeds - Second Sale Interest Bond Proceeds - Second Sale Interest Bond Proceeds - Third Sale Bond Proceeds - Third Sale Bond Proceeds - Fourth Sale Bond Proceeds - Fith Sale Bond Proceeds - Fith Sale Bond Proceeds - Futh Sale Bond Proceeds - Fith Sale Bond Proceeds - Fith Sale Bond Proceeds - Futh Sale	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	2,333,524 9,006,882 600,000 360,000 960,000 18,645,140 DURCES 37,000,000 3,042,656 8,000,000 5,142,889 76,500,000 5,858,814 17,000,000	\$ (100,000) \$ (100,000)	\$ 7,329,299 \$ 7,329,299 \$ 7,329,299 \$ 60,500,000 \$ 60,500,000 \$ 67,500,000 Tota	\$ (136) \$ (10,418,619) 	\$ 4,080 \$ 16,330 \$ 599 \$ 366 \$ 959 \$ 367 \$ 37,000 \$ 37,000 \$ 37,000 \$ 37,000 \$ 3,042 \$ 8,000 \$ 3,042 \$ 4,000 \$ 3,042 \$ 3,042 \$ 4,000 \$ 3,042 \$ 101,000 \$ 5,856 \$ 117,000 \$ 5,856 \$ 117,000 \$ 5,857 \$ 117,000 \$ 117,000 \$ 5,857 \$ 117,000 \$ 5,857 \$ 117,000 \$ 117,000 \$ 5,857 \$ 117,000 \$ 1

Project Funding Summary

Project Title		Budget		op O Funding ith set asides)		Other Direct Funding		otential oursements	Source	Status
110,000 1100		Dudgot	(s	-	\$		Demolition escrow account	Demolition escrow check received for \$3,000,000
Albion Dairy Park - Demolition & Remediation	\$	3,956,400	\$	3,956,400	\$	556,524	\$	-	Sprint Nextel and Swiss II lease payment	Lease payment of \$556,524 received
	Ť	0,000,100	Ť	0,000,100	\$		\$	20,952	City Clerk	Rental reimbursement of \$20,952 approved
Albion Dairy Park - Land Acquisition - COMPLETED	\$	-	\$	17,560,000	T		\$	- 20,002	N/A	N/A
	÷	4.4 700 000						000 000		Grant reimbursement of \$600,000 received; grant
Catch Basin Inserts and Coverings Phase I - COMPLETED	\$	14,702,886	\$	14,702,886	\$	-	\$	600,000	Prop 40	completed
Catch Basin Opening Screen Covers Phase II - COMPLETED	\$	9,362,404	\$	9,362,404	\$		\$			
	φ		φ		-	-	•	-	N/A	N/A
Catch Basin Opening Screen Covers Phase III	\$	44,500,000	\$	44,500,000		-	\$		N/A	N/A
					\$		\$		DWP	Secured
Cesar Chavez Ground Water Improvement	\$	9,841,230	\$	3,040,000	\$	750,000 387,230			CIWMB UDAG	Secured
					\$ \$		<u></u> \$	-	CIEP	Secured Secured
Echo Park Lake Rehabilitation	¢	84,263,313	¢	84,263,313	э \$		φ \$		Prop K	Secured
Elmer Avenue Phase II: Elmer Paseo	\$	1,275,000	\$	829,000		446,000	\$	-	Council for Watershed Health	Secured
Glenoaks/Sunland Stormwater Capture	\$	508,696		508,696			\$	-	N/A	N/A
Grand Blvd. Tree Wells - COMPLETED	\$		\$				\$	250.000		Grant reimbursement of \$350,000 received; grant
Grand Bivd. Tree Wells - COMPLETED	φ	780,282	¢	780,282		-	Þ	350,000	Prop 50-SMBRP	completed
Hansen Dam Wetlands Restoration	\$	2,517,702	\$	2,220,702		- ,	\$		Caltrans - FTIP	Secured by MRCA for Design
Imperial Highway Sunken Median Stormwater BMP	\$	2,723,403	\$	2,723,403			\$	-	N/A	N/A
Inner Cabrillo Beach Bacterial Water Quality Improvement	\$	16,000,000	\$	8,000,000		8,000,000	\$	-	Port of Los Angeles	Secured
La Cienega Fairfax Stormwater BMP - CANCELED	\$	668,159	\$	668,159		-	\$	-	N/A	Project canceled
Los Angeles Zoo Parking Lot	\$	13,904,243	\$	13,904,243			\$	4 207 500	N/A Prop 50 IPW/MP	N/A Secured
Machado Lake-Phase I (Wilmington Drain)	\$	21,049,911	\$	21,049,911	\$ TBI		\$ \$		Prop 50-IRWMP LA County Flood Control District	Final Agreement Pending
Wachado Lake-Friase I (Willinington Drain)	φ	21,049,911	φ	21,049,911	ты \$			-	Lawsuit Settlement	Secured
	1				\$		\$	-	Prop K	Secured
Machado Lake Ecosystem Rehabilitation	\$	99,523,897	\$	99,523,897			Ŷ			oodubu
·····,···	·		·		\$	296,997			Coastal Conservancy	Grant reimbursement of \$296,997 paid; grant completed
							¢	4 777 000	American Recovery & Reinvestment Act	
Mar Vista Recreation Center Stormwater BMP	\$	4,556,186	\$	4,556,186	¢		\$	1,777,838	(ARRA)	Grant reimbursement of \$1,600,054 received
War visia Recreation Center Stofffwater Divir	φ	4,550,100	φ	4,550,100	φ	-	\$	300,000		Grant reimbursement of \$300,000 received; grant
							•		Prop 50-SMBRP	completed
Oros Green Street - COMPLETED	\$	784,251	\$	197,600	\$	586,651		-	Prop 13 & CWA 319th	Secured
Peck Park Canyon Enhancement	\$	8,231,118	\$	6,190,000	\$		\$	-	Prop 50	\$1,586,193 in grant funding authorized for payment
•	\$	22 505 000	¢		\$ \$	120,000	<u>\$</u> \$	-	Rec & Trails Grant N/A	\$120,000 in grant funding received; grant completed N/A
Penmar Water Quality Improvement (Phase I & II)	Ŷ	23,585,000	¢	23,585,000	э \$		<u></u> \$	-	Prop K	Secured
Rosecrans Recreation Center Stormwater Enhancements	\$	6,754,033	\$	4,829,119	\$		\$	-	TBD	Prop O K to find funding or down scope project
					,				American Recovery & Reinvestment Act	Grant reimbursement of \$4,361,106 received; ARRA
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 1	\$	6,814,377	\$	6,814,377	\$	-	\$	4,364,420	(ARRA)	funding for Pkg. 2 is bundled with Pkg. 1
Santa Monica Bay Low Flow Diversion Opgrades, Fkg. 1	φ	0,014,377	φ	0,014,377	\$		\$	767,077		Grant reimbursement of \$767,077 received; grant
					φ	-	φ	101,011	Prop 50-CBI	completed
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 2	\$	3,380,111	\$	3,380,111	\$	-	\$	-	American Recovery & Reinvestment Act	
			•		•			7 000 000	(ARRA)	ARRA funding for Pkg. 2 is bundled with Pkg. 1
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 3	\$	20,634,036	\$	20,634,036	\$		\$	7,000,000	SCM Fund	Secured
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 4	\$	6,290,504	\$	6,290,504	\$	-	\$	-	Prop 50-CBI	Prop 50-CBI funding for Pkg. 4 is bundled with Pkg. 1 Grant reimbursement of \$1,498,123 received.
					\$	-	\$	3,300,000	Prop 50-IRWMP	\$1,789,379 authorized for payment
										Grant reimbursement of \$2,011,937 received; grant
					\$	-	\$	2,011,937	Prop 12 (RZH) - for Land Acquisition	completed
					\$	1,282,721			Prop 40 (RZH)	Grant funding of \$916,188 paid
					<u>_</u>		•		Collection System Settlement Agreement -	- · ·
South Los Apagles Watende Dark (includes Otta Deadings)	\$	26 274 007	\$	16 670 000	\$		\$	-	Supplemental Environmental Project	Funding of \$2,717,394 paid
South Los Angeles Wetlands Park (includes Site Readiness)	Э	26,374,067	¢	16,678,202	\$	1,000,000	\$	-	Prop K - for Land Acquisition	Secured
	1				\$	500,000	\$	-	Prop K	Grant funding of \$500,000 paid, grant completed
	1				\$		\$	900,000	MTA - max potential reimbursement for	
					, ,				remediation	Reimbursement of \$858,525 received
	1				\$	67,501	\$	-	MTA - lease payment	Lease payment of \$67,501 received
	1				\$	-	\$	200,000	EPA - Brownfields grant	Grant reimbursement of \$199,977 received & grant
Strothern Dit Multiuse Land Agguinitien	¢	28,000,000	¢	10.000.000					LA County Flood Control District	completed Secured
Strathern Pit Multiuse - Land Acquisition Strathern Wetlands Park	\$ \$	28,000,000		10,000,000 7,800,000		18,000,000 14,200,000	\$	-	LA County Flood Control District	Secured
Taylor Yard River Park - Parcel G2 Land Acquisition	⇒ TBD		э \$	12,440,000			TBD		TBD	TBD
Temescal Canyon Park Stormwater BMP (Phase I & II)	S IBL	18,646,000	φ ¢	12,440,000			тв <u>р</u> \$	_	N/A	N/A
Westchester Stormwater BMP	э \$	32,722,000	\$	32,722,000			\$		N/A	N/A
Westminster Dog Park Stormwater BMP	\$	1,438,755	Š	1,438,755			\$		N/A	N/A
	Ť	.,	Ť	.,						Grant reimbursement of \$ 2,000,000 received; grant
	1		\$	0.004.500	\$		\$	2,000,000	Prop 50-SMBRP	completed
Wastaida Bark Painwatar Irrigation	¢	9 204 500							0.1.1	
Westside Park Rainwater Irrigation	\$	8,304,589	φ	6,904,589	\$	900,000			Quimby	Secured
Westside Park Rainwater Irrigation	\$		φ	6,904,589	\$ \$	900,000 292,038			Quimby Prop K	Secured Secured
Westside Park Rainwater Irrigation		8,304,589 TOTALS 544,092,553		510,699,775	\$		\$			



2.0 SCHEDULE

2.1 Project Schedules

The following table summarizes the schedule status for projects in the Program Schedule Update and are grouped by project phase.

Description	Sch	edule Sta	atus
Description	Ahead	On	Behind
Projects in Pre-Design			
Penmar Water Quality Improvement Phase II		\checkmark	
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 3 Phase II		\checkmark	
Temescal Canyon Park Stormwater BMP Phase II		\checkmark	
Land Acquisition Projects			
Taylor Yard River Park-Parcel G2 Land Acquisition*		NACTIV	E
Projects in Design			
Glenoaks/Sunland Stormwater Capture		\checkmark	
Strathern Wetlands Park		\checkmark	
Westchester Stormwater BMP		NACTIV	E
Projects in Bid & Award			
Elmer Avenue Phase II: Elmer Paseo		\checkmark	T
Machado Lake Ecosystem Rehabilitation		\checkmark	
Machado Lake Phase I (Wilmington Drain)		\checkmark	
Projects in Construction	I		
Albion Dairy Park – Demolition & Remediation		~	
Catch Basin Opening Screen Covers Phase III*		√*	
Echo Park Lake Rehabilitation		\checkmark	
Penmar Water Quality Improvement Phase I		\checkmark	
Rosecrans Recreation Center Stormwater Enhancements*		√*	1
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 3		\checkmark	-
Temescal Canyon Park Stormwater BMP Phase I		\checkmark	_
Projects in Post Construction			
Hansen Dam Wetlands Restoration			
Mar Vista Recreation Center Stormwater BMP			
Peck Park Canyon Enhancement			
South Los Angeles Wetlands Park			
Projects Completed			
Albion Dairy Park – Land Acquisition*			
Catch Basin Inserts and Coverings Phase I			
Catch Basin Opening Screen Covers Phase II			
Cesar Chavez Ground Water Improvement* (a.k.a. Sheldon Arleta)			
Grand Blvd. Tree Wells			
Imperial Highway Sunken Median Stormwater BMP			
Inner Cabrillo Beach Bacterial Water Quality Improvement*			
Los Angeles Zoo Parking Lot			
Oros Green Street			
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 1			
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 2			
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 4			
Strathern Pit Multiuse – Land Acquisition*			
Westminster Dog Park Stormwater BMP			
Westside Park Rainwater Irrigation			
*Schedule not controlled by Prop O			

Proposition O Program Master Schedule September 2012 Half 2, 2011 Half 1, 2012 Half 2, 2012 Half 1, 2013 Half 2, 2013 Half 1, 2014 Half 2, 2014 Half 1, 2015 J J A S OND J F M A M J J A S ON D J F M A M J J A S ON D J F M A M J J A S ON D J F M A M J J CD PROJECT TITLE Catch Basin Opening Screen Covers Ph III, Const Ends 1/1/2017 VR 11 Santa Monica Bay Low Flow Diversion Upgrades 4* Peck Park Canyon Enhancement Project 15 South Los Angeles Wetlands Park 9 10 Westside Park Rainwater Irrigation Project Penmar Water Quality Improvement Phase I* 11 Santa Monica Bay Low Flow Diversion Upgrades 3* 11 LA Zoo Parking Lot 4 Hansen Dam Wetlands Restoration 7 Echo Park Lake Rehabilitation 13 1 Albion Dairy-Demolition & Remediation 11 **Temescal Canyon Stormwater BMP Phase I*** 15 **Rosecrans Recreation Center Stormwater Enhancements** Machado Lake Phase I (a.k.a. Wilmington Drain) Const Ends 4/6/16 15 Machado Lake Ecosystem - Water Quality, Const Ends 4/6/16 15 6 Elmer Av-Phase II 11 Santa Monica Bay LFD Upgrades Package 3 - Ph 2 **Glenoaks/Sunland Storm Water Capture** 2,6 6 Strathern Wetlands Park Project (LA County) Const Ends 7/30/19 Temescal Canyon Park Stormwater BMP Phase II 11 Penmar Water Quality Improvement Ph II 11 Westchester Stormwater BMP* 11 1 Taylor Yard River Park - Parcel G2 Land Acquisition **Project Inactive** R/W & Approval Progress Bid & Award Status Date: Sun 9/30/12 Project by Others(Schedule not controlled by Prop O Project Award / Construction Date Submitted: Tue 10/9/12 Pre Design Post Construction Design *TMDL Project 14



3.0 PROP O PROGRAM BUDGET

3.1 Budget vs. Actual Expenditure


Project		Prop O Budget	Prop O Appropriation	Prop O Expenditures for September	Prop O Total Expenditures
Albion Dairy Park Demolition &					
Remediation	Land Acquisition	\$0		\$0	\$0
Funding Category 3	Pre-Design/Design	\$485,313		\$0	\$423,705
	Construction Cost	\$3,140,000		\$0 \$0	\$2,133,404
	Construction Management	\$331,087		\$4,999	\$331,123
	Sub-total	\$3,956,400	\$4,056,400	\$4,999	\$2,888,232
Albion Dairy Park Land Acquisition	Land Acquisition	\$17,560,000		\$0	\$17,468,154
Funding Category 2	Pre-Design/Design	\$0		\$0	\$47,604
	Construction Cost	\$0		\$0	\$0
	Construction Management Sub-total	\$0	\$17,515,758	\$0 \$0	\$0 \$17,515,758
Ostak Dasin Incente and Coursinns		÷ · · ;- · · ;- · · ·	••••••••••		÷··;-·-;-
Catch Basin Inserts and Coverings Ph I	Land Acquisition	0.0		01	¢0
		\$0		\$0 \$0	\$0
Funding Category 1	Pre-Design/Design Cost Construction Cost	\$0		\$0 ©	\$0
		\$14,607,953 \$04,022		\$0 \$0	\$14,607,953
	Construction Management Sub-total	\$94,933 \$14,702,886	\$14,607,953	\$0	\$0 \$14,607,953
0.4.4. D ' 0		• • • • • • • • • • • • • • • • • • •	•••••••••••••••	••	• • • • • • • • • • • • • • • • • • •
Catch Basin Opening Screen Covers Ph II	Land Acquisition	0.0		01	¢0
Funding Category 1	Pre-Design/Design Cost	\$0		\$0 \$0	\$0
runuing category r	Construction Cost	\$0 \$9,246,965		\$0 \$0	\$0 \$9,246,965
	Construction Management	\$9,246,965 \$115,439		\$0 \$0	\$9,246,963
	Sub-total	\$9,362,404	\$9,246,965	\$0	\$9,246,965
Catch Basin Opening Screen Covers					
Ph III	Land Acquisition	\$0		\$0	\$0
Funding Category 1 & 4	Pre-Design/Design	\$250,000		\$0	\$0
	Construction Cost	\$42,025,000		\$0	\$37,983,482
	Construction Management	\$2,225,000		\$0	\$69,687
	Sub-total	\$44,500,000	\$41,258,368	\$0	\$38,053,169
Cesar Chavez Ground Water	Land Acquisition	¢040		* 0	\$ 0
Improvement	Pre-Design/Design Cost	\$212		\$0 \$0	\$0
Funding Category 2	Construction Cost	\$663,238		\$0 \$0	\$0
	Construction Cost	\$1,805,050 \$571,500		\$0 \$0	\$1,815,625 \$0
	Sub-total	\$3,040,000	\$1,815,625	\$0	\$1,815,625
Echo Park Lake Rehabilitation	Land Acquisition	\$0		\$0	\$0
Funding Category 1, 2, 3, & 4	Pre-Design/Design	\$10,997,899		\$0	\$6,228,082
	Construction Cost	\$64,693,522		\$1,909,874	\$15,257,762
	Construction Management	\$8,571,892		\$0	\$644,052
	Sub-total	\$84,263,313	\$59,413,140	\$1,909,874	\$22,129,896
Elmor Avenue Phone III Elmon Para	Land Acquisition	*^		* ~	•••
Elmer Avenue Phase II: Elmer Paseo Funding Category 3		\$0		\$0 \$0	\$0
r unully calegory s	Pre-Design/Design Construction Cost	\$206,000 \$510,100		\$0 \$0	\$95,430
	Construction Management	\$510,100 \$112,900		\$0 \$0	\$0 \$0
	Sub-total	\$829,000	\$829,000	\$0	\$95,430
Glenoak/Sunland Stormwater Capture					
Funding Cotogory 2	Land Acquisition	\$0		\$0	\$0
Funding Category 3	Pre-Design/Design	\$106,436		\$0	\$0
	Construction Cost Construction Management	\$340,000		\$0 \$0	\$0 \$0
	-	\$62,260		\$0	\$0
	Sub-total	\$508,696	\$508,696	\$0	\$0

			Prop O	Prop O	Prop O Total
Project		Prop O Budget	Appropriation	Expenditures for September	Expenditures
Grand Blvd. Tree Wells	Land Acquisition	\$0		\$0	\$0
Funding Category 1	Pre-Design/Design Cost	\$270,308		\$0	\$196,02
	Construction Cost	\$382,444		\$0	\$382,44
	Construction Management	\$127,530		\$0	\$0
	Sub-total	\$780,282	\$578,465	\$0	\$578,465
Hansen Dam Wetland Restoration	Land Acquisition	\$0		\$0	\$0
Funding Category 3	Pre-Design/Design	\$395,835		\$0	\$C
	Construction Cost	\$1,583,400		\$6,700	\$1,304,130
	Construction Management	\$241,467		\$5,294	\$73,800
	Sub-total	\$2,220,702	\$1,923,702	\$11,994	\$1,377,930
Imperial Hwy Sunken Median		•			
Stormwater BMP	Land Acquisition	\$0		\$0	\$0
Funding Category 1	Pre-Design/Design	\$334,200		\$0	\$315,288
	Construction Cost Construction Management	\$2,217,703 \$171,500		\$0 \$0	\$764,536 \$12,724
	Sub-total	\$2,723,403	\$1,251,144	\$0	\$1,092,548
Innen Cabrille Desel, Destarial Water		<i> </i>	••,=••,•••		¢ 1,002,0 K
Inner Cabrillo Beach Bacterial Water Quality Improvement	Land Acquisition	N/A		N/A	N//
Funding Category 1	Pre-Design/Design	\$347,826		\$0	\$0
	Construction Cost	\$6,956,522		\$0	\$6,906,550
	Construction Management	\$695,652		\$0	\$0
	Sub-total	\$8,000,000	\$6,906,550	\$0	\$6,906,550
La Cienega/Fairfax Stormwater BMP					
(Canceled)	Land Acquisition	\$0		\$0	\$C
Funding Category 1	Pre-Design/Design	\$668,159		\$0	\$621,752
	Construction Cost	\$0		\$0	\$0
	Construction Management	\$0		\$0	\$0
	Sub-total	\$668,159	\$621,752	\$0	\$621,752
LA Zoo Parking Lot	Land Acquisition	\$0		\$0	\$C
Funding Category 1 & 3	Pre-Design/Design	\$1,743,743		\$0	\$861,586
	Construction Cost	\$11,129,500		\$0	\$4,479,213
	Construction Management	\$1,031,000		\$0	\$351,238
	Sub-total	\$13,904,243	\$6,129,609	\$0	\$5,692,037
Machado Lake - Phase I (Wilmington	Land Acquisition	A 0		0 0	
Drain) Funding Category 1 & 3	Land Acquisition Pre-Design/Design	\$0		\$0	\$0
Funding Category 1 & 3	Construction Cost	\$3,250,959 \$15,751,285		\$11,683 \$0	\$3,344,422 \$0
	Construction Management	\$2,047,667		\$0 \$0	\$C \$C
	Sub-total	\$21,049,911	\$21,049,911	\$11,683	\$3,344,422
Machado Lake Ecosystem					
Rehabilitation	Land Acquisition	\$0		\$0	\$C
Funding Category 1 & 3	Pre-Design/Design	\$12,989,683		\$3,427	\$7,657,629
	Construction Cost	\$76,409,901		\$0	\$C
	Construction Management	\$10,124,313		\$0	\$0
	Sub-total	\$99,523,897	\$95,249,121	\$3,427	\$7,657,629
Mar Vista Recreation Center		.		.	
Stormwater BMP Funding Category 1	Land Acquisition Pre-Design/Design	\$0 \$752.655		\$0 ©	\$C
Funding Category	Construction Cost	\$753,655		\$0 \$0	\$734,160
	Construction Management	\$3,425,704 \$376,827		\$0 \$6,616	\$2,405,822 \$293,195
	Sub-total	\$4,556,186	\$4,467,642	\$6,616	\$3,433,177
Oros Green Street	Land Acquisition	\$0	-	\$0	\$0
Funding Category 4	Pre-Design/Design	\$0 \$0		\$0 \$0	\$C \$C
	Construction Cost	ەن \$197,600		\$0 \$0	ېر \$197,600
	Construction Management	\$0		\$0	\$137,000 \$0

Proposition O - Clean	Nater Bond		Monthly P	rogress Report - Sep	tember 2012
Project		Prop O Budget	Prop O Appropriation	Prop O Expenditures for September	Prop O Total Expenditures
Peck Park Canyon Enhancement	Land Acquisition	\$0		\$0	\$
Funding Category 3	Pre-Design/Design	\$477,551		\$0	\$1,059,98
	Construction Cost	\$5,475,338		\$0	\$2,698,12
	Construction Management	\$237,111		\$0	\$497,86
	Sub-total	\$6,190,000	\$6,190,000	\$0	\$4,255,97
Penmar Water Quality Improvement					
Phase I	Land Acquisition	\$0		\$0	\$
Funding Category 2 & 4	Pre-Design/Design Construction Cost	\$2,395,140		\$14,903	\$1,892,17
	Construction Management	\$16,808,000 \$1,551,660		\$607,455 \$0	\$8,883,58 \$394,38
	-		¢20.754.900		
	Sub-total	\$20,754,800	\$20,754,800	\$622,358	\$11,170,15
Penmar Water Quality Improvement Phase II	Land Acquisition	\$0		\$0	\$1
Finase ii Funding Category 4	Pre-Design/Design	\$0 \$326,600		\$0 \$0	ۍ ډا
anding category 4	Construction Cost	\$328,800		\$0 \$0	5' \$(
	Construction Management	\$211,600		\$0	\$
	Sub-total	\$2,830,200	\$2,630,200	\$0	\$
Rosecrans Recreation Center					
Stormwater Enhancements	Land Acquisition	\$0		\$0	\$
Funding Category 3 & 4	Pre-Design/Design	\$767,095		\$0	\$8,39
	Construction Cost	\$3,722,692		\$0	\$1,385,66
	Construction Management	\$339,332		\$0	\$
	Sub-total	\$4,829,119	\$4,829,119	\$0	\$1,394,06
Santa Monica Bay Low Flow Diversion	Land Acquisition	*		\$ 2	
Upgrades P 1		\$0		\$0	\$
Funding Category 1	Pre-Design/Design Construction Cost	\$1,097,819 \$4,949,401		\$0 \$0	\$577,52 \$3,632,08
	Construction Management	\$767,157		\$0 \$0	\$471,42
	Sub-total	\$6,814,377	\$6,562,066	\$0	\$4,681,02
Santa Monica Bay Low Flow Diversion	1				
Upgrades P 2	Land Acquisition	\$0		\$0	\$
Funding Category 1	Pre-Design/Design	\$544,547		\$0	\$396,20
	Construction Cost	\$2,455,034		\$0	\$1,175,37
	Construction Management	\$380,530		\$0	\$186,46
	Sub-total	\$3,380,111	\$2,257,710	\$0	\$1,758,03
Santa Monica Bay Low Flow Diversion					
Upgrades P 3	Land Acquisition	\$2,000,000		\$0	\$440,68
Funding Category 1	Pre-Design/Design	\$3,324,213		\$0	\$1,738,58
	Construction Cost Construction Management	\$13,255,258 \$2,054,565		\$0 \$30,951	\$7,388,39 \$731,23
	Sub-total	\$20,634,036	\$12,780,718	\$30,951	\$10,298,89
Santa Monica Bay Low Flow Diversion					
Upgrades P 4	Land Acquisition	\$0		\$0	\$
Funding Category 1	Pre-Design/Design	\$1,013,421		\$0	\$574,05
	Construction Cost	\$4,568,903		\$0	\$2,457,04
	Construction Management Sub-total	\$708,180 \$6,290,504	\$5,003,055	\$0 \$0	\$363,82 \$ 3,394,92
•	Sub-total	ψ0,230,304	<i>\$</i> 3,003,033	\$U	¢J,JJ+,JZ
South Los Angeles Wetlands Park (includes Site Readiness)	Land Acquisition	\$2,011,937		\$0	\$1
Funding Category 3	Pre-Design/Design Cost	\$1,638,000		\$0 \$0	\$3,012,26
	Construction Cost	\$11,722,602		\$0	\$3,476,44
		\$1,305,663		\$0	\$861,89
	Construction Management	\$1,303,003		ψ0	\$001,05

Proposition O - Clean				Progress Report - Sep Prop O	
Project		Prop O Budget	Prop O Appropriation	Expenditures for September	Prop O Total Expenditures
Strathern Pit Multiuse -Land					
Acquisition	Land Acquisition	\$10,000,000		\$0	\$0
Funding Category 2	Pre-Design/Design	\$0		\$0	\$C
	Construction Cost	\$0		\$0	\$0
	Construction Management	\$0		\$0	\$0
	Sub-total	\$10,000,000	\$10,000,000	\$0	\$0
Strathern Wetlands Park Funding Category 2	Land Acquisition Pre-Design/Design	\$0 \$0		\$0 \$0	\$0 \$0
	Construction Cost	\$7,800,000		\$0 \$0	\$0
	Construction Management	\$0		\$0 \$0	\$0
	Sub-total	\$7,800,000	\$7,800,000	\$0	\$0
Taylor Yard River Park - Parcel G2 Land	Land Acquisition	\$12,440,000		\$0	\$0
Acquisition	Pre-Design/Design	\$0		\$0	\$0
Funding Category 3 & 4	Construction Cost	\$0		\$0	\$0
	Construction Management	\$0		\$0	\$0
	Sub-total	\$12,440,000	\$0	\$0	\$0
Temescal Canyon Park Stormwater	Land Acquisition	\$0		\$0	\$0
BMP Phase I	Pre-Design/Design	\$1,725,352		\$0	\$2,344,151
Funding Category 3 & 4	Construction Cost Construction Management	\$12,104,809 \$1,117,274		\$0 \$0	\$2,977,195 \$382,745
	Sub-total		\$14,974,353	\$0	\$5,704,091
Temescal Canyon Park Stormwater					
BMP Phase II	Land Acquisition	\$0		\$0	\$0
Funding Category 3 & 4	Pre-Design/Design	\$426,918		\$0	\$0
	Construction Cost	\$2,995,191		\$0	\$0
	Construction Management	\$276,456		\$0	\$0
	Sub-total	.,,,	\$3,671,647	\$0	\$0
Westchester Stormwater BMP	Land Acquisition	\$0		\$0	\$0
Funding Category 1, 2, & 4	Pre-Design/Design Construction Cost	\$3,776,050		\$0 \$0	\$2,168,614
	Construction Management	\$26,500,000 \$2,445,950		\$0 \$0	\$0 \$0
	Sub-total	\$32,722,000	\$4,200,200	\$0	\$2,168,614
Westminster Dog Park Stormwater					
ВМР	Land Acquisition	\$0		\$0	\$C
Funding Category 4	Pre-Design/Design	\$169,577		\$0	\$224,005
	Construction Cost	\$1,159,000		\$0	\$254,960
	Construction Management	\$110,178		\$0	\$46,346
	Sub-total		\$558,649	\$0	\$525,311
Westside Park Rainwater Irrigation	Land Acquisition	\$0		\$0	\$0
Project Funding Category 1	Pre-Design/Design Construction Cost	\$747,945 \$5,756,644		\$0 \$0	\$785,172
r ununing outegory r	Construction Management	\$400,000		\$0	\$2,987,320 \$241,080
	Sub-total	\$6,904,589	\$4,302,563	\$0	\$4,013,572
PROJECTS SUBTOTAL		\$510,699,775	\$410,817,263	\$2,601,902	\$193,970,397
Consultant Cost – Program Related Bu	ıdget				
Program Development Full Proposal Development		\$599,684 \$360,000	\$599,684 \$360,000	\$0 \$0	\$599,864 \$360,000
City Staff - Program Related Budget*		+0,000	+-00,000	ţ.	2000,000
Office of Accounting		\$895,696	\$670,265	\$0	\$430,978
Bureau of Engineering		\$695,696 \$4,057,743	\$070,205 \$10,441,634	\$0 \$0	\$6,636,626
Bureau of Contract Administratior		φ + ,007,7 + 0 **	\$3,988,428	\$0 \$0	\$1,346,807
Bureau of Sanitation		\$5,344,625	\$7,431,598	\$0 \$0	\$5,779,227
Indirect Cost		\$3,629,458	\$7,000,123	\$0	\$4,573,624
Arbitrage Fund 16F (1st Bond Sale)		\$7,340	\$7,340	\$0	\$7,340
PROGRAM TOTAL		\$525,594,321	\$441,316,335	\$2,601,902	\$213,704,863
		\$J∠J,394,3Z1	φ++1,310,333	\$2,001,902	φ 213,704,00 .

*Appropriations and expenditures represent Program and Project related City Staff Cost "No Program related Budget



4.1 Project Status Report

A brief status report for each project is provided on the following pages. The report identifies key project information, the planned scope of work, progress date, updated construction costs and percentage complete for all Proposition O projects.

The Percentage Complete at the far right hand column of the diagram uses a color-coding system to designate the current phase of each project.

Turquoise	Pre-Design
Yellow	Right of Way Acquisition/ Land Acquisition
Red	Design
Violet	Bid and Award
Green	Construction
Blue	Post Construction

Progress for each project is tracked by a color-coded pie chart. The color-coding system shows work completed in the darker shade of each color and the lighter shade denotes work to be completed. For example, if a project is in design the pie chart begins as light red. As progress is made, a darker red will indicate the approximate percentage of design work completed to date.

Proposition O - Clean Water Bond Program

PROJECT STATUS REPORT

PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION	COST	PERCENT COMPLETE
Albion Dairy Park - Demolition & Remediation	CD 1 - Ed P. Reyes	Demolition of the buildings and	Project team is preparing the	Notice to Proceed: Contract Duration:	7/8/2011 350 days	
1739 N. Albion Street	Designer: Malcolm Pirnie	improvements of an industrial	scope of work for the additional	City Engineer's Est.		
+ 11		facility, remediation and	soil remediation.	(Class A): Contract Award	\$2,468,100	
I	Contractor: National Demolition	abatement of all hazardous materials and soils onsite, and		Amount: Contract Award +	\$1,269,555	
	Proj. Mgr.: Iftekhar Ahmed	the importation of clean soil to leave the property in a level,		Contingency (20%) CO's to date	\$1,523,466	
	Contact #: 213-485-5875	graded condition.		(9, 86%): Award Amount +	\$1,087,296	
2000				CO's Issued	\$2,356,851	70%
	Photo of Project Site	Funding: Prop O		Master Sch. Constr. Completion Date:	Pre JUL 2012 Design	Land Design Bid & Const Post Cons Acquire Award
Albion Dairy Park - Land						
Acquisition		Acquire a parcel of land adjacent	The Purchase and Sale	Prop O Acquisition		
1739 N. Albion Street	CD 1 - Ed P. Reyes	to the LA River as part of LA	Agreement was executed on	Cost:	\$17,474,154	
1739 N. Albion Street	Designer: N/A	River Revitalization Master Plan.	10/2/09. Escrow closed on	Orig. Const. Contr.:	N/A	
T	Contractor: N/A	\sim	10/23/09. Park land acquisition	CO's to date:	N/A	
And in case of the second s	Proj. Mgr.: Kendrick Okuda	() ()				
	Contact #: 213-485-1165			Rev. Constr. Contr.:	N/A	
				Payment to date:	\$17,474,154	100%
Tiles				Master Sch. Constr.	Pre Design	Land Design Bid & Const Post Const Acquire Award
Oskrita Dassa Wallausu/Dila	Photo of Project Site	Funding: Prop O		Completion Date:	N/A	
Cabrito Paseo Walkway/Bike Path				Est. Prop O Constr.		
	CD 6 - Tony Cárdenas	Implement stormwater best management practices	Project is on hold due to funding issues. The Los Angeles	Cost:	\$1,007,558	
btwn Marson St. and Raymer St.	Designer: TBD	including: installation of	Neighborhood Land Trust	Orig. Const. Contr.:	N/A	$\langle \cdot \rangle$
	Contractor: TBD	bioswales, trash capture	(LANLT) is unable to secure	CO's to date:	N/A	
	Proj. Mgr.: Iftekhar Ahmed	devices, tree wells to aid in filtration, and a "\$MART"	additional \$3 million in funds			
	Contact #: 213-485-5875	irrigation system.	ANET requested to withdraw	Rev. Constr. Contr.:	N/A	
	Contact #. 213-403-3073		their request for project funding.			
* * * * * * * *		Funding: Prop-Q, Kaiser	ツ	Payment to date: Master Sch. Constr.	N/A Pre	Land Design Bid & Const Post Cons
$\rightarrow \rightarrow \rightarrow \rightarrow \rightarrow \rightarrow \rightarrow$	Proposed Project Site Plan	Foundation, & LANLT		Completion Date:	Design N/A	Acquire Award
Catch Basin Inserts and						
Covers Phase I		Install 8,000 inserts and 6,000	This project is complete.	Prop O Constr.		
Citywide	CD: All	screens in the high trash	- F1	Cost:	\$14,900,000	
	Designer: Bureau of Sanitation	generation areas, in the City, to achieve 20% trash reduction in				
	Contractor: Various	the Ballona Creek and Los				
A Charles	Proj. Mgr.: Alfredo Magallanes	Angeles River Watersheds.				
A PAR	Contact #: 213-485-3958					
			$\Box \subseteq [\Box U]$	Payment to date:	\$14,202,869	Land Design Bid & Const Post Const
	Photo of Catch Basin Insert	Funding: Prop O & Prop 40		Construction Completion Date:	SEP 2007	Acquire Design Bid & Const Post Const Award
				Completion Date.	JEF 2007	



PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION O	COST	PERCENT COMPLETE
Catch Basin Opening Screen Covers Phase II Citywide	CD: All Designer: Bureau of Sanitation Contractor: Various Proj. Mgr.: Alfredo Magallanes Contact #: 213-485-3958 Photo of Catch Basin Screen Cover	Install approximately 6,400 screens in medium trash generation areas, in the City, to increase trash reduction from 20% (accomplished in Phase 1) to 30%)trash reduction in Ballona Creek and LA River D Watersheds.	This project is complete.	Prop O Constr. Cost: Payment to date: Construction Completion Date:	\$9,400,000 \$9,246,965 OCT 2007	Land Acquire Bid & Const Award Award Award Award
Catch Basin Opening Screen Covers Phase III Citywide	CD: All Designer: Bureau of Sanitation Contractor: TBD Proj. Mgr.: Alfredo Magallanes Contact #: 213-485-3958	Retrofit of approximately 24,219 catch basins with opening screen covers and 2,600 inserts. Includes City-owned catch basins not covered in Phases I & II, as well as all State and County catch basins within the City.	A new procurement and installation services contract will install 2,600 catch basin inserts throughout the City to comply with trash TMDL.	Notice to Proceed: Contract Duration: City Engineer's Est. (Class A): Contract Award Amount: Contract Award + Contingency (10%) CO's to date (#, %): Award Amount + CO's Issued	\$42,025,000 \$42,025,000 \$0 \$0 \$0	49%
	Photo of Catch Basin Screen Cover	Funding: Prop O		Master Sch. Constr. Completion Date:	DEC 2016	Land Design Bid & Const Post Const Acquire Award
Cesar Chavez Ground Water Improvement 12455 Wicks Street	CD 6 - Tony CárdenasDesigner:Kleinfelder/GeosyntecContractor:Environmental ConstructionProj. Mgr.:Fang ChangContact #:213-978-1896Photo of Project Site	Retrofit existing gas collection system, install new flare & restore capacity in adjacent Tujunga Spreading Grounds through renovation of closed collection system Funding: Prop O WH, CWMB Grant, UDA Grant, & CIEP	The board report to the Board of Public Works (BPW) to accept the construction contract is being prepared.	Prop O Constr. Cost: Orig. Const. Contr.: CO's to date: Rev. Constr. Contr.: Payment to date: Construction Completion Date:	\$1,805,050 \$7,471,676 \$727,278 \$8,198,954 \$7,131,597 Pre Design OCT 2009	Land Design Bid & Const Post Const Acquire Award
Echo Park Lake Rehabilitation 751 Echo Park Avenue	CD 13 - Eric Garcetti Designer: Black & Veatch	In-lake improvements, in-lake vegetation (wetlands) and habitat improvements, and parkland structural best	Installation of the bentonite liner in the the lake bottom is complete north of the berm. The soil in the lake bottom in the	Notice to Proceed: Contract Duration: City Engineer's Est. (Class A):	7/11/2011 600 Days \$49,580,000	
	Contractor: Ford E.C. Proj. Mgr.: Julie Allen Contact #: 213-485-1454 Photo of Existing Lake	Funding: Prop O & Prop K	south cell is being prepared to receive the bentonite and the remaining vinyl sheet piles for the wetlands are being installed.	Contract Award Amount: Contract Award + Contingency (10%) CO's to date (26, 3%): Award Amount + CO's Issued Master Sch. Constr. Completion Date:	\$24,485,000 \$26,933,500 \$642,949 \$25,127,949 MAR 2013 Pre Design	74%


Proposition O - Clean Water Bond Program

PROJECT STATUS REPORT

PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION C	OST	PERCENT C	OMPLET	E
Elmer Avenue Phase II:								
Elmer Paseo	CD 6 - Tony Cárdenas	Convert a paved 20' x 270' alley	Project is in the bid and award	Est. Prop O Constr.	¢000.000			
7702 North Elmer Avenue		into a pocket park with water	phase. Seven (7) bids received	Cost:	\$829,000			
		quality improvements, including a pervious pedestrian pathway	on 8/15/2012. The bids received are being evaluated.	Orig. Const. Contr.: CO's to date:	N/A			
	Contractor: TBD	and a vegetated swale.	are being evaluated.		N/A			
and A manufactor	Proj. Mgr.: Iftekhar Ahmed Contact #: 213-485-5875	Sedimentation removal devices will also be installed.		Rev. Constr. Contr.:	N1/A			
	Contact #: 213-485-5875			Payment to date:	N/A		40%	
The states				Master Sch. Constr.	\$0 Pre	Land Design Bi	d & Const	Post Const
	Photo of Existing Paseo	Funding: Prop O		Completion Date:	JUL 2013	Acquire A	vard	
Glenoaks-Sunland								
Stormwater Capture		This project will install infiltration	This project is in the design	Est. Prop O Constr.				
Intersection of Sunland & Glenoaks	CD 6 - Tony Cárdenas	wells and other storm water Best	phase.	Cost:	\$475,000			
	Designer: Bureau of Sanitation	Management Practices (BMPs)		Orig. Const. Contr.:	N/A			
THE REAL PROPERTY OF THE REAL PROPERTY OF THE		n to help alleviate flooding at the subject intersection during storm		CO's to date:	N/A			
	Proj. Mgr.: Iftekhar Ahmed	events.						
A state of the	Contact #: 213-485-5875			Rev. Constr. Contr.:	N/A			
and the second second	Dhote of Flooding at Subject			Payment to date:	\$0 Pre	57% Land Design Bi	d & Const	Post Const
Sale Contraction	Photo of Flooding at Subject Intersection	Funding: Prop O		Master Sch. Constr. Completion Date:	NOV 2013		vard	
Grand Blvd. Tree Wells				Notice to Proceed:	7/7/2008			•
	CD 11 - Bill Rosendahl	Install seven stormwater	This project is complete.	Contract Duration:	100 days			
Intersection Grand & Riviera	Designer: PSOMAS	bioretention filters in a high-		City Engineer's Est. (Class A):	\$428,900			
Rhens's Right		density residential and commercial corridor in the		Contract Award	\$426,900			
Environ line prices	Contractor: Andrew Papac & Sons	Venice area to treat runoff from		Amount: Contract Award +	\$401,797			
				Contingency				
	Proj. Mgr.: Andy Flores			(24.8%) CO's to date	\$501,797			
Sten Wate follow ('First Rust')	Contact #: 213-485-4496			(5, -15%): Award Amount +	-\$19,353			
Contribution				CO's Issued	\$382,444			100%
ReadwayParting Lat				Construction	Pre Design		d & Const vard	Post Const
	Conceptual Drawing of Tree Well	Funding: Prop O & Prop 50		Completion Date:	DEC 2009			
Hansen Dam Wetlands		Ctormulator runs#fram these	Drojaat completed. Cite is now	Notice to Proceed:	2/3/2011			
Restoration Osborne Street @ Foothill Blvd.	CD 7 - Richard Alarcón	Stormwater runoff from three existing parking lots will be sent	Project completed. Site is now open for public use.	Contract Duration: City Engineer's Est.	240 days			
	Designer: MRCA	through newly constructed		(Class A):	\$1,159,000			
A The MAN	Contractor: Lee Construction	sediment forebays for removal of trash & sediments prior to		Contract Award Amount:	\$955,257			
		wetlands discharge.		Contract Award + Contingency (10%)				
Parking Area Management	Proj. Mgr.: Iftekhar Ahmed			CO's to date	\$1,050,257			
Upper- Person	Contact #: 213-485-5875			(32, 41%): Award Amount +	\$394,150			
Area				CO's Issued	\$1,334,496			98%
		Funding: Prop O & Caltrans-		Master Sch. Constr.	Pre Design		d & Const vard	Post Const
	Proposed Project Layout	FTIP		Completion Date:	FEB 2012			

Proposition O - Clean Water Bond Program

PROJECT STATUS REPORT

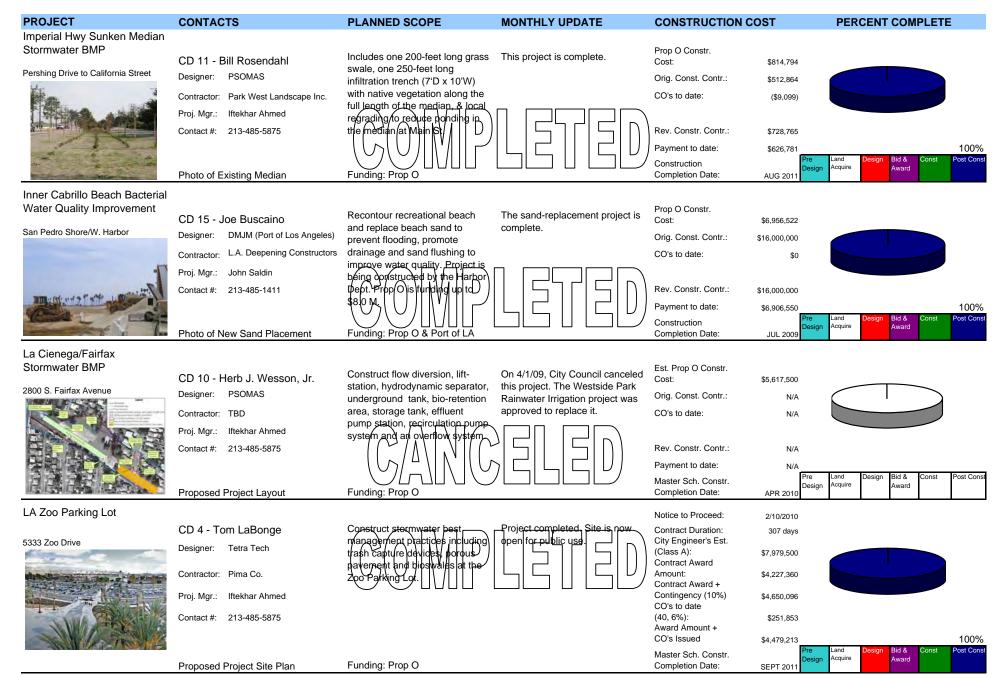



PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION	COST	PERCENT COMPLETE
Machado Lake-Phase I						
(Wilmington Drain)	CD 15 - Joe Buscaino	Install trash netting systems,	Project in bid & award phase.	Est. Prop O Constr. Cost:	\$15,751,285	
PCH & Vermont Avenue	Designer: CDM Smith	install smart irrigation in landscaped areas, use biofilters		Orig. Const. Contr.:	0,701,200 N/A	
	Contractor: TBD	or similar vegetated BMPs, and		CO's to date:	N/A	
	Proj. Mgr.: Iftekhar Ahmed	recontour and align the channel.				
The second second	Contact #: 213-485-5875			Rev. Constr. Contr.:	N/A	
				Payment to date:	N/A	
	Photo of Existing Conditions	Funding: Prop O & Prop 50		Master Sch. Constr. Completion Date:	APR 2016	Pre Land Design Bid & Const Post Cons Design Acquire Award
Vachado Lake Ecosystem	-					· · · · · · · · ·
Rehabilitation		In-lake rehabilitation techniques,	Project in bid & award phase.	Est. Prop O Constr.		
PCH & Vermont Avenue	CD 15 - Joe Buscaino _ Designer: CDM Smith	riparian system enhancements,	r toject in bid & award phase.	Cost:	\$76,409,901	
State No.		and treatment best management practices.		Orig. Const. Contr.: CO's to date:	N/A	
UN	Contractor: TBD Proj. Mgr.: Julie Allen			COS lo dale.	N/A	
and the second s	Contact #: 213-485-1454			Rev. Constr. Contr.:	N/A	
				Payment to date:	N/A	
CHARLES				Master Sch. Constr.		Pre Land Design Bid & Const Post Const Design Acquire Award
Carlos Ca	Photo of Existing Lake	Funding: Prop O & Prop K		Completion Date:	APR 2016	
Mar Vista Recreation Center Stormwater BMP				Notice to Proceed:	5/4/2009	
	CD 11 - Bill Rosendahl	-	Project continues in the post construction phase. Bureau of	Contract Duration: City Engineer's Est.	365 days	
1430 W. Woodbine	Designer: PSOMAS	underground detention tank,	h tank, Sanitation and the Bureau of al effluent Engineering continue implement optimization of the system.	(Class A):	\$2,979,900	
the proder and	Contractor: LA Engineering Inc.	chlorination facility, final effluent pump station, recirculation pump,		Contract Award Amount:	\$2,340,120	
- AND	Proj. Mgr.: Andy Flores	and overflow piping at Mar Vista		Contract Award + Contingency (19%)	\$2,790,120	
		Park.		CO's to date		
	Contact #: 213-485-4496			(18, 3%): Award Amount +	\$65,702	
Contra 1		Funding: Prop O, Prop 50 &		CO's Issued	\$2,405,822	99% Pre Land Design Bid & Const Post Const
	Proposed Project Site Plan	ARRA		Master Sch. Constr. Completion Date:	NOV 2010	Design Acquire Award
Oros Green Street						
	CD 13 - Eric Garcetti	Construct five curb side	This project is complete.	Prop O Constr.	#000.000	
between Blake Avenue & LA River	Designer: North East Trees (NET)	"stormwater gardens" in street		Cost: Orig. Const. Contr.:	\$300,000 N/A	
	Contractor: Street Services	parkway and a large infiltration gallery beneath Steelhead Park.		CO's to date:	N/A \$0	
N-TE TO A THE P				Rev. Constr. Contr.:		
	Proj. Mgr.: Dean Harding Contact #: 213-473-4242			Payment to date:	\$300,000 \$0	
	Oonaol #. ∠15-4/5-4242			Construction		
	Photo of New Sidewalk & Stormwater	Funding: Prop OL Prop 13 &		Completion Date: Construction	AUG 2007	Pre Land Design Bid & Const Post Const
-	Gardens			Completion Date:	MAY 2010	Design Acquire Award



Peck Park Canyon Enhancement		PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION (2051	PERCENT COMPLETE
Enhancement				Notice to Proceed:	5/3/2010	
	CD 15 - Joe Buscaino	Install vegetated bio-swales,	Conducting Mitigation Measures	Contract Duration:	593 days	
560 N. Western Avenue	Designer: Tetra Tech	infiltration strips, stormwater catch basins, armoring and re-	establishment and Best Management Practices (BMP)	City Engineer's Est. (Class A):	\$4,000,641	
	Contractor: C.S. Legacy Construction, Inc	vegetation for bank stabilization, and a step pool channel in Peck Park.	optimization.	Contract Award Amount: Contract Award +	\$3,636,946	
	Proj. Mgr.: John Saldin			Contingency (10%) CO's to date	\$4,000,640	
	Contact #: 213-485-1411			(32, 8%): Award Amount +	\$301,760	
				CO's Issued	\$3,938,706	99% Pre Land Design Bid & Const Post Const
	Proposed Project Layout	Funding: Prop O, Prop 50 & Rec and Trails Grant		Master Sch. Constr. Completion Date:	MAY 2011	Design Acquire Award
Penmar Water Quality				Notice to Proceed:	12/12/2010	
Improvement Phase I	CD 11 - Bill Rosendahl	Capture & treat dry/wet weather	Project construction phase	Contract Duration:	600 days	
1216 E. Rose Ave	Designer: Brown & Caldwell	diverted to sanitary sewer for a treatment. Wet weather runoff to el	continues. Ongoing construction activities include completion of	City Engineer's Est. (Class A):	\$13,878,500	
	Contractor: Pacific Hydrotech		electrical and mechanical systems; landscaping; baseball	Contract Award Amount: Contract Award +	\$11,360,700	
	Proj. Mgr.: Andy Flores	storage tank for discharge to sanitary sewer.	field restoration, systems testing and commissioning to follow.	Contingency (10%)	\$12,500,700	
	Contact #: 213-485-4496	Sumary Sewer.	and commissioning to follow.	CO's to date (36, 3%): Award Amount +	\$301,933	
				CO's Issued	\$11,662,633	
				Master Sch. Constr.		Pre Land Design Bid & Const Post Const Design Acquire Award
	Proposed Project Layout	Funding: Prop O		Completion Date:	JAN 2013	
Penmar Water Quality						
Improvement Phase II		Install a water treatment system	This project is in the pre-design	Est. Prop O Constr.		
1216 E. Rose Ave	CD 11 - Bill Rosendahl	for the purpose of reusing	phase.	Cost:	\$2,292,000	
1216 E. ROSE AVE	Designer: AECOM	collected stormwater.		Orig. Const. Contr.:	N/A	
	Contractor: TBD			CO's to date:	N/A	
International Control of Control	Proj. Mgr.: Katie Doherty					
	Contact #: 213-847-0395			Rev. Constr. Contr.:	N/A	
				Payment to date:	N/A	78%
				Master Sch. Constr.		Pre Land Design Bid & Const Post Const Design Acquire Award
	Proposed Project Layout	Funding: Prop O		Completion Date:	MAR 2015	
Rosecrans Rec. Center				Notice to Proceed:	1/17/2011	
Stormwater Enhancements	CD 15 - Joe Buscaino	Install "SMART" irrigation system,	Project is in the construction	Contract Duration:	640 days	
15000 S. Vermont Avenue	Designer: Withers & Sandgren	bioswales, vegetated retention basins, infiltration basins,	phase.	City Engineer's Est. (Class A):	\$3,500,000	
	Contractor: Horizon Construction Intl.	synthetic soccer field, decomposed granite pathway,		Contract Award Amount:	\$3,195,540	
Terrate Monteniar Monteniar Monteniar Monteniar	Proj. Mgr.: Ray Araujo	and landscaping.		Contract Award + Contingency (10%)	\$3,515,094	
				CO's to date (4, 2%):	\$32,151	
	Contact #: 213-473-9717				4 - 7 -	
	Contact #: 213-473-9717			Award Amount +		
	Contact #: 213-473-9717				\$3,237,940	



PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION COS	T PERCENT COMPLETE
Santa Monica Bay Low Flow				Notice to Proceed:	7/6/2009
Diversion Upgrades Pkg 1	CD 11 - Bill Rosendahl	Upgrade Marquez, Bay Club,	Project is complete.		366 days
PCH Several Locations	Designer: PSOMAS	Thornton, Venice Pavilion, and Imperial Low Flow Diversion			,949,401
Concerned to a local of	Contractor: LA Engineering, Inc.	systems to divert both summer		Contract Award Amount: \$3	0,024,545
	Proj. Mgr.: Andy Flores	and winter dry-weather flows, in order to comply with the bacteria		Contract Award + Contingency (10%) \$3	328,998
	Contact #: 213-485-4496	TMDL wihter dry-weather		CO's to date	\$190,854
	00ma0r#. 210400 4400			Award Amount +	,215,399 100%
		Funding: Prop O, Prop 50 &		Master Sch. Constr.	Pre Land Design Bid & Const Post Const Design Acquire Award
	Photo of Marquez Ave. LFD	ARRA		Completion Date:	JUL 2010
Santa Monica Bay Low Flow					/27/2009
Diversion Upgrades Pkg 2 At Temescal Canyon Park	CD 11 - Bill Rosendahl	Upgrade the existing Temescal Canyon Low Flow Diversion	Project continues in the post construction phase. Bureau of	Contract Duration: City Engineer's Est.	
At remescal carlyon raik	Designer: PSOMAS	System to comply with the	-Sanitation and the Bureau of		,807,900
	Contractor: LA Engineering, Inc.	bacteria/TMDA winter dry	Engineering continue implement		,207,440
and the second	Proj. Mgr.: Andy Flores			Contract Award + Contingency (9.9%) \$1	227.440
				CO's to date	,327,440
	Contact #: 213-485-4496			(11, 3%): Award Amount +	\$42,074
					,249,514 100% Pre Land Design Bid & Const Post Const
	Proposed Improvements at Temescal Cyn LFD	Funding: Prop O & ARRA		Master Sch. Constr. Completion Date: C	Design Acquire Award Award
Santa Monica Bay Low Flow				Notice to Proceed: 10	/20/2010
Diversion Upgrades Pkg 3	CD 11 - Bill Rosendahl	Construct a relief sewer (CIRS)	The installation of the northern	Contract Duration:	660 days
Along PCH	Designer: PSOMAS	to the Coastal Interceptor Sewer in order to comply with the	sewer reach along PCH and in Will Rogers Parking Lot 1 has	City Engineer's Est. (Class A): \$13	,255,258
	Contractor: Blois Construction	bacteria TMDL winter dry-	been completed. Restoration of	Contract Award Amount: \$8	3,468,451
		weather regulations.	Will Rogers Parking Lots 1 and 2 is being completed.	Contract Award +	
	Proj. Mgr.: Andy Flores			CO's to date	,740,902
	Contact #: 213-485-4496			(25, 9%): Award Amount +	\$755,819
SHE -					,224,270 99% Pre Land Design Bid & Const Post Const
	Photo of Relief Sewer Location	Funding: Prop O & SCM		Master Sch. Constr. Completion Date: C	Pre Land Design Bid & Const Post Const Design Acquire Award INCT 2012
Santa Manina Roy Low Flow					
Santa Monica Bay Low Flow Diversion Upgrades Pkg 4	CD 11 - Bill Rosendahl	This project will upgrade the	The project is complete.		/23/2009
Will Rogers Beach Parking Lot	Designer: PSOMAS	existing Low Flow Diversion	me project is complete.	City Engineer's Est.	65 DAYS
LASS	Designer. FSOWAS	System at Santa Monica Canyon and Palisades Park Low Flow		(Class A): \$3 Contract Award	9,798,800
	Contractor: Griffith Company	Diversion System. Upgrades		Amount: \$2 Contract Award +	2,279,000
	Proj. Mgr.: Andy Flores	include pump and electrical upgrades and automatic control	- - - - - - - - -	Contingency (10%) \$2	2,507,000
the Call	Contact #: 213-485-4496	from Venice Pump Plant.			\$178,640
and the second				Award Amount + CO's Issued \$2	457,640 100%
	I			Master Sch. Constr.	Pre Land Design Bid & Const Post Const Design Acquire Award
	Photo of Channel at Diversion Site	Funding: Prop O & Prop 50		Completion Date: A	PR 2011

Proposition O - Clean Water Bond Program

PROJECT STATUS REPORT

PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION CO	ST PI	ERCENT COMPLETE	
South Los Angeles Wetlands Park 54th St & Avalon Boulevard	CD 9 - Jan Perry Designer: PSOMAS Contractor: Ford E.C. Proj. Mgr.: John Saldin Contact #: 213-485-1411 Rendering of Proposed Project	Construct a wetlands park at 54th St. and Avalon Blvd to improve area stormwater quality, and provide recreational space for the surrounding community. Funding: Prop O, Prop K, Prop 12, Prop 50, Prop 40, CSSA(SEP), Brownfields Grant, & MTA	The Park area is complete. The Grand Opening was held on Feb. 9th. An investigation of alternatives to mitigate excess water loss is on-going. The preferred alternative is installation of a plastic liner.	Notice to Proceed: Contract Duration: City Engineer's Est. (Class A): Contract Award Amount: Contract Award + Contingency (10%) CO's to date (62, 12%): Award Amount + CO's Issued Master Sch. Constr. Completion Date:	4/9/2010 683 days \$10,354,300 \$6,370,000 \$7,297,000 \$740,126 \$7,029,379 Pre Dec 2011	a Land Design Bid & Const Acquire Design Award Acquire Const Award	16% Post Const
Strathern Pit Multiuse - Land Acquisition 8175 & 8216 Fair Avenue	CD 6 - Tony Cárdenas Designer: LA County Contractor: N/A Proj. Mgr.: Andy Flores Contact #: 213-485-4496 Proposed Project Site Plan	Acquire the land necessary to convert a 30-acre gravel pit site into a multipurpose facility dedicated to stormwater retention and reuse G G G G G G G G G G G G G G G G G G G	This project is complete.	Est. Prop O Acquisition Cost: s Orig. Const. Contr.: CO's to date: Rev. Constr. Contr.: Payment to date: Expected Acquisition Date:	\$10,000,000 N/A N/A N/A N/A TBD	100% e Land Design Bid & Const Acquire Design Award	Post Const
Strathern Wetlands Park 8175 & 8216 Fair Avenue	CD 6 - Tony Cárdenas Designer: LA County Contractor: N/A Proj. Mgr.: Andy Flores Contact #: 213-485-4496 Proposed Project Site Plan	The Strathern Pit Multiuse Project will convert a 30-acre landfill to a wetlands park facility to provide enhanced water quality, flood protection, habitat creation, groundwater recharge, recreational and water reuse. Funding: Prop O & LA County	Los Angeles County Public Works has acquired the land and the project continues in the design phase.	Est. Prop O Construction Cost: Orig. Const. Contr.: CO's to date: Rev. Constr. Contr.: Payment to date: Master Sch. Constr. Completion Date:	\$7,800,000 N/A N/A N/A N/A JUL 2019	65% Acquire Design Bid & Const Avard	Post Const
Taylor Yard River Park - Parcel G2 Land Acquisition 2850 Kerr Street	CD 1 - Ed P. Reyes Designer: N/A Contractor: N/A Proj. Mgr.: Kendrick Okuda Contact #: 213-485-1165 Photo of G2 Parcel & LA River	Acquire a parcel of land adjacent to the LA River as part of Revitalization Master Plan. \$25M in Prop O funds must be augmented. CD 1 leads purchase negotiations (coordination with Trust for Public Land). Funding: Prop O & TBD	Land acquisition is in negotiation.	Est. Prop O Acquisition Cost: S Orig. Const. Contr.: CO's to date: Rev. Constr. Contr.: Payment to date: Expected Acquisition Date:	\$12,440,000 N/A N/A N/A N/A TBD	e Land Design Bid & Const Acquire Acquire	Post Const

Proposition O - Clean Water Bond Program

PROJECT STATUS REPORT

PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION COST	PERCENT COMPLETE
Temescal Canyon Park				Notice to Proceed: 8/1	7/2011
Stormwater BMP Ph I	CD 11 - Bill Rosendahl	Divert stormwater from an	Preparation for the detention tank	Contract Duration: 61	6 days
15900 Pacific Coast Highway	Designer: AECOM	existing storm drain to Temescal Canyon Park for treatment by a	concrete work continues.Concrete is being	City Engineer's Est. (Class A): \$8,0 Contract Award	08,800
ANSIS AND	Contractor: LA Engineering, Inc.	hydrodynamic separator, underground detention tank and diversion to a sanitary sewer for	poured to form the lower walls and slabs. Contractor is working to backfill and compact the soil at		19,800
	Proj. Mgr.: Iftekhar Ahmed	treatment at treatment plant.	the diversion structure.	Contingency (10%) \$7,7 CO's to date	21,780
	Contact #: 213-485-5875			(6, 12%): \$8 Award Amount +	49,460
					69,260 70%
	Proposed Project Layout	Funding: Prop O		Master Sch. Constr. Completion Date: JU	Pre Land Design Bid & Const Post Const Design Acquire Acquire Award
Temescal Canyon Park					
Stormwater BMP Ph II	CD 11 - Bill Rosendahl	Phase II of the Temescal Canyon	This project is in the pre-design	Est. Prop O Constr. Cost: \$2,9	95,191
15900 Pacific Coast Highway	Designer: AECOM	Park Stormwater BMP Project proposes the construction of an	phase.	Orig. Const. Contr.:	N/A
C SALE SALE	Contractor: TBD	onsite stormwater treatment /		CO's to date:	N/A
	Proj. Mgr.: Katie Doherty	disinfection system. The treated stormwater is to be used for			
	Contact #: 213-847-0395	landscape irrigation.		Rev. Constr. Contr.:	N/A
				Payment to date:	N/A 78%
The standard states	Proposed Project Layout	Funding: Prop O		Master Sch. Constr. Completion Date: MAI	R 2015 Acquire Award
Westchester Stormwater					
BMP	CD 11 - Bill Rosendahl	Capture and treat stormwater	Bureau of Sanitation (BOS) staff	Est. Prop O Constr.	
Los Angeles World Airport	Designer: AECOM	runoff from three existing	continues to work with LAWA to	Cost: \$26,5 Orig. Const. Contr.:	00,000 N/A
	Contractor: TBD	stormdrains through the project BMP elements, including Trash	finalize the lease agreement of the project site.	CO's to date:	N/A
	Proj. Mgr.: Salem Garawi	Net System, Underground Detention Tank and Underground			
	Contact #: 213-847-0345	Infiltration Facility.		Rev. Constr. Contr.:	N/A
				Payment to date:	N/A
	Proposed Project Layout	Funding: Prop O		Master Sch. Constr. Completion Date: OC	Pre Land Bid & Const Post Cons Design Acquire Award
Westminster Dog Park	Tiposed Tiojeot Layout	r anding. r top o			1 2014
Stormwater BMP		The device of the fail of the state of the second state.	This contraction is some late	Prop O Constr.	
1203 South Main Street	CD 11 - Bill Rosendahl	Includes installation of a modular constructed wetland	This project is complete.		85,330
	Designer: PSOMAS	(bioremediation filter), so that on-			85,330
	Contractor: Fleming Environmental, Inc.	site runoff will be captured and treated prior to discharging into		CO's to date: (\$3	80,370)
	Proj. Mgr.: Salem Garawi Contact #: 213-847-0345	the storm drain system D		Rev. Constr. Contr.: \$2	54,960
			L C C V ,		54,585 100%
All services and a service service services and a service service services and a service service service service services and a service se				Master Sch. Constr.	Pre Land Design Bid & Const Post Const Design Acquire Award



PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION C	OST	PERCENT COMPLETE		
Westside Park Rainwater				Notice to Proceed:	6/3/2010)		
Irrigation	CD 10 - Herb J. Wesson, Jr.	Treat pollutants from on-site and	Project completed. Seventeen	Contract Duration:	270 days	3		
2785 Clyde Avenue	Designer: PSOMAS	off-site stormwater by installing a stormwater lift station, a subsurface irrigation system, and	(17) solar lights installed by Recreation & Parks.	City Engineer's Est. (Class A): Contract Award	\$2,766,900			
The state	Contractor: PPC Construction, Inc.	a dry creek with a perforated pipe		Amount: Contract Award +	\$2,675,963	3		
	Proj. Mgr.: Iftekhar Ahmed	for collecting and returning excess irrigation water to the		Contingency (10%) CO's to date	\$2,943,559			
	Contact #: 213-485-5875	existing stormdrain.		(37, 22%): Award Amount +	\$600,216	3		
and the second second				CO's Issued	\$3,276,179)		100%
	Photo of Completed Park	Funding: Prop O, Prop 50, Prop K, Quimby		Construction Completion Date:	AUG 2011	Pre Land Design Bid & Design Acquire Award	Const	Post Const




5.0 APPENDIX

5.1 Map of Proposition O Projects Approved for Implementation

See attached

5.2 Catch Basin Retrofits Screen Covers and Inserts by Council Districts

CATCH BASIN RETROFITS						
Council	Inserts			Screen Covers		
District	Phase I	Phase III		Phase I & II	Phase III	
	(COMPLETED)			(COMPLETED)		
	Installed	Planned	Installed	Installed	Planned	Installed*
1	1,174	200	0	960	960	960
2	0	10	0	505	1,436	1,436
3	0	10	0	1,230	1,790	1,790
4	580	500	0	890	1,454	1,454
5	98	20	0	1,186	2,673	2,673
6	0	0	0	380	1,162	1,162
7	0	0	0	960	1,306	1,306
8	1,370	50	0	1,526	1,611	1,611
9	1,300	500	0	1,936	1,040	1,040
10	809	100	0	1,200	1,716	1,716
11	71	10	0	399	2,581	2,581
12	0	20	0	985	2,294	2,294
13	570	320	0	790	941	941
14	1,480	220	0	1,125	1,642	1,642
15	168	40	0	228	1,581	1,581
TOTALS	7,620	2,000	0	14,300	24,219	24,219

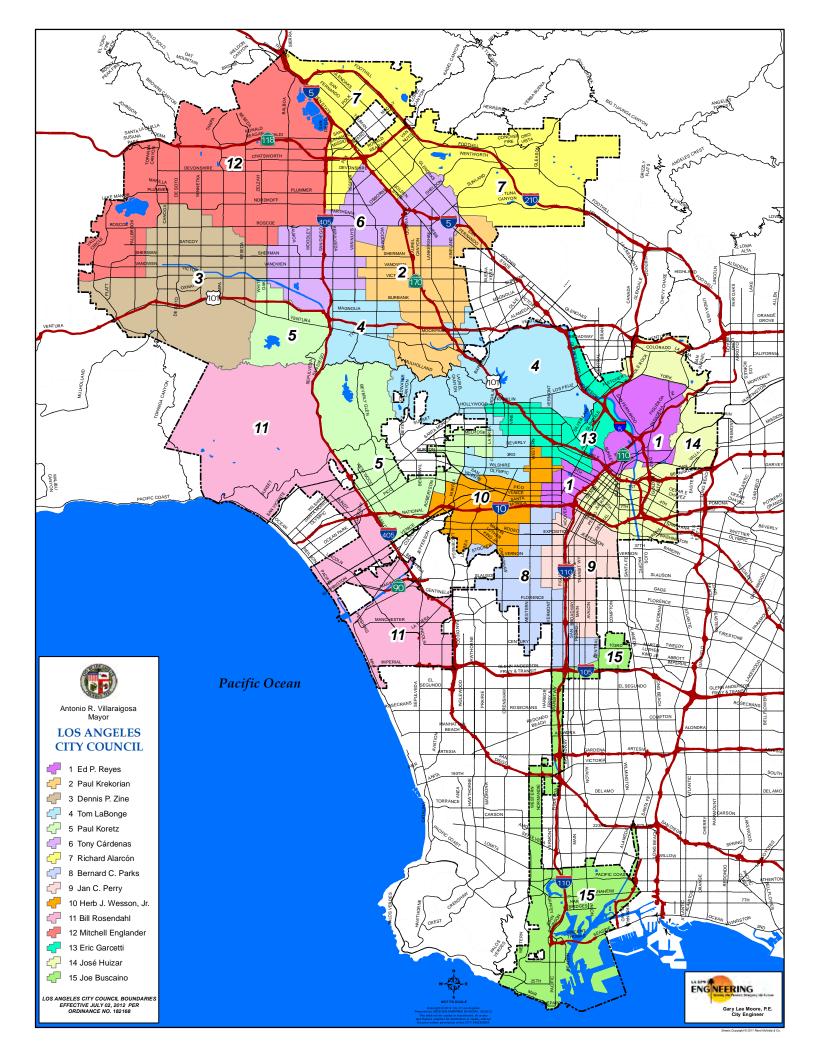

Proposition O Projects Approved for Implementation

