

# **Proposition O – Clean Water Bond Program**

# **June 2013 Monthly Report**



# ECHO PARK LAKE REHABILITATION PROJECT GRAND OPENING

#### **Administrative Oversight Committee**

Miguel Santana, City Administrative Officer, Chair Capri W. Maddox, Board of Public Works Gerry Miller, Chief Legislative Analyst Ronald Nichols, Department of Water and Power Romel Pascual, Office of the Mayor

#### **Citizens Oversight Advisory Committee**

Adi Liberman, Chair Francine Diamond Mark Gold Tiger Kang Miguel Luna Cynthia McClain-Hill Craig A. Perkins M. Teresa Villegas

PREPARED BY
BUREAU OF ENGINEERING
PROP O BOND DIVISION





#### **Distribution List**

Miguel Santana, City Administrative Officer Office of the City Administrative Officer (CAO)

Capri W. Maddox, President Board of Public Works

Gerry F. Miller, Chief Legislative Analyst
Ronald Nichols, General Manager

Office of the Chief Legislative Analyst (CLA)
Department of Water and Power (DWP)

Romaid Nichols, General Manager Department of Water and Power (Disposed Pascual, Deputy Mayor Mayor's Office

Adi Liberman, Chair Citizens Oversight Advisory Committee

Francine Diamond

Mark Gold

Tiger Kang

Miguel Luna

Cynthia McClain-Hill

Craig A Perkins

Citizens Oversight Advisory Committee

Craig A. Perkins

M. Teresa Villegas

Valerie Lynne Shaw, Vice President

Citizens Oversight Advisory Committee

Citizens Oversight Advisory Committee

Board of Public Works

Warren T. Furatani, Commissioner

Jerilyn Lopez Mendoza, Commissioner

Steven T. Nutter, Commissioner

Board of Public Works
Board of Public Works
Board of Public Works

Gary Lee Moore, City Engineer Bureau of Engineering (BOE)

John L. Reamer, Jr., Director Bureau of Contract Administration (BCA)

Nazario Sauceda, Director

Enrique C. Zaldivar, Director

Bureau of Street Services
Bureau of Sanitation (BOS)

Victoria Santiago, Director

Jon Kirk Mukri, General Manager

Board of Public Works, Office of Accounting
Department of Recreation & Parks (RAP)

Kenneth R. Redd, Deputy City Engineer BOE Adel H. Hagekhalil, Assistant Director BOS

Edward Jordan, Assistant City Attorney City Attorney's Office


David H. Hirano CAO
Rafael E. Prieto CLA
Charles E. Modica CLA

Michael E. Mullin Mayor's Office

David Pettijohn DWP
Shahram Kharaghani BOS
Kendrick K. Okuda BOE

Comments or suggestions regarding the Proposition O Monthly Report may be directed to Kendrick K. Okuda, BOE Proposition O Implementation Program Manager, at 213-485-1165 or email at Kendrick.Okuda@lacity.org

This report is available for viewing online at the Bureau of Engineering website: http://eng.lacity.org/projects/prop\_o/report2013.htm



# **TABLE OF CONTENTS**

<u>Sec</u>	tion				Page
1.0	Execu	utive Su	ımmar <u>y</u>		
	1.1			ary	4
		1.1.1		AOC, and Other Highlights	4
		1.1.2		les	5
		1.1.3		Community Meetings Schedule	6
	1.2	Bond	-	, , , , , , , , , , , , , , , , , , , ,	7
	1.3			Summary	8
		1.3.1		in Planning	8
		1.3.2		AOC Project Funding Recommendations	9
				COAC & AOC Project Recommendations	
		1.3.3		in Implementation	10
		1.3.4		and Program Budget Summary	11
			1.3.4.1	Project Budget Summary	11
			1.3.4.2	Program Budget Summary	12
			1.3.4.3	Project Funding Summary	
2.0	Sche	<u>dule</u>		,	
	2.1	Projec	t Schedul	es	14
	2.2			r Schedule	15
3.0	Budg	<u>et</u>			
	3.1	Budge	et vs. Actu	al Expenditure	16
4.0	<u>Proje</u>	ct Statu	<u>s</u>		
	4.1	Projec	t Status R	Report	20
5.0	Appe	ndix			
	5.1	Map c	f Proposit	ion O Projects Approved for Implementation	32
	5.2	Table	of Catch I	Basin Retrofits Screen Covers and Inserts by Council Districts	31
	5.3	Cound	cil District	Map	33

#### 1.0 EXECUTIVE SUMMARY

# 1.1 Program Summary

In November 2004, voters of the City of Los Angeles passed the Proposition O - Clean Water Bond, authorizing \$500 million of general obligation bonds for projects to protect public health by cleaning up pollution in the City's rivers, lakes, and beaches. The projects are intended to assist the City of Los Angeles in meeting Federal Clean Water Act requirements. Proposition O - Clean Water Bond will also fund improvements to protect water quality, provide flood protection, increase water conservation, provide habitat protection, and create open space.

This monthly progress report summarizes the status of activities and progress of the Proposition O - Clean Water Bond program, for June 2013.

# 1.1.1 <u>Citizens Oversight Advisory Committee (COAC), Administrative Oversight</u> Committee (AOC), and Other highlights

- The June 20, 2013 COAC meeting was canceled.
- On June 20, 2013 the AOC met for a Special Meeting and the committee heard several reports. The AOC heard an update on the vegetation removal at the Machado Lake Ecosystem Rehabilitation project site. The AOC approved the use of \$800,000 in Proposition O funding from the Machado Lake Ecosystem Rehabilitation project budget to initiate vegetation removal to help mosquito abatement at the project site. This will allow mosquito abatement to occur this summer and reduce vegetation removal scope during project construction. The AOC also heard presentations on the Broadway Neighborhood Stormwater Greenway and Avalon Green Alley South projects. West Nile virus has been detected in mosquitoes at project site. The AOC approved \$4,626,502 in Prop O appropriations to fund the Broadway Neighborhood Stormwater Greenway project and \$1,602,642 in Prop O appropriations for the Avalon Green Alley South project.
- The June 27, 2013 AOC meeting was canceled.

#### 1.1.2 Key Issues

#### Machado Lake Ecosystem Rehabilitation

- Issue 1: On February 27, 2013 three construction bids were received. The three bids were \$68.8 million, 82.6 million, and \$99 million. The City Engineers' estimate was \$60.3 million.
- Status: The Board rejected all bids on May 8, 2013.
- Action: The design team is implementing all recommended cost saving measures and project is expected to be re-advertised in July 2013.
- Issue 2: The Regional Water Quality Control Board has not issued the 401 Certification for the project, citing concerns with insufficient sand placement on top of the AquaBlok cap.
- Status: Application submitted in June 2012. We have met with the RWQCB staff on 4 occasions, latest meeting on 7/2 to provide rationale for current design and request issuance of the permit.
- o Action: Continue to request the RWQCB to issue the permit.
- o Issue 3: The United States Army Corps of Engineers has not issued the 404 Certification.
- Status: Application submitted in June 2012. Review process has been ongoing, but the USACE has mentioned that they are busy and have less staff time due to sequester.
- Action: Continue to talk to USACE staff to try to expedite permit processing.

#### Westchester Stormwater BMP Project

- o **Issue:** Land use agreement between the City (BOS) and Los Angeles World Airport (LAWA) has not been finalized.
- Status: Meeting with Mayor's Office, CLA, City Attorneys Office, BOS, LAWA, and BOE held to resolve this issue.
- Action: City Attorney, LAWA, and BOS are working to document and finalize resolution of land use issues.

# • Santa Monica Bay LFD Upgrades Package 3 Phase 2

- Issue: Protracted Caltrans Encroachment permit processing has resulted in the delay of project construction contract award.
- Status: The project was advertised on April 12, 2013 for bids to be received on May 29, 2013. A motion was approved by the Board of Public Works on May 22, 2013 to extend the bid due date to June 26, 2013 because Caltrans required additional permit processing time. Subsequently, a second motion was approved by the Board on June 12, 2013 to extend bid due date to August 7, 2013 because the permit had not been issued. It is anticipated that the Caltrans permit will not be issued in time to meet the extended bid due date of August 7, 2013.
- o **Action**: Options are being evaluated for resolution of this item.

# 1.1.3 **Project Community Meetings Schedule**

The following is a list of Proposition O project meetings with the public that occurred in June and are planned for the month of July.

## **COMMUNITY MEETINGS**

Date	Time	Project	Group	Location
6/5/13	10:00 AM	Santa Monica Bay Low Flow Diversion Upgrades Pkg. 3 Phase 2	PCH Taskforce	Malibu City Hall Multipurpose Room 23825 Stuart Ranch Road
		Temescal Canyon Park Stormwater BMP Phase 1		Malibu, CA 90265
6/15/13	10:00 AM	Echo Park Lake Rehabilitation Project	Community and Council District 13 Grand Opening	751 N. Echo Park Avenue Los Angeles, CA 90026
7/18/13	10:00 AM	Rory M. Shaw Wetlands Park	Sun Valley Watershed Stakeholders	Sun Valley Park and Recreation Center 8133 Vineland Avenue Los Angeles, CA 91352



# 1.2 Bond Sales

The following table is a summary of the bond sales that fund Proposition O.

PROPOSITION (	O BOND SALE SUM	MMARY	
General Obligation Bonds Approved by Voters			\$500,000,000
Total Bond Sales to Date  Fund 16F July 13, 2005 City Council Approved Bond Sale (Ord. 176839 CF 05-1408)		\$37,000,000	\$439,500,000
Fund 16M July 21, 2006 City Council Approved Bond Sale (Ord. 177733 CF 06-0600-S37)	\$3,074,734	\$8,000,000	
Fund 16Q July 22, 2008 City Council Approved Bond Sale (Ord. 180090 CF 08-1706)	\$883,653	\$101,000,000	
Fund 16T July 21, 2009 City Council Approved Bond Sale (Ord. 180808 CF 09-1674)	\$5,994,350	\$176,500,000	
Bond Interest Earnings (As of June 2013)	\$9,715,498		
Fund 16V July 28, 2011 City Council Approved Bond Sale (Ord. 181755 CF 11-0841)		\$117,000,000	
Bond Interest Earnings (As of June 2013)	\$ 2,802,857		
Total Bond Interest Earnings to Date	\$22,471,092		
General Obligation Bonds Remaining to be		\$60,500,000	



# 1.3 Project Status Summary

# 1.3.1 Projects In Planning (Pending AOC & COAC Approval)

The following table summarizes the projects that are being considered. The projects will be presented to the AOC & COAC for approval.

	PROJECTS												
Project Title	Applicant	Prop O Funding Request	Prop O Set Aside Funds Request	Funds From Other Sources (if applicable)	Total Project Funding Needed		ented to the COAC						
Albion Riverside Park Project	BOS/CD 1	\$11,455,000	\$0	\$10,497,000	\$21,952,000	3/13	TBD						
Avalon Green Alley South Project-LID Demonstration Project*	BOS	\$1,602,642	\$0	\$891,344	\$1,602,642	5/13	6/20						
Broadway Neighborhood Stormwater Greenway Project*	BOS	\$4,626,502	\$0	\$2,939,361	\$4,626,502	5/13	6/20						
Trash TMDL Implementation Phase IV Catch Basin Inserts and Opening Screen Covers	BOS	\$6,160,000	\$0	\$0	\$6,160,000	5/13	TBD						
Verdugo Hills**	BOS	\$33,460,603	\$0	\$746,213	\$34,206,816	TBD	TBD						
Vermont Avenue Stormwater Capture and Green Street Project*	BOS	\$1,000,000	\$0	\$3,980,000	\$4,980,000	5/13	TBD						
Westwood Neighborhood Greenway	BOS	\$3,162,958	\$0	\$0	\$3,162,958	TBD	TBD						
			7	OTALS		1							
		\$61,467,705	\$0	\$19,053,918	\$76,690,918								

<sup>\*</sup>Grant Funding has not been secured

<sup>\*\*</sup>Funding from other sources have not yet been identified

## 1.3.2 COAC & AOC Funding Recommendations (Pending Mayor Approval)

The following table summarizes the projects approved and recommended by COAC and AOC for funding. The projects will be presented to the City Council and Mayor for approval.

	PROJECTS RECOMMENDED FOR FUNDING BY COAC AND AOC												
		Prop O Funding	Prop O Set Aside Funds	Funds From Other Sources	Total Project Funding	_	O Funding mendations	Month/Year Recommended by					
Project Title	Applicant	Request	Request	(if applicable)	Needed	COAC	AOC	COAC & AOC					
N/A N/A \$0		\$0	\$0	\$0	\$0	\$0	N/A						
	TOTALS												
	\$0 \$0 \$0 \$0 \$0												

# 1.3.2.1 COAC & AOC Project Recommendations (Pending Funding Approval)

The following table summarizes the projects approved by COAC and AOC, without funding authority.

	PROJECTS RECOMMENDED BY COAC AND AOC												
Project Title	Applicant	Prop O Funding Request	Prop O Set Aside Funds Request	Funds From Other Sources (if applicable)	Total Project Funding Needed	Month/Year Recommended by COAC & AOC							
Aliso Creek & Limekiln Creek Restoration	Mountains Recreation and Conservation Authority	\$7,842,042	\$0	\$0	\$7,842,042	July 2007							
Boyle Heights Joint City of LA, Use Community Council District 14		\$2,291,000	\$0	\$528,000	\$2,819,000	July 2007							
	TOTALS												
	\$10,133,042 \$0 \$528,000 \$10,661,042												



## 1.3.3 Projects in Implementation (Approved by City Council & Mayor)

The following table lists the projects approved for Proposition O funding by the City Council and the Mayor.

PROJECTS IN IMPLEMENTATION    Current Council/Mover   Bron O Set Acids   Current Total   Betantial Funda From										
Project Title	Current Council/Mayor Approved Budget	Prop O Set Aside Approved	Current Total Project Budget	Potential Funds From Other Sources*						
Projects in Pre-Design										
Land Acquisition Projects										
Taylor Yard River Park – Parcel G2 Land Acquisition	\$0	\$12,440,000	TBD	TBD						
Projects in Design										
Penmar Water Quality Improvement Phase II	\$2,830,200	\$0	\$2,830,200	\$0						
Rory M. Shaw Wetlands Park	\$7,800,000	\$0	\$22,000,000	\$14,200,000						
Temescal Canyon Park Stormwater BMP Phase II	\$3,698,565	\$0	\$3,698,564	\$0						
Westchester Stormwater BMP	\$32,722,000	\$0	\$32,722,000	\$0						
Projects in Bid & Award										
Machado Lake Ecosystem Rehabilitation	\$99,523,897	\$0	\$99,523,897	\$1,076,997						
Projects in Construction										
Albion Dairy Park – Demolition & Remediation	\$3,956,400	\$0	\$3,956,400	\$3,577,476						
Catch Basin Opening Screen Covers Phase III	\$44,500,000	\$0	\$44,500,000	\$0						
Echo Park Lake Rehabilitation	\$69,263,313	\$0	\$69,263,313	\$599,875						
Elmer Avenue Phase II: Elmer Paseo	\$829,000	\$0	\$1,275,000	\$446,000						
Glenoaks/Sunland Stormwater Capture	\$508,696	\$0	\$508,696	\$0						
Machado Lake Phase I (Wilmington Drain)	\$21,049,911	\$0	\$21,049,911	\$4,397,500*						
Penmar Water Quality Improvement Phase I	\$20,754,800	\$0	\$20,754,800	\$0						
Rosecrans Recreation Center Stormwater Enhancements	\$4,829,119	\$0	\$6,754,033	\$1,924,914						
Temescal Canyon Park Stormwater BMP Phase I	\$14,947,435	\$0	\$14,947,435	\$0						
Projects in Post Construction										
Hansen Dam Wetlands Restoration	\$2,220,702	\$0	\$2,517,702	\$297,000						
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 3	\$20,634,036	\$0	\$20,634,036	\$7,000,000						
Projects Completed										
Albion Dairy Park – Land Acquisition	\$17,537,311	\$0	TBD	TBD						
Catch Basin Inserts and Coverings Phase I	\$14,702,886	\$0	\$14,702,886	\$600,000*						
Catch Basin Opening Screen Covers Phase II	\$9,630,788	\$0	\$9,630,788	\$0						
Cesar Chavez Ground vvater improvement (a.k.a Sheidon	\$2,527,873	\$0	\$9,841,230	\$6,801,230						
Grand Blvd. Tree Wells	\$713,039	\$0	\$780,282	\$350,000*						
Imperial Highway Sunken Median Stormwater BMP	\$1,301,724	\$0	\$2,723,403	\$0						
Inner Cabrillo Beach Bacterial Water Quality Improvement	\$6,921,409	\$0	\$16,000,000	\$8,000,000						
La Cienega/Fairfax Stormwater BMP (CANCELED)	\$668,569	\$0	\$668,569	\$0						
Los Angeles Zoo Parking Lot	\$6,240,455	\$0	\$13,904,243	\$0						
Mar Vista Recreation Center Stormwater BMP	\$4,556,186	\$0	\$4,556,186	\$2,077,838*						
Oros Green Street	\$198,924	\$0	\$784,251	\$586,651						
Peck Park Canyon Enhancement	\$6,190,000	\$0	\$7,896,193	\$1,706,193*						
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 1	\$6,814,377	\$0	\$6,814,377	\$5,131,497**						
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 2	\$3,380,111	\$0	\$3,380,111	**						
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 4	\$6,290,504	\$0	\$6,290,504	**						
South Los Angeles Wetlands Park (includes Site Readiness)	\$16,678,202	\$0	\$26,374,067	\$13,001,866*						
Strathern Pit Multiuse - Land Acquisition	\$10,000,000	\$0	\$28,000,000	\$18,000,000						
Westminster Dog Park Stormwater BMP	\$687,888	\$0	\$687,888	\$0						
Westside Park Rainwater Irrigation	\$6,904,589	\$0	\$8,304,589	\$3,192,038*						
	TOTALS									

<sup>\*</sup>Estimated grant funds/reimbursements that may be available. \*\*American Recovery and Reinvestment Act (ARRA) funding for Pkg. 2 is bundled with Pkg. 1. Prop 50-CBI funding for Pkg. 4 is bundled with Pkg. 1.

## 1.3.4 Project and Program Budget Summary

# 1.3.4.1 Total Project Budget Summary

The following table is a summary of the Proposition O project funding.

PROJECT BUDGET SUMMARY											
Description	Prop O Funding	Prop O Set Aside	Potential Funds From Other Sources*	Total Project Budget							
Projects In Planning– Prop O Funding Request	\$0	\$0	\$0	\$0							
Projects Recommended by AOC	\$0	\$0	\$0	\$0							
Projects In Implementation	\$472,012,909	\$12,440,000	\$78,767,075	\$528,275,554							
	TOTAL	_S									
	\$472,012,909	\$12,440,000	\$78,767,075	\$528,275,554							
Prop O Total Project Obligation	\$484,4	52,909									

<sup>\*</sup>Estimated grant funds/reimbursements that may be available

#### 1.3.4.2 Program Budget Summary

The table on the following pages gives an updated program budget summary for Proposition O.

## 1.3.4.3 Project Funding Summary

The table on the following pages gives an updated project funding summary for Proposition O.

June 2013 Monthly Report

	Council / Ma	yor Approved			Current
Draines Tisle		Approved	Future Needs	Cost Reductions	Council/Mayor
Project Title	Original Budget		Future Needs	Reductions	Approved Budget
Albion Dairy Park - Demolition & Remediation Albion Dairy Park - Land Acquisition - COMPLETED	\$ 6,956,400 \$ 17,560,000				\$ 6,956,400 \$ 14,560,000
Aliso Wash - Limekiln Creek Confluence Restoration	\$ -	1			\$ -
Boyle Heights Joint Use Community Center Improvements	\$ -				\$ -
Catch Basin Inserts and Coverings Phase I - COMPLETED	\$ 17,000,000			\$ (2,297,114)	\$ 14,702,886
Catch Basin Opening Screen Covers Phase II - COMPLETED	\$ 10,000,000			\$ (369,212)	\$ 9,630,788
Catch Basin Opening Screen Covers Phase III Cesar Chavez Ground Water Improvement - COMPLETED	\$ 44,500,000 \$ 3,040,000			\$ (512,127)	\$ 44,500,000 \$ 2,527,873
Echo Park Lake Rehabilitation	\$ 84,263,313			\$ (15,000,000)	\$ 69,263,313
Elmer Avenue Phase II: Elmer Paseo	\$ 829,000				\$ 829,000
Glenoaks/Sunland Stormwater Capture Grand Blvd. Tree Wells - COMPLETED	\$ 508,696			¢ (200,000)	\$ 508,696
Hansen Dam Wetlands Restoration	\$ 1,075,927 \$ 2,220,702			\$ (362,888)	\$ 713,039 \$ 2,220,702
Imperial Highway Sunken Median Stormwater BMP- COMPLETED	\$ 2,723,403			\$ (1,421,679)	\$ 1,301,724
Inner Cabrillo Beach Bacterial Water Quality Improvement	\$ 8,000,000				\$ 8,000,000
La Cienega/Fairfax Stormwater BMP - CANCELED	\$ 7,667,888			\$ (6,999,728)	\$ 668,159
Los Angeles Zoo Parking Lot - COMPLETED	\$ 13,904,243			\$ (7,663,788)	\$ 6,240,455
Machado Lake-Phase I (Wilmington Drain)  Machado Lake Ecosystem Rehabilitation	\$ 21,049,911 \$ 99,523,897		+	+	\$ 21,049,911 \$ 99,523,897
Mar Vista Recreation Center Stormwater BMP	\$ 4,556,186				\$ 99,523,897 \$ 4,556,186
Oros Green Street - COMPLETED	\$ 386,000			\$ (187,076)	\$ 198,924
Peck Park Canyon Enhancement	\$ 6,190,000				\$ 6,190,000
Penmar Water Quality Improvement Phase I	\$ 20,754,800 \$ 2,830,200		1		\$ 20,754,800
Penmar Water Quality Improvement Phase II Rory M. Shaw Wetlands Park	\$ 2,830,200 \$ 7,800,000				\$ 2,830,200 \$ 7,800,000
Rosecrans Recreation Center Stormwater Enhancements	\$ 4,829,119		<u> </u>		\$ 4,829,119
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 1	\$ 6,814,377				\$ 6,814,377
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 2	\$ 3,380,111				\$ 3,380,111
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 3	\$ 20,634,036				\$ 20,634,036
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 4 South Los Angeles Wetlands Park (includes Site Readiness)	\$ 6,290,504 \$ 16,678,202				\$ 6,290,504 \$ 16,678,202
Strathern Pit Multiuse - Land Acquisition	\$ 10,070,202				\$ 10,000,000
Taylor Yard River Park - Parcel G2 Land Acquisition	,	\$ 12,440,000			\$ 12,440,000
Temescal Canyon Park Stormwater Phase I	\$ 14,947,435				\$ 14,947,435
Temescal Canyon Park Stormwater Phase II	\$ 3,698,565				\$ 3,698,565
Westchester Stormwater BMP Westminster Dog Park Stormwater BMP - COMPLETED	\$ 32,722,000 \$ 1,438,755			\$ (750,867)	\$ 32,722,000 \$ 687,888
Westside Park Rainwater Irrigation	\$ 6,904,589			ψ (750,007)	\$ 6,904,589
Total - Project Budge			ls -	\$ (35,564,479)	\$ 485,553,779
City Staff - Program Related Budget (as of June 30, 2011 )	, , , , , ,	, .,		, (,, -,	
Office of Accounting	\$ 587,723		\$ 491,450		\$ 1,079,173
Bureau of Contract Administration  Bureau of Engineering	\$ 2,003,796		\$ 2,504,606		\$ 4,508,402
Bureau of Sanitation	\$ 2,003,796		\$ 2,586,746		\$ 6,668,585
Related Costs	\$ 2,333,524		\$ 1,746,497		\$ 4,080,021
Subtota			\$ 7,329,299		\$ 16,336,181
Consultants - Program Related Budget (as of as of June 30, 2011)	Ta -		1	T	
Program Development/Implementation Full Proposal Development	\$ 600,000 \$ 360,000			\$ (136)	\$ 599,864 \$ 360,000
Subtota				\$ (136)	
Total - Prop O Budge	•		\$ 7329299	\$ (35,564,615)	
	DING SOURCES	Ψ 12,440,000	Ψ 1,525,255	ψ (55,564,615)	Ψ 302,043,024
Funding Sources (as of September 30, 2011)	PINO GOURGES				
Bond Proceeds - First Sale	\$ 37,000,000				\$ 37,000,000
Bond Proceeds - First Sale Interest	\$ 3,042,656				\$ 3,042,656
Bond Proceeds - Second Sale	\$ 8,000,000		-		\$ 8,000,000
Bond Proceeds - Second Sale Interest Bond Proceeds - Third Sale	\$ 854,249 \$ 101,000,000				\$ 854,249 \$ 101,000,000
Bond Proceeds - Third Sale  Bond Proceeds - Third Sale Interest	\$ 5,142,889				\$ 5,142,889
Bond Proceeds - Fourth Sale	\$ 176,500,000				\$ 176,500,000
Bond Proceeds - Fourth Sale Interest	\$ 5,858,814				\$ 5,858,814
Bond Proceeds - Fifth Sale	\$ 117,000,000		1	-	\$ 117,000,000
Bond Proceeds - Fifth Sale Interest Bond Proceeds - Future Sales	\$ -		\$ 60,500,000		\$ 60,500,000
Bond Proceeds - Secured Grants Received	\$ 13,412,918		Ψ 00,000,000	1	\$ 13,412,918
Less Set-Aside for Future Arbitrage Payments	, , , , , , , , , , , , ,	\$ (100,000)	)		\$ (100,000
Sewer Construction and Maintenance (SCM)	<u> </u>		\$ 7,000,000.00	<u> </u>	\$ 7,000,000
Total - Funding Sources	s \$ 467,811,526	\$ (100,000)	\$ 67,500,000	\$ -	\$ 535,211,520
			Tota	al - Prop O Budget	\$ (502,849,824
	<u> </u>	PROP O PR	ROGRAM BUDGET	CONTINGENCY	\$ 32,361,701
Bond Proceeds - Secured Grants Anticipated	\$ 7,500,388				\$ 7,500,388

Project Fulluling Sullimary										
Project Title		Budget		riginal Prop O nding (with set asides)		er Direct unding		Potential hbursements	Source	Status
					\$		\$	500,000	Brownsfield	Secured
	1.				\$		\$		Demolition escrow account	Demolition escrow check received for \$3,000,000
Albion Dairy Park - Demolition & Remediation	\$	3,956,400	\$	3,956,400	\$	556,524	\$		Sprint Nextel and Swiss II lease payment	Lease payment of \$571,320 received
					\$	-	\$		City Clerk	Rental reimbursement of \$20,952 approved
Albion Dairy Park - Land Acquisition - COMPLETED	\$	_	\$	17,560,000	\$		\$		N/A	N/A
	+ -				-					Grant reimbursement of \$600,000 received; grant
Catch Basin Inserts and Coverings Phase I - COMPLETED	\$	14,702,886	\$	14,702,886	\$	-	\$	600,000	Prop 40	completed
Catch Basin Opening Screen Covers Phase II - COMPLETED	\$	9,362,404		9,362,404	\$		\$		N/A	N/A
Catch Basin Opening Screen Covers Phase III	\$	44,500,000	\$	44,500,000	\$		\$		N/A	N/A
					\$ :		\$		DWP CIWMB	Secured Secured
Cesar Chavez Ground Water Improvement	\$	9,841,230	\$	3,040,000	Φ	387,230			UDAG	Secured
				-	\$	414,000			CIEP	Secured
Echo Park Lake Rehabilitation	\$	84,263,313	\$	84,263,313	\$		\$		Prop K	Secured
Elmer Avenue Phase II: Elmer Paseo	\$	1,275,000		829,000	\$	446,000		-	Council for Watershed Health	Secured
Glenoaks/Sunland Stormwater Capture	\$	508,696		508,696	\$		\$	-	N/A	N/A
										Grant reimbursement of \$350,000 received; grant
Grand Blvd. Tree Wells - COMPLETED	\$	780,282		780,282	\$	-	\$		Prop 50-SMBRP	completed
Hansen Dam Wetlands Restoration	\$	2,517,702 2,723,403		2,220,702 2,723,403	\$	297,000	\$		Caltrans - FTIP N/A	Secured by MRCA for Design N/A
Imperial Highway Sunken Median Stormwater BMP Inner Cabrillo Beach Bacterial Water Quality Improvement	\$	16,000,000		8,000,000	\$	- 000,000,8	٠		Port of Los Angeles	N/A Secured
La Cienega Fairfax Stormwater BMP - CANCELED	\$	668,159	_	668,159	\$		\$		N/A	Project canceled
Los Angeles Zoo Parking Lot	\$	13,904,243		13,904,243	\$		\$		N/A	N/A
LOS Arigeres 200 Farking Lot	φ	13,904,243	φ	13,304,243	\$		\$		Prop 50-IRWMP	Secured
Machado Lake-Phase I (Wilmington Drain)	\$	21,049,911	\$	21,049,911	TBD		\$		LA County Flood Control District	Final Agreement Pending
madriade Zane i riade i (iriininington Brain)	1	21,049,911	ľ	21,010,011	\$	10,000	٠		Lawsuit Settlement	Secured
	1				\$				Prop K	Secured
Machado Lake Ecosystem Rehabilitation	\$	99,523,897	\$	99,523,897			Ψ		7 10 F K	0000.00
	Ť	,,	*	,,	\$	296,997			Coastal Conservancy	Grant reimbursement of \$296,997 paid; grant completed
	Ī						\$	1,777,838	American Recovery & Reinvestment Act	
Mar Vista Recreation Center Stormwater BMP	\$	4,556,186	œ	4,556,186	\$	_	Ą	1,777,030	(ARRA)	Grant reimbursement of \$1,777,838 received
Ivial Visia Necreation Center Stormwater Divi	Ψ	4,550,100	Ψ	4,550,100	Ψ	-	\$	300,000		Grant reimbursement of \$300,000 received; grant
							•		Prop 50-SMBRP	completed
Oros Green Street - COMPLETED	\$	784,251	\$	197,600	\$	586,651	\$		Prop 13 & CWA 319th	Secured
Peck Park Canyon Enhancement	\$	7,896,193	\$	6,190,000	\$		\$		Prop 50	\$1,586,193 in grant funding authorized for payment
Penmar Water Quality Improvement (Phase I & II)	•	23,585,000	\$	23,585,000	\$	120,000	\$		Rec & Trails Grant N/A	\$120,000 in grant funding paid; grant completed N/A
Rory M. Shaw Wetlands Park	\$	22,000,000		7,800,000	\$ 1	4,200,000	Ф		LA County Flood Control District	Secured
Noty W. Silaw Wellands Falk	+-				φ 1		\$		Prop K	Secured
Rosecrans Recreation Center Stormwater Enhancements	\$	6,754,033	\$	4,829,119	\$		\$		TBD	Prop O K to find funding or down scope project
									American Recovery & Reinvestment Act	Grant reimbursement of \$4,361,106 received; ARRA
					\$	-	\$	4,364,420	(ARRA)	funding for Pkg. 2 is bundled with Pkg. 1
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 1	\$	6,814,377	\$	6,814,377	•		•	707.077	,	Grant reimbursement of \$767,077 received; grant
				ŀ	\$	-	\$	767,077	Prop 50-CBI	completed
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 2	\$	3,380,111	\$	3,380,111	\$		\$		American Recovery & Reinvestment Act	
Santa Monica Bay Low Flow Diversion Opgrades, Pkg. 2	Ф		Ф		Ф				(ARRA)	ARRA funding for Pkg. 2 is bundled with Pkg. 1
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 3	\$	20,634,036	\$	20,634,036	\$	-	\$	7,000,000	SCM Fund	Secured
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 4	\$	6,290,504	\$	6,290,504	\$	-	\$		Prop 50-CBI	Prop 50-CBI funding for Pkg. 4 is bundled with Pkg. 1
					\$	-	\$	3,300,000	Prop 50-IRWMP	Grant reimbursement of \$2,895,750 received. \$3,300,000 authorized for payment
					•		¢	2.044.007	. Top ou nevin	Grant reimbursement of \$2,011,937 received; grant
	1		1		\$		\$	2,011,937	Prop 12 (RZH) - for Land Acquisition	completed
					\$	1,282,721			Prop 40 (RZH)	Grant funding of \$916,188 paid
					\$	3,739,707	\$		Collection System Settlement Agreement -	
South Los Angeles Wetlands Park (includes Site Readiness)	\$	26,374,067	\$	16,678,202					Supplemental Environmental Project	Funding of \$2,717,394 paid
255 2557 (Inguies Wellands Fair (Indudes Ofte Readilless)	<b>"</b>	20,017,001	ľ	10,010,202		, ,			Prop K - for Land Acquisition	Secured
					\$	500,000	\$		Prop K	Grant funding of \$500,000 paid, grant completed
	1		1		\$	-	\$	900,000	MTA - max potential reimbursement for	Deimburgement of \$942 FOF
					\$	67,501	\$		remediation MTA - lease payment	Reimbursement of \$813,525 received  Lease payment of \$67,501 received
							φ		min icase payment	Grant reimbursement of \$199,977 received & grant
	1		1		\$	-	\$	200,000	EPA - Brownfields grant	completed
Strathern Pit Multiuse - Land Acquisition	\$	28,000,000	\$	10,000,000	\$ 1	8,000,000	\$	_	LA County Flood Control District	Secured
Taylor Yard River Park - Parcel G2 Land Acquisition	TBD		\$	12,440,000	TBD	,	TBD		TBD	TBD
Temescal Canyon Park Stormwater BMP (Phase I & II)	\$	18,646,000	\$	18,646,000	\$	-	\$	-	N/A	N/A
Westchester Stormwater BMP	\$	32,722,000		32,722,000			\$		N/A	N/A
Westminster Dog Park Stormwater BMP	\$	1,438,755		1,438,755	\$		\$		N/A	N/A
					\$		\$	2,000,000		Grant reimbursement of \$ 2,000,000 received; grant
Westside Park Rainwater Irrigation	\$	8,304,589	\$	6,904,589					Prop 50-SMBRP	completed
Tools as Fair Nairwater Irrigation	Ψ .	0,007,003	ľ	0,004,009	\$	900,000			Quimby	Secured
	1		<u> </u>		\$	292,038		-	Prop K	Secured
						TOT				
	\$	543,757,628	\$	510,699,775	\$ 6	1,987,351	\$	31,479,724		



# 2.0 SCHEDULE


# 2.1 Project Schedules

The following table summarizes the schedule status for projects in the Program Schedule Update and are grouped by project phase.

Schedule Status								
Description	Ahead	On	Behind					
Projects in Pre-Design								
Land Acquisition Projects								
Taylor Yard River Park-Parcel G2 Land Acquisition*	I	NACTIVE	<u> </u>					
Projects in Design	<u> </u>							
Penmar Water Quality Improvement Phase II			✓					
Rory M. Shaw Wetlands Park*			✓					
Temescal Canyon Park Stormwater BMP Phase II			✓					
Westchester Stormwater BMP		NACTIVE						
Projects in Bid & Award								
Machado Lake Ecosystem Rehabilitation			<b>√</b>					
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 3 Phase II			<b>√</b>					
Projects in Construction	<u> </u>							
Albion Dairy Park – Demolition & Remediation			<b>√</b>					
Catch Basin Opening Screen Covers Phase III*		<b>√</b> *	<u> </u>					
Echo Park Lake Rehabilitation		•	<b>✓</b>					
Elmer Avenue Phase II: Elmer Paseo		<b>√</b>						
Glenoaks/Sunland Stormwater Capture	✓							
Machado Lake Phase I (Wilmington Drain)		✓						
Penmar Water Quality Improvement Phase I			✓					
Rosecrans Recreation Center Stormwater Enhancements*			<b>√</b> *					
Temescal Canyon Park Stormwater BMP Phase I			✓					
Projects in Post Construction								
Hansen Dam Wetlands Restoration								
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 3								
Projects Completed								
Albion Dairy Park – Land Acquisition*								
Catch Basin Inserts and Coverings Phase I								
Catch Basin Opening Screen Covers Phase II								
Cesar Chavez Ground Water Improvement* (a.k.a. Sheldon Arleta)								
Grand Blvd. Tree Wells								
Imperial Highway Sunken Median Stormwater BMP								
Inner Cabrillo Beach Bacterial Water Quality Improvement*								
Los Angeles Zoo Parking Lot								
Mar Vista Recreation Center Stormwater BMP								
Oros Green Street								
Peck Park Canyon Enhancement								
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 1								
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 2								
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 4								
South Los Angeles Wetlands Park								
Strathern Pit Multiuse – Land Acquisition*								
Westminster Dog Park Stormwater BMP								
Westside Park Rainwater Irrigation *Schoolule not controlled by Prop O								

<sup>\*</sup>Schedule not controlled by Prop O

# Proposition O Program Master Schedule June 2013

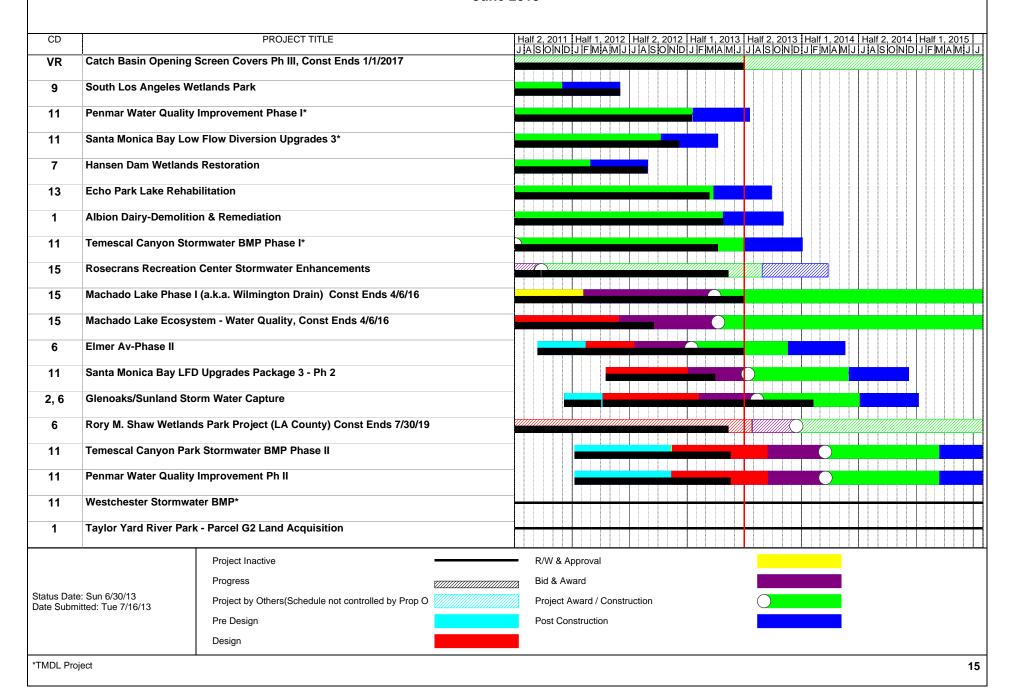



# 3.0 PROP O PROGRAM BUDGET

# 3.1 Budget vs. Actual Expenditure

Project		Original Prop O Budget	Current Prop O Budget	Prop O Total Expenditures <sup>1</sup>
Albion Dairy Park Demolition & Remediation	Land Acquisition Pre-Design/Design/	\$0	\$0	\$0
Funding Category 3	Construction Management Construction Cost	\$816,400 \$6,139,999	\$816,400 \$6,140,000	1,660,176 \$3,421,011
	Sub-total	·	\$6,956,400	\$5,081,187
Albion Dairy Park Land Acquisition	Land Acquisition Pre-Design/Design/	\$17,560,000	\$14,560,000	\$14,465,528
Funding Category 2	Construction Management Construction Cost	\$0 \$0	\$0 \$0	71,782 \$0
	Sub-total	·	\$14,560,000	\$14,537,311
Catch Basin Inserts and Coverings Ph I	Land Acquisition	\$0	\$0	\$0
Funding Category 1	Pre-Design/Design/ Construction Management Construction Cost	\$2,100,000	\$560,017 \$44,442,860	\$560,017
COUNCIL/MAYOR APPROVED CLOSE-OUT	Sub-tota	\$14,900,000 I \$17,000,000	\$14,142,869 \$14,702,886	\$14,142,869 <b>\$14,702,886</b>
Catab Basin Opening Serson Covers Bh II	Land Acquisition	<b>*</b> 0	go.	<b>\$0</b>
Catch Basin Opening Screen Covers Ph II Funding Category 1	Pre-Design/Design/ Construction Management	\$0 \$0	\$0 383,822	\$0 383,822.00
COUNCIL/MAYOR APPROVED CLOSE-OUT	Construction Cost  Sub-total	\$10,000,000 \$10,000,000	\$9,246,965 <b>9,630,788</b>	\$9,246,965 \$9,630,788
	Sub-total	\$10,000,000	9,630,766	\$9,030,766
Catch Basin Opening Screen Covers Ph III	Land Acquisition Pre-Design/Design/	\$0	\$0	\$0
Funding Category 1 & 4	Construction Management Construction Cost	\$2,475,000 \$42,024,999	\$2,475,000 \$42,025,000	4,406,192 \$38,067,224
	Sub-total	\$44,499,999	\$44,500,000	\$42,473,417
Cesar Chavez Ground Water Improvement	Land Acquisition Pre-Design/Design/	\$0	\$0	\$0
Funding Category 2	Construction Management Construction Cost	\$1,234,950 \$1,805,050	712,248 \$1,815,625	712,248 \$1,815,625
COUNCIL/MAYOR APPROVED CLOSE-OUT	Sub-total		\$2,527,873	\$2,527,873
Echo Park Lake Rehabilitation	Land Acquisition	\$0	\$0	\$0
Funding Category 1, 2, 3, & 4	Pre-Design/Design/ Construction Management Construction Cost	\$19,569,791 \$64,693,522	\$19,569,791 \$49,693,522	9,689,838 \$23,750,981
	Sub-total		\$69,263,313	\$33,440,819
Elmer Avenue Phase II: Elmer Paseo	Land Acquisition	\$0	\$0	\$0
Funding Category 3	Pre-Design/Design/ Construction Management	\$318,900	\$318,900	198,549
	Construction Cost Sub-total	\$510,100 \$829,000	\$510,100 \$829,000	\$185,891 \$384,441
Glenoak/Sunland Stormwater Capture	Land Acquisition	60	***	<b>6</b> 0
Funding Catagory 2	Pre-Design/Design/	\$0 \$168,696	\$0 \$168,696	\$0 9,047
Funding Category 3	Construction Management Construction Cost	\$340,000	\$340,000	\$0
	Sub-total	\$508,696	\$508,696	\$9,047



Project		Original Prop O Budget	Current Prop O Budget	Prop O Total <sup>1</sup> Expenditures
Grand Blvd. Tree Wells	Land Acquisition	\$0	\$0	\$0
Funding Category 1	Pre-Design/Design/ Construction Management Construction Cost	\$248,927 \$827,000	330,595 \$382,444	330,595 \$382,444
COUNCIL/MAYOR APPROVED CLOSE-OUT	Sub-total		\$713,039	\$713,039
Hansen Dam Wetland Restoration	Land Acquisition	\$0	\$0	\$0
Funding Category 3	Pre-Design/Design/ Construction Management	\$637,302	\$637,302	446,911
	Construction Cost	\$1,583,400	\$1,583,400	\$1,345,488
	Sub-total	\$2,220,702	\$2,220,702	\$1,792,400
Imperial Hwy Sunken Median Stormwater BMP	Land Acquisition	<b>*</b> 0	¢o.	o.c
DINIF	Pre-Design/Design/	\$0	\$0	\$0
Funding Category 1	Construction Management Construction Cost	\$505,700 \$3,347,703	537,188	537,188
COUNCIL/MAYOR APPROVED CLOSE-OUT	Sub-total	\$2,217,703 \$2,723,403	\$764,536 \$1,301,724	\$764,536 \$1,301,724
Inner Cabrillo Beach Bacterial Water Quality				
Improvement	Land Acquisition	N/A	N/A	N/A
Funding Category 1	Pre-Design/Design/ Construction Management	\$1,043,478	\$1,043,478	14,859
,	Construction Cost	\$6,956,522	\$6,956,522	\$6,906,550
COUNCIL/MAYOR APPROVED CLOSE-OUT	Sub-tota	\$8,000,000	\$8,000,000	\$6,921,409
La Cienega/Fairfax Stormwater BMP				
(Canceled)	Land Acquisition Pre-Design/Design/	\$0	\$0	\$0
Funding Category 1	Construction Management Construction Cost	\$2,050,388 \$5,617,500	\$668,159 \$0	\$668,569 \$0
CANCELED	Sub-total		\$668,159	\$668,569
LA Zoo Parking Lot	Land Acquisition	\$0	\$0	\$0
_	Pre-Design/Design/		·	
Funding Category 1 & 3	Construction Management Construction Cost	\$2,774,743 \$11,129,500	1,726,283 \$4,514,172	1,726,283 \$4,514,172
COUNCIL/MAYOR APPROVED CLOSE-OUT	Sub-total		\$6,240,455	\$6,240,455
Machado Lake - Phase I (Wilmington Drain)	Land Acquisition Pre-Design/Design/	\$0	\$0	\$0
Funding Category 1 & 3	Construction Management	\$5,298,626	\$5,298,626	3,814,083
	Construction Cost  Sub-total	\$15,751,285 <b>\$21,049,911</b>	\$15,751,285 \$21,049,911	\$0 \$3,814,083
	Sub-tota	Ψ21,049,911	\$21,043,311	\$3,014,000
Machado Lake Ecosystem Rehabilitation	Land Acquisition	\$0	\$0	\$0
Funding Category 1 & 3	Pre-Design/Design/ Construction Management	\$23,113,996	\$23,113,996	8,656,966
	Construction Cost	\$76,409,901	\$76,409,901	\$0
	Sub-total	\$99,523,897	\$99,523,897	\$8,656,966
Mar Vista Recreation Center Stormwater BMP	Land Acquisition	\$0	\$0	\$0
	Pre-Design/Design/			
Funding Category 1	Construction Management Construction Cost	\$1,130,482 \$3,425,704	\$1,130,482 \$3,425,704	1,484,998 \$2,421,603
	Sub-total		\$4,556,186	\$3,906,601
Oros Green Street	Land Acquisition	\$0	\$0	\$0
Funding Category 4	Pre-Design/Design/ Construction Management	\$300,000	1,325	1,325
			A	0407.000
COUNCIL/MAYOR APPROVED CLOSE-OUT	Construction Cost  Sub-total	\$86,000 \$386,000	\$197,600 \$198,924	\$197,600 \$198,924



Project		Original Prop O Budget	Current Prop O Budget	Prop O Total <sup>1</sup> Expenditures
Peck Park Canyon Enhancement	Land Acquisition	\$0	\$0	\$0
Funding Category 3	Pre-Design/Design/ Construction Management	\$714,662	\$714,662	2,622,405
	Construction Cost	\$5,475,338	\$5,475,338	\$2,578,129
	Sub-total	\$6,190,000	\$6,190,000	\$5,200,534
Penmar Water Quality Improvement Phase I	Land Acquisition	\$0	\$0	\$0
Funding Category 2 & 4	Pre-Design/Design/ Construction Management	\$3,946,800	\$3,946,800	4,555,136
	Construction Cost	\$16,808,000	\$16,808,000	\$11,450,148
	Sub-total	\$20,754,800	\$20,754,800	\$16,005,284
Penmar Water Quality Improvement Phase II	Land Acquisition Pre-Design/Design/	\$0	\$0	\$0
Funding Category 4	Construction Management	\$538,200	\$538,200	56,016
	Construction Cost	\$2,292,000	\$2,292,000	\$0
	Sub-total	\$2,830,200	\$2,830,200	\$56,016
Rory M. Shaw Wetlands Park	Land Acquisition Pre-Design/Design/	\$0	\$0	\$0
Funding Category 2	Construction Management	\$0	\$0	1,635
	Construction Cost	\$7,800,000	\$7,800,000	\$0
	Sub-total	\$7,800,000	\$7,800,000	\$1,635
Rosecrans Recreation Center Stormwater				
Enhancements	Land Acquisition Pre-Design/Design/	\$0	\$0	\$0
Funding Category 3 & 4	Construction Management Construction Cost	\$1,106,427 \$3,722,692	\$1,106,427 \$3,722,692	104,629 \$1,913,984
	Sub-total	\$4,829,119	\$4,829,119	\$2,018,613
Santa Monica Bay Low Flow Diversion				
Upgrades P 1	Land Acquisition Pre-Design/Design/	\$0	\$0	\$0
Funding Category 1	Construction Management	\$1,864,976	\$1,864,976	1,384,519
	Construction Cost  Sub-total	\$4,949,401 \$6,814,377	\$4,949,401 \$6,814,377	\$3,199,746 \$4,584,264
Santa Monica Bay Low Flow Diversion				
Upgrades P 2	Land Acquisition Pre-Design/Design/	\$0	\$0	\$0
Funding Category 1	Construction Management	\$925,077	\$925,077	821,896
	Construction Cost	\$2,455,034	\$2,455,034	\$1,173,948
	Sub-total	\$3,380,111	\$3,380,111	\$1,995,844
Santa Monica Bay Low Flow Diversion	5	<b>#</b> 0.000.000	<b>#</b> 0.000.000	<b>#0.40.000</b>
Upgrades P 3	Right of Way Pre-Design/Design/	\$2,000,000	\$2,000,000	\$342,680
Funding Category 1	Construction Management Construction Cost	\$5,378,778 \$13,255,258	\$5,378,778 \$13,255,258	3,910,302 \$8,437,225
	Sub-total	\$20,634,036	\$20,634,036	\$12,690,207
Santa Monica Bay Low Flow Diversion		_		
Upgrades P 4	Land Acquisition Pre-Design/Design/	\$0	\$0	\$0
Funding Category 1	Construction Management	\$1,721,601	\$1,721,601	1,374,419
	Construction Cost Sub-total	\$4,568,903 \$6,290,504	\$4,568,903 \$6,290,504	\$2,457,042 <b>\$3,831,461</b>
South Los Angeles Wetlands Park (includes				
- · · · · · · · · · · · · · · · · · · ·	Land Acquisition	\$2,011,937	\$2,011,937	\$0
Site Readiness)	Pre-Design/Design/			
Site Readiness) Funding Category 3	Pre-Design/Design/ Construction Management	\$4,466,265	\$4,466,265	5,808,447
•		\$10,200,000	\$4,466,265 \$10,200,000 <b>\$16,678,202</b>	5,808,447 \$3,842,350 <b>\$9,650,797</b>



Project		Original Prop O Budget	Current Prop O Budget	Prop O Total <sup>1</sup> Expenditures
Strathern Pit Multiuse -Land Acquisition	Land Acquisition Pre-Design/Design/	\$10,000,000	\$10,000,000	\$0
Funding Category 2	Construction Managemen Construction Cost	t \$0 \$0	\$0 \$0	\$0 \$0
		total \$10,000,000	\$10,000,000	\$0
	Land Acquisition			
	Pre-Design/Design/	\$12,440,000	\$12,440,000	\$0
Taylor Yard River Park - Parcel G2 Land Acquisition	Construction Managemen Construction Cost		\$0	\$0
Funding Category 3 & 4		\$0	\$0	\$0
		total \$12,440,000	\$12,440,000	\$0
Temescal Canyon Park Stormwater BMP	Land Acquisition Pre-Design/Design/	\$0	\$0	\$0
Phase I	Construction Managemen	t \$2,842,626	\$2,842,626	4,246,633
Funding Category 3 & 4	Construction Cost	\$12,104,809	\$12,104,809	\$7,781,990
	Sub-	total \$14,947,435	\$14,947,435	\$12,028,623
Temescal Canyon Park Stormwater BMP				
Phase II	Land Acquisition Pre-Design/Design/	\$0	\$0	\$0
Funding Category 3 & 4	Construction Managemen	t \$703,374	\$703,374	65,257
	Construction Cost	\$2,995,191	\$2,995,191	\$0
	Sub-	total \$3,698,565	\$3,698,565	\$65,257
Westchester Stormwater BMP	Land Acquisition Pre-Design/Design/	\$0	\$0	\$0
unding Category 1, 2, & 4	Construction Managemen	t \$6,222,000	\$6,222,000	2,540,275.6
	Construction Cost	\$26,500,000	\$26,500,000	\$0
	Sub-	total \$32,722,000	\$32,722,000	\$2,540,276
Westminster Dog Park Stormwater BMP	Land Acquisition	\$0	\$0	\$0
Westimister bog Fark Otorinwater bini	Pre-Design/Design/	ΨΟ	ΨΟ	ΨΟ
Funding Category 4	Construction Managemen	* -,	432,928	432,928
COUNCIL/MAYOR APPROVED CLOSE-OUT	Construction Cost	\$1,159,000	\$254,960	\$254,960
		total \$1,438,755	\$687,888	\$687,888
	Land Acquisition Pre-Design/Design/	\$0	\$0	\$0
Westside Park Rainwater Irrigation Project	Construction Managemen	* / /-	\$1,147,945	1,566,040
Funding Category 1	Construction Cost	\$5,756,644 total \$6,904,589	\$5,756,644 <b>\$6,904,589</b>	\$2,986,142 <b>\$4,552,181</b>
PROJECTS SUBTOTAL	- Oub-	\$524,118,258	\$485,553,780	\$232,910,819
		<b>Ф</b> 524,110,250	<b>\$465,555,760</b>	\$232,910,019
Consultant Cost – Program Related Budget			<b>4500.004</b>	<b>#</b> 500.004
Program Development Full Proposal Development			\$599,684 \$360,000	\$599,864 \$360,000
City Staff - Program Related Budget				
Office of Accounting			\$1,829,590	\$548,323
Bureau of Engineering Bureau of Sanitation			\$7,784,270 \$15,268,594	\$2,750,735 \$8,286,682
Arbitrage			Ţ.3, <u>2</u> 00,001	\$3,233,002
Fund 16F (1st Bond Sale)			\$7,340	\$7,340
Program Contingency			\$25,145,955	\$0
Controller				\$2,700
PROGRAM TOTAL			\$536,549,212	\$245,466,462

<sup>1.</sup> City Staff expenditures for the month of June are included in the Prop O Expenditures column.



#### **4.0 PROJECT STATUS REPORT**

# 4.1 Project Status Report

A brief status report for each project is provided on the following pages. The report identifies key project information, the planned scope of work, progress date, updated construction costs and percentage complete for all Proposition O projects.


The Percentage Complete at the far right hand column of the diagram uses a color-coding system to designate the current phase of each project.

Turquoise Pre-Design

Yellow Right of Way Acquisition/ Land Acquisition

Red Design
Violet Bid and Award
Green Construction
Blue Post Construction

Progress for each project is tracked by a color-coded pie chart. The color-coding system shows work completed in the darker shade of each color and the lighter shade denotes work to be completed. For example, if a project is in design the pie chart begins as light red. As progress is made, a darker red will indicate the approximate percentage of design work completed to date.



PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION	COST	PERCENT COMPLETE
Albion Dairy Park - Demolition	ı			Notice to Proceed:	7/8/2011	
& Remediation	CD 1 - Ed P. Reyes	Demolition of the buildings and	Additional soil remediation is	Contract Duration:	\$440	
1739 N. Albion Street	Designer: Malcolm Pirnie	improvements of an industrial	complete. Storm drain and catch	City Engineer's Est. (Class A):	\$2,468,100	
		facility, remediation and abatement of all hazardous	basin installation will complete in August 2013.	Contract Award	\$2,466,100	
I	Contractor: National Demolition	materials and soils onsite, and	7.tagast 20.0.	Amount:	\$1,269,555	
		the importation of clean soil to		Contract Award +		
	Proj. Mgr.: Iftekhar Ahmed	leave the property in a level, graded condition.		Contingency (241%) CO's to date	\$4,469,555	
	Contact #: 213-485-5875	g		(12, 222%):	\$2,817,428	
				Award Amount + CO's Issued	\$4,086,983	99%
				Master Sch. Constr.	\$4,000,903 Pre	Land Design Bid & Const Post Const
	Photo of Project Site	Funding: Prop O		Completion Date:	APR 2013 Design	Acquire Award
Albion Dairy Park - Land						
Acquisition	CD 1 - Ed P. Reyes	Acquire a parcel of land adjacent	The Purchase and Sale	Prop O Acquisition Cost:	<b>047.474.454</b>	
1739 N. Albion Street	Designer: N/A	to the LA River as part of LA	Agreement was executed on		\$17,474,154	
5 ///		River Revitalization Master Plan.	10/2/09. Escrow closed on 10/23/09. Park land acquisition is	Orig. Const. Contr.:	N/A	
T T	Contractor: N/A	$\bigcirc$	complete.	CO's to date:	N/A	
	Proj. Mgr.: Kendrick Okuda	$(\sqrt{\sqrt{\sqrt{\sqrt{ \sqrt{ \sqrt{ \sqrt{ \sqrt{ \sqrt{ \sqrt{ \sqrt{ \sqrt{ \sqrt{ \sqrt{$				
	Contact #: 213-485-1165			Rev. Constr. Contr.:	N/A	
		$( \cup )( \cup )( )( )( )( )( )( )( )( )( )( )( )( )( $	└¬  └¬      └¬  <i>∪  </i>	Payment to date:	\$17,474,154 Pre	100%  Land Design Bid & Const Post Const
No.	Photo of Project Site	Funding: Prop O		Master Sch. Constr. Completion Date:	Design N/A	
Cabrito Paseo Walkway/Bike	Those of Froject end	. anamg			14/1	<u> </u>
Path		Implement stormwater best	Draiget is an hold due to funding	Est. Prop O Constr.		
	CD 6 -	Implement stormwater best management practices including:	Project is on hold due to funding issues. The Los Angeles	Cost:	\$1,007,558	
btwn Marson St. and Raymer St.	Designer: TBD	installation of bioswales, trash	Neighborhood Land Trust	Orig. Const. Contr.:	N/A	
	Contractor: TBD	capture devices, tree wells to aid	(LANLT) is unable to secure	CO's to date:	N/A	
	Proj. Mgr.: Iftekhar Ahmed	in filtration, and a "SMART" irrigation system.	additional \$3 million in funds			
	Contact #: 213-485-5875		ANET requested to withdraw	Rev. Constr. Contr.:	N/A	
	Contact #. 213-403-3073	[	their request for project funding.			
		Funding: Prop O Kaiser	/)	Payment to date:  Master Sch. Constr.	N/A Pre	Land Design Bid & Const Post Const
$\rightarrow$ $\rightarrow$ $\rightarrow$ $\rightarrow$ $\rightarrow$ $\rightarrow$	Proposed Project Site Plan	Foundation, & LANLT		Completion Date:	N/A Design	Acquire Award
Catch Basin Inserts and						
Covers Phase I		Leatell 0 000 Seconds and 0 000	This content is a content	Prop O Constr.		
O	CD: All	Install 8,000 inserts and 6,000 screens in the high trash	This project is complete.	Cost:	\$14,900,000	
Citywide	Designer: Bureau of Sanitation	generation areas, in the City, to				
	Contractor: Various	achieve 20% trash reduction in				
	Proj. Mgr.: Alfredo Magallanes	the Ballona Creek and Los Angeles River Watersheds.				
	Contact #: 213-485-3958					
				Payment to date:	\$14,202,869	100%
				Construction	Pre Design	Land Design Bid & Const Post Const Acquire Award
	Photo of Catch Basin Insert	Funding: Prop O & Prop 40		Completion Date:	SEP 2007	



# Proposition O - Clean Water Bond Program

PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION C	OST	PERCENT COMPLETE
Catch Basin Opening Screen				Prop O Constr.		
Covers Phase II	CD: All	Install approximately 6,400	This project is complete.	Cost:	\$9,400,000	
Citywide	Designer: Bureau of Sanitation	screens in medium trash				
	Contractor: Various	generation areas, in the City, to increase trash reduction from				
-/	Proj. Mgr.: Alfredo Magallanes	20% (accomplished in Phase 1)				
man total	Contact #: 213-485-3958	to 30% trash reduction in Ballona	││			
	Odinact #. 210 400 0000	Creek and LA River Watersheds.		Payment to date:	\$9,246,965	100%
				Construction	Pre	Land Design Bid & Const Post Co.
	Photo of Catch Basin Screen Cover	Funding: Prop O		Completion Date:	OCT 2007	Acquire Award
Catch Basin Opening Screen				Notice to Bosses I		
Covers Phase III	05.44	Retrofit of approximately 24,219	A new procurement and	Notice to Proceed:		
Citywide	CD: All	catch basins with opening screen	installation services contract will	Contract Duration: City Engineer's Est.	\$42,025,000	
and the second s	Designer: Bureau of Sanitation	covers and 2,600 inserts.	install 2,600 catch basin inserts	(Class A):	\$42,025,000	
The state of the s	Contractor: TBD	Includes City-owned catch basins not covered in Phases I & II, as	throughout the City to comply with trash TMDL.	Contract Award Amount:	\$0	
	Duri Maria Alfarda Maria II.	well as all State and County		Contract Award +		
	Proj. Mgr.: Alfredo Magallanes	catch basins within the City.		Contingency (10%) CO's to date		
	Contact #: 213-485-3958			(#, %): Award Amount +	\$0	
				CO's Issued	\$37,595,224	59%
				Master Sch. Constr.	Pre Design	Land Design Bid & Const Post Con Acquire Award
	Photo of Catch Basin Screen Cover	Funding: Prop O		Completion Date:	DEC 2016	
Cesar Chavez Ground Water						
Improvement	CD 6 -	Retrofit existing gas collection	The board report to the Board of	Prop O Constr. Cost:	\$1,805,050	
12455 Wicks Street	Designer: Kleinfelder/Geosyntec	system, install new flare & restore capacity in adjacent Tujunga	Public Works (BPW) to accept the construction contract is being	Orig. Const. Contr.:	\$7,471,676	
	Contractor: Environmental Construction	Spreading Grounds through	prepared.	CO's to date:	\$727,278	
NAME OF TAXABLE PARTY.	Proj. Mgr.: Fang Chang	renovation of closed collection			ψ. 2.1,2.10	
	Contact #: 213-978-1896	system.		Rev. Constr. Contr.:	\$8,198,954	
	Odinact #. 210 370 1030			Payment to date:	\$7,131,597	100
and the state of the state of		Punding: Prop O, DWP CIWMB		Construction	Pre	Land Design Bid & Const Post Con
	Photo of Project Site	Grant, UDA Grant, & CIEP		Completion Date:	OCT 2009 Design	Acquire Award
Echo Park Lake				Notice to Proceed:	7/11/2011	
Rehabilitation		In-lake improvements, in-lake	Grand Opening event occurred			
751 Echo Park Avenue	CD 13 - Eric Garcetti	vegetation (wetlands) and habitat	on June 15, 2013. The park is	Contract Duration: City Engineer's Est.	600 Days	
751 EUTO PAIK AVEITUE	Designer: Black & Veatch	improvements, and parkland structural best management	open to the public.	(Class A):	\$49,580,000	
	Contractor: Ford E.C.	practices (swales), lake re-		Contract Award Amount:	\$24,485,000	
The same of the sa		circulation system, lake aeration		Contract Award +	\$26,933,500	
	Proj. Mgr.: Julie Allen	system, relocate fountain pump house.		Contingency (10%) CO's to date		
	Contact #: 213-485-1454	nouse.		(62, 7%): Award Amount +	\$1,715,087	
				CO's Issued	\$26,200,087	98%
				Master Sch. Constr.		Land Design Bid & Const Post Con



PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION	COST	PERCENT COMPLETE
Elmer Avenue Phase II:				Notice to Proceed:	12/10/2012	
Imer Paseo	CD 6 -	Convert a paved 20' x 270' alley	Project is in the construction	Contract Duration:	180 days	
02 North Elmer Avenue	Designer: Tetra Tech	into a pocket park with water	phase.	City Engineer's Est. (Class A)	\$000.0 <b>7</b> 5	
	Tetta Tech	quality improvements, including a pervious pedestrian pathway and		Contract Award	\$306,375	
The state of the s	Contractor: Adjul Corporation	a vegetated swale.		Amount Contract Award +	\$358,256	
	Proj. Mgr.: Iftekhar Ahmed	Sedimentation removal devices		Contingency (20%)	\$429,906	
	0	will also be installed.		CO's to date (3,-		
	Contact #: 213-485-5875			.17%): Award Amount +	-\$614	
				CO's Issued	\$357,642	54%
	Photo of Existing Paseo	Funding: Prop O		Construction Completion Date:	Pre JUL 2013 Design	Land Design Bid & Const Po
lamantia Cumland	Thota of Exicting Facco	. anamg rep o		Completion Date.	002 2010	
enoaks-Sunland ormwater Capture				Notice to Proceed:	12/9/2011	
·	CD 6 -	This project will install infiltration	This project is in the construction	Contract Duration:		
ersection of Sunland & Glenoaks	Designer: Bureau of Sanitation	wells and other storm water Best Management Practices (BMPs) to	phase.	City Engineer's Est. (Class A)	\$508,696	
THE PARTY NO.		help alleviate flooding at the		Contract Award		
	Contractor: Hollywood Beautification Tea			Amount Contract Award +	\$508,696	
Jaims In	Proj. Mgr.: Iftekhar Ahmed	events.		Contingency (0%)	\$508,696	
	Contact #: 213-485-5875			CO's to date (0,0):	N/A	
				Award Amount + CO's Issued	N/A	55%
	Photo of Flooding at Subject			Construction	Pre	Land Design Bid & Const P
rand Blvd. Tree Wells	Intersection	Funding: Prop O		Completion Date:	NOV 2013 Design	Acquire Award
rand bivd. Tree wells	CD 11 - Bill Rosendahl	Install seven stormwater	This project is complete.	Notice to Proceed: Contract Duration:	7/7/2008 100 days	
ersection Grand & Riviera		bioretention filters in a high-	This project is complete.	City Engineer's Est.	100 days	
ligh flow Dyress	Designer: PSOMAS	density residential and		(Class A): Contract Award	\$428,900	
Filters* at Righer Elevation than Dyposis	Contractor: Andrew Papac & Sons	commercial corridor in the Venice area to treat runoff from 6.8		Amount:	\$401,797	
		aves.		Contract Award +		
0-	Proj. Mgr.: Andy Flores	( \ \ \ \ \ \ \ \ \ \ \ \ \ \ \ \ \ \ \		Contingency (24.8%)	\$501,797	
Stem Water laflow	0			CO's to date		
("First Riss")	Contact #: 213-485-4496			(5, -15%): Award Amount +	-\$19,353	
History Container		$( \cup ) ( \cup ) ( ) ( ) ( ) ( ) ( ) ( ) ( ) $		CO's Issued	\$382,444	
Booksay Parking Lat	Conceptual Drawing of Tree Well	Funding: Prop O & Prop 50		Construction Completion Date:	DEC 2009 Design	Land Design Bid & Const Po
nsen Dam Wetlands	<del></del>			Notice to Proceed:	2/3/2011	
estoration	CD 7 - Richard Alarcón	Stormwater runoff from three	Project completed. Site is now	Contract Duration:	240 days	
sborne Street @ Foothill Blvd.	Designer: MRCA	existing parking lots will be sent	open for public use.	City Engineer's Est.		
	3	through newly constructed sediment forebays for removal of		(Class A): Contract Award	\$1,159,000	
	Contractor: Lee Construction	trash & sediments prior to		Amount:	\$955,257	
Lover	Proj. Mgr.: Iftekhar Ahmed	wetlands discharge.		Contract Award + Contingency (10%)	\$1,050,257	
Parking Area Detention Area	. 0			CO's to date		
Upper- Paking	Contact #: 213-485-5875			(32, 41%): Award Amount +	\$394,150	
Area				CO's Issued	\$1,334,496	
				Master Sch. Constr.	Pre Desigr	Land Design Bid & Const Po
	Proposed Project Layout	Funding: Prop O & Caltrans-FTIP		Completion Date:	FEB 2012	




PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION COST	PERCENT COMPLETE
Imperial Hwy Sunken Median Stormwater BMP	CD 11 - Bill Rosendahl	Includes one 200-feet long grass	This project is complete.	Prop O Constr. Cost: \$814,75	14
Pershing Drive to California Street	Designer: PSOMAS	swale, one 250-feet long infiltration trench (7'D x 10'W)		Orig. Const. Contr.: \$512,86	
	Contractor: Park West Landscape Inc.	with native vegetation along the		CO's to date: (\$9,09	9)
	Proj. Mgr.: Iftekhar Ahmed Contact #: 213-485-5875	full length of the median, & local regrading to reduce ponding in the median at Main St.		Rev. Constr. Contr.: \$728,76  Payment to date: \$626,78  Construction	11 100% Pre Land Design Bid & Const Post Const
	Photo of Existing Median	Funding: Prop O		Completion Date: AUG 201	Design Acquire Award
Inner Cabrillo Beach Bacterial Water Quality Improvement	CD 15 - Joe Buscaino	Recontour recreational beach	The sand-replacement project is	Prop O Constr. Cost: \$6,956,52	
San Pedro Shore/W. Harbor	Designer: DMJM (Port of Los Angeles)	and replace beach sand to prevent flooding, promote	complete.	Orig. Const. Contr.: \$16,000,00	00
	Contractor: L.A. Deepening Constructors	drainage and sand flushing to		CO's to date:	50
	Proj. Mgr.: John Saldin Contact #: 213-485-1411	improve water quality. Project is being constructed by the Harbor Dept. Prop O is funding/up to \$8.0 M.		Rev. Constr. Contr.: \$16,000,000 Payment to date: \$6,906,580 Construction	100% Pre Land Design Bid & Const Post Const
	Photo of New Sand Placement	Funding: Prop O & Port of LA		Completion Date: JUL 200	Design Acquire Award
La Cienega/Fairfax Stormwater BMP 2800 S. Fairfax Avenue	CD 10 - Herb J. Wesson, Jr.  Designer: PSOMAS  Contractor: TBD  Proj. Mgr.: Iftekhar Ahmed	Construct flow diversion, lift- station, hydrodynamic separator, underground tank, bio-retention area, storage tank, effluent pump station_recirculation_pump	On 4/1/09, City Council canceled this project. The Westside Park Rainwater Irrigation project was approved to replace it.	Est. Prop O Constr. Cost: \$5,617,50 Orig. Const. Contr.: N/ CO's to date: N/	A
	Proj. Mgr.: Iftekhar Ahmed  Contact #: 213-485-5875  Proposed Project Layout	system and an overflow system  Funding: Prop O		Rev. Constr. Contr.: NA Payment to date: NA Master Sch. Constr. Completion Date: APR 201	Pre Land Design Bid & Const Post Const Design Acquire Award
LA Zoo Parking Lot				Notice to Proceed: 2/10/201	0
5333 Zoo Drive	CD 4 - Tom LaBonge Designer: Tetra Tech	Construct stermwater best management plactices including trash capture bevices protous	Project completed. Site is now open for public use.	Contract Duration: 307 day City Engineer's Est. (Class A): \$7,979,50	<i>y</i> s
Continue a Paris de	Contractory Dima Co	pavement and bioswales at the		Contract Award	
	Contractor: Pima Co.  Proj. Mgr.: Iftekhar Ahmed	Zoo Parking Los.		Contract Award + Contingency (10%) \$4,650,08	
	Contact #: 213-485-5875			CO's to date (40, 6%): \$251,85	33
				Award Amount + CO's Issued \$4,479,21	3 100% Pre Land Design Bid & Const Post Const
	Proposed Project Site Plan	Funding: Prop O		Master Sch. Constr.  Completion Date: SEPT 201	Design Acquire Award




	_					
PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION C	OST	PERCENT COMPLETE
Machado Lake-Phase I				Notice to Proceed:	5/13/2013	
(Wilmington Drain)	CD 15 - Joe Buscaino	Install trash netting systems,	Project is in construction phase.	Contract Duration:	\$830	
PCH & Vermont Avenue	Designer: CDM Smith/Parsons	install smart irrigation in landscaped areas, use biofilters	ed areas, use biofilters	City Engineer's Est. (Class A) Contract Award	\$15,910,250	
	Contractor: Ford E.C.	or similar vegetated BMPs, and recontour and align the channel.		Amount: Contract Award +	\$14,940,264	
	Proj. Mgr.: Iftekhar Ahmed			Contingency (10%): CO's to date	\$16,434,290	
	Contact #: 213-485-5875			(#,%) Award Amount +	\$0	
				CO's Issued	\$14,940,264	8% Pre Land Design Bid & Const Post Con
	Photo of Existing Conditions	Funding: Prop O & Prop 50		Master Sch. Constr. Completion Date:	APR 2016	Design Acquire Design Award
Machado Lake Ecosystem						
Rehabilitation	CD 45 les Bussins	In-lake rehabilitation techniques,	All bids were rejected by the	Est. Prop O Constr.		
PCH & Vermont Avenue	CD 15 - Joe Buscaino Designer: CDM Smith	riparian system enhancements,	Board of Public Works on May 8,	Cost:	\$76,409,901	
		and treatment best management	2013. The project will be	Orig. Const. Contr.:	N/A	
	Contractor: TBD  Proj. Mgr.: Julie Allen	practices.	advertised for bids in the summer of 2013.	CO's to date:	N/A	
	Contact #: 213-485-1454			Rev. Constr. Contr.:	N/A	
				Payment to date:	N/A	35%
	Photo of Existing Lake	Funding: Prop O & Prop K		Master Sch. Constr. Completion Date:	APR 2016	Pre Land Design Bid & Const Post Con Award
Mar Vista Recreation Center				Notice to Proceed:	5/4/2009	
Stormwater BMP	CD 11 - Bill Rosendahl	Construction of a stormwater lift	Bureau of Sanitation and the	Contract Duration:	365 days	
11430 W. Woodbine	Designer: PSOMAS	station, hydrodynamic separator, underground detention tank,	Bureau of Engineering continue implement optimization of the	City Engineer's Est. (Class A):	\$2,979,900	
	Contractor: LA Engineering Inc.	chlorination facility, final effluent pump station, recitculation pump.	system.	Contract Award Amount:	\$2,340,120	
	Proj. Mgr.: Andy Flores	and/overflow piping at Mar Vista		Contract Award + Contingency (19%)	\$2,790,120	
	Contact #: 213-485-4496			CO's to date (18, 3%): Award Amount +	\$65,702	
				CO's Issued	\$2,405,822	1009
	Proposed Project Site Plan	Funding: Prop O, Prop 50 & ARRA		Master Sch. Constr. Completion Date:	NOV 2010	Pre Land Design Bid & Const Post Con Award
Oros Green Street						
	CD 12 Erio Corocati	Construct five curb side	This project is complete.	Prop O Constr.		
between Blake Avenue & LA River	CD 13 - Eric Garcetti	"stormwater gardens" in street	project to complete.	Cost:	\$300,000	
Detween Blake Avenue & LA River	Designer: North East Trees (NET)	parkway and a large infiltration		Orig. Const. Contr.:	N/A	
	Contractor: Street Services	gallery beneath Steelhead Park.		CO's to date:	\$0	
	Proj. Mgr.: Dean Harding			Rev. Constr. Contr.:	\$300,000	
	Contact #: 213-473-4242			Payment to date: Construction	\$0	
1			$ \subseteq                                   $	Completion Date:	AUG 2007	1009
	Photo of New Sidewalk & Stormwater Gardens	Aunding: Prop O Prop 13 & CWA		Construction Completion Date:	MAY 2010	Pre Land Design Bid & Const Post Cor Award



PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION COST	PERCENT COMPLETE
Peck Park Canyon				Notice to Proceed: 5/3/	2010
Enhancement	CD 15 - Joe Buscaino	Install vegetated bio-swales,	Conducting Mitigation Measures		days
560 N. Western Avenue	Designer: Tetra Tech	infiltration strips, stormwater catch basins, armoring and re-	establishment and Best  Management Practices (BMP)	City Engineer's Est. (Class A): \$4,000 Contract Award	,641
	Contractor: C.S. Legacy Construction, Inc.	vegetation for bank stabilization	optimization.	Amount: \$3,636	,946
	Proj. Mgr.: John Saldin	Park.		Contract Award + Contingency (10%) \$4,000 CO's to date	,640
O Planting	Contact #: 213-485-1411			(32, 8%): \$301	,760
				Award Amount + CO's Issued \$3,938	
	Proposed Project Layout	Funding: Prop O, Prop 50 & Rec and Trails Grant		Master Sch. Constr. Completion Date: MAY	Pre Design Acquire Design Bid & Const Post Const Award
Penmar Water Quality				Notice to Proceed: 12/12/	2010
Improvement Phase I	CD 11 - Bill Rosendahl	Capture & treat dry/wet weather	Project construction phase is		days
1216 E. Rose Ave	Designer: Brown & Caldwell	runoff. Dry weather runoff to be diverted to sanitary sewer for treatment. Wet weather runoff to	almost complete. Pending items include completion of final inspection corrections and	City Engineer's Est. (Class A): \$13,878 Contract Award	3,500
	Contractor: Pacific Hydrotech	be diverted to the underground	SCADA programming. Beyond	Amount: \$11,360	7,700
	Proj. Mgr.: Andy Flores	storage tank for discharge to	this the system is operational and	Contract Award + Contingency (10%) \$12,500	7,700
A STANDARD OF THE PROPERTY OF	Contact #: 213-485-4496	sanitary sewer.	park has been opened to the public.	CO's to date (50, 4%): \$45	1,705
	Contact #. 213-463-4490			Award Amount +	
- 310				CO's Issued \$11,812	2,405 99% Pre Land Design Bid & Const Post Const
	Proposed Project Layout	Funding: Prop O		Master Sch. Constr. Completion Date: JAN	Design Acquire Award
Penmar Water Quality					
Improvement Phase II	CD 44 Dill December	Install a water treatment system	This project is in the design	Est. Prop O Constr.	
1216 E. Rose Ave	CD 11 - Bill Rosendahl  Designer: Carollo Engineers	for the purpose of reusing	phase.	Cost: \$2,292	
		collected stormwater.		Orig. Const. Contr.:	N/A
DOUBLE OF THE PARTY OF	Contractor: TBD			CO's to date:	N/A
HERACONAND CARRIES FACE DATES	Proj. Mgr.: Katie Doherty				
ANGADARY STREET	Contact #: 213-847-0395			Rev. Constr. Contr.:	N/A
				Payment to date:	N/A 58%  Pre Land Design Bid & Const Post Const
	Proposed Project Layout	Funding: Prop O		Master Sch. Constr. Completion Date: MAR	Design Acquire Award
Rosecrans Rec. Center				Notice to Proceed: 1/17/	2011
Stormwater Enhancements	CD 15 - Joe Buscaino	Install "SMART" irrigation system,	Project is in the construction		days
15000 S. Vermont Avenue	Designer: Withers & Sandgren	bioswales, vegetated retention basins, infiltration basins,	phase.	City Engineer's Est. (Class A): \$3,500	0,000
	Contractor: Horizon Construction Intl.	synthetic soccer field, decomposed granite pathway,		Contract Award Amount: \$3,198 Contract Award +	5,540
Secretary of the secret	Proj. Mgr.: Ray Araujo	and landscaping.		Contingency (10%) \$3,518 CO's to date	5,094
Internal States	Contact #: 213-473-9717				2,151
				Award Amount + CO's Issued \$3,23	7,940 83%
	Proposed Project Layout	Funding: Prop O & Prop K		Master Sch. Constr. Completion Date: FEB	Pre Design Land Design Bid & Const Post Const Award
	r roposeu r roject Layout	r anding. I Top O & I Top IX		Completion Date. FEB	2010



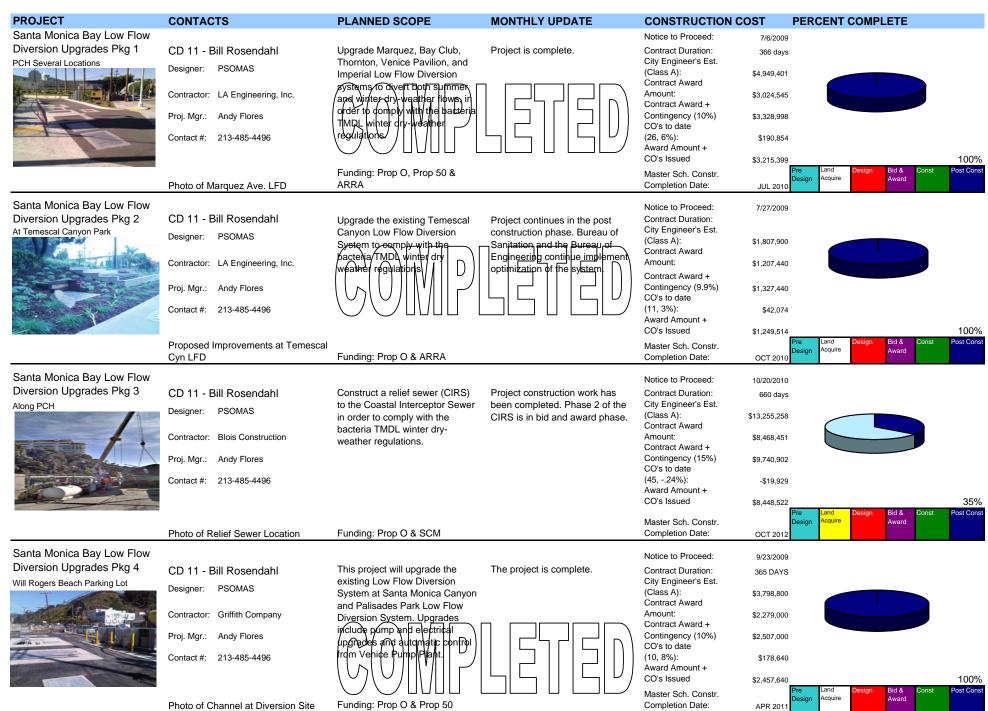



PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION C	COST	PERCENT COMPLETE
South Los Angeles Wetlands				Notice to Proceed:		
Park	CD 9 - Jan Perry	Construct a wetlands park at 54th	The wetlands cells are in the	Contract Duration:	4/9/2010 683 days	
54th St & Avalon Boulevard	Designer: PSOMAS	St. and Avalon Blvd to improve	optimization phase.	City Engineer's Est.		
45/200	Designer. Teenwite	area stormwater quality, and provide recreational space for the		(Class A): Contract Award	\$10,354,300	
	Contractor: Ford E.C.	syrrounding community.		Amount: Contract Award +	\$6,370,000	
	Proj. Mgr.: John Saldin			Contingency (10%)	\$7,297,000	
L WIND OF THE STATE OF THE STAT	Contact #: 213-485-1411	$\langle \langle \rangle \langle \rangle \langle \rangle \rangle \langle \rangle \rangle \langle \rangle \langle \rangle \langle \rangle \langle \rangle \langle$		CO's to date (65, 11%):	\$713,375	5
		Funding: Prop O, Prop K, Prop		Award Amount + CO's Issued	¢7 020 270	100%
SAME TO SERVICE SERVIC		12, Prop 50, Prop 40,			\$7,029,379	Pre Land Design Bid & Const Post Const
	Rendering of Proposed Project	CSSA(SEP), Brownfields Grant, & MTA		Master Sch. Constr. Completion Date:	DEC 2011	Design Acquire Award
Strathern Pit Multiuse - Land	5 ,		•	·		
Acquisition		Acquire the land necessary to	This project is complete.	Est. Prop O		
8175 & 8216 Fair Avenue	CD 6 -	convert a 30-acre gravel pit site	This project is complete.	Acquisition Cost:	\$10,000,000	
orro d ozro raii zwonao	Designer: LA County	into a multipurpose facility dedicated to stormwater retention		Orig. Const. Contr.:	N/A	
to bear	Contractor: N/A	and reuse		CO's to date:	N/A	
former for	Proj. Mgr.: Andy Flores			Rev. Constr. Contr.:		
40 Yunan Harris Dar brown Harris Sa Yunan	Contact #: 213-485-4496			Payment to date:	N/A	
St. Clark				Expected Acquisition	N/A	Pre Land Design Bid & Const Post Const
	Proposed Project Site Plan	Funding: Prop O & LA County		Date:	TBD	Design Acquire Award
Rory M. Shaw Wetlands Park						
	CD 6 -	The Strathern Pit Multiuse	Los Angeles County Public	Est. Prop O Construction Cost:	\$7,800,000	
8175 & 8216 Fair Avenue	Designer: LA County	Project will convert a 30-acre landfill to a wetlands park facility	Works has acquired the land and the project continues in the	Orig. Const. Contr.:	Ψ7,000,000 N/A	
	Contractor: N/A	to provide enhanced water	design phase. The projects new	CO's to date:	N/A	
to house Season	Proj. Mgr.: Andy Flores	quality, flood protection, habitat creation, groundwater recharge,	name is the Rory Shaw Wetlands Park.			
On house the same of the same	Contact #: 213-485-4496	recreational and water reuse.	raik.	Rev. Constr. Contr.:	N/A	
to Name For				Payment to date:	N/A	91%
the state of the s				Master Sch. Constr.		Pre Land Design Bid & Const Post Const Design Acquire Award
	Proposed Project Site Plan	Funding: Prop O & LA County		Completion Date:	JUL 2019	) and the state of
Taylor Yard River Park -						
Parcel G2 Land Acquisition	CD 1 - Ed P. Reyes	Acquire a parcel of land adjacent	Land acquisition is in negotiation.	Est. Prop O Acquisition Cost:	\$12,440,000	
2850 Kerr Street	Designer: N/A	to the LA River as part of Revitalization Master Plan. \$25M		Orig. Const. Contr.:	N/A	
The state of the season	Contractor: N/A	in Prop O funds must be		CO's to date:	N/A	
	Proj. Mgr.: Kendrick Okuda	augmented. CD 1 leads purchase negotiations (coordination with				
San al	Contact #: 213-485-1165	Trust for Public Land).		Rev. Constr. Contr.:	N/A	
				Payment to date:	N/A	
	Dhoto of CO Dorock 9 LA Diver	Funding: Prop C 9 TPD		Expected Acquisition		Pre Land Design Bid & Const Post Const Award
	Photo of G2 Parcel & LA River	Funding: Prop O & TBD		Date:	TBD	<u>'I I I I I I I I I I I I I I I I I I I </u>



PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION C	OST	PERCENT COMPLETE
Temescal Canyon Park				Notice to Proceed:	8/17/2011	1
Stormwater BMP Ph I	CD 11 - Bill Rosendahl	Divert stormwater from an	Project is in the construction	Contract Duration:	616 days	
15900 Pacific Coast Highway	Designer: AECOM	existing storm drain to Temescal Canyon Park for treatment by a	phase.	City Engineer's Est. (Class A): Contract Award	\$8,008,800	
	Contractor: LA Engineering, Inc.	hydrodynamic separator, underground detention tank and		Amount: Contract Award +	\$7,019,800	
	Proj. Mgr.: Iftekhar Ahmed	diversion to a sanitary sewer for treatment at treatment plant.		Contingency (24%) CO's to date	\$7,721,780	)
	Contact #: 213-485-5875	·		(34, 24%): Award Amount +	\$1,679,178	3
				CO's Issued	\$8,698,978	
	Proposed Project Layout	Funding: Prop O		Master Sch. Constr. Completion Date:	JUL 2013	Pre Land Design Bid & Const Post Const Award
Temescal Canyon Park						
Stormwater BMP Ph II	CD 11 - Bill Rosendahl	Phase II of the Temescal Canyon	This project is in the design	Est. Prop O Constr. Cost:	\$2,995,191	I
15900 Pacific Coast Highway	Designer: Carollo Engineers	Park Stormwater BMP Project proposes the construction of an	phase.	Orig. Const. Contr.:	N/A	
	Contractor: TBD	onsite stormwater treatment /		CO's to date:	N/A	
	Proj. Mgr.: Katie Doherty	disinfection system. The treated stormwater is to be used for				
	Contact #: 213-847-0395	landscape irrigation.		Rev. Constr. Contr.:	N/A	A
				Payment to date:	N/A	
	Proposed Project Layout	Funding: Prop O		Master Sch. Constr. Completion Date:	MAR 2015	Pre Land Design Bid & Const Post Const Award
Westchester Stormwater						
ВМР	CD 11 - Bill Rosendahl	Capture and treat stormwater	Bureau of Sanitation (BOS) staff	Est. Prop O Constr. Cost:	\$26,500,000	)
Los Angeles World Airport	Designer: AECOM	runoff from three existing stormdrains through the project	continues to work with LAWA to finalize the MOU.	Orig. Const. Contr.:	N/A	
Party Control of the	Contractor: TBD	BMP elements, including Trash		CO's to date:	N/A	
The state of the s	Proj. Mgr.: Salem Garawi	Net System, Underground Detention Tank and Underground				
The state of the s	Contact #: 213-847-0345	Infiltration Facility.		Rev. Constr. Contr.:	N/A	A
I to deal on other to depart of all				Payment to date:	N/A	
better all of the second of th	Proposed Project Layout	Funding: Prop O		Master Sch. Constr. Completion Date:	OCT 2014	Pre Land Bid & Const Post Const Design Acquire Award
Westminster Dog Park						
Stormwater BMP	CD 44 Bill December	Includes installation of a modular	This project is complete.	Prop O Constr.		
1203 South Main Street	CD 11 - Bill Rosendahl	constructed wetland	project to complete.	Cost:	\$385,330	
	Designer: PSOMAS	(bioremediation filter), so that on- site runoff will be captured and		Orig. Const. Contr.:	\$285,330	
	Contractor: Fleming Environmental, Inc.	treated prior to discharging into		CO's to date:	(\$30,370)	
	Proj. Mgr.: Salem Garawi	the storm drain system		Rev. Constr. Contr.:	<b>#05.1.0</b>	
E TO THE REAL PROPERTY OF THE PARTY OF THE P	Contact #: 213-847-0345			Payment to date:	\$254,960	
THE RESERVE TO THE RE		\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\		Master Sch. Constr.	\$254,585	Pre Land Design Bid & Const Post Const
	Photo of Existing Dog Park	Funding: Prop O		Completion Date:	FEB 2010	Design Acquire Award

PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION CO	OST	PERCENT COMPL	.ETE	
Westside Park Rainwater Irrigation 2785 Clyde Avenue	CD 10 - Herb J. Wesson, Jr. Designer: PSOMAS  Contractor: PPC Construction, Inc.	Treat pollutants from on-site and off-site stormwater by installing a stormwater lift station, a subsurface irrigation system, and a divided by the with a perforated by the state of the s	Project completed. Seventeen (17) solar lights installed by Recreation & Parks.	Notice to Proceed: Contract Duration: City Engineer's Est. (Class A): Contract Award Amount: Contract Award +	6/3/2010 270 day: \$2,766,900 \$2,675,963	0 s	EIE	
THE STATE OF THE S	Proj. Mgr.: Iftekhar Ahmed	for collecting and returning excess irrigation water to the existing stormdrain.		Contingency (10%) CO's to date	\$2,943,559			
1	Contact #: 213-485-5875			(37, 22%): Award Amount + CO's Issued	\$600,210 \$3,276,179			100%
	Photo of Completed Park	Funding: Prop O, Prop 50, Prop K, Quimby		Construction Completion Date:	AUG 201	Pre Land Design Design Acquire	Bid & Const Award	Post Const

# **5.0 APPENDIX**

# 5.1 Map of Proposition O Projects Approved for Implementation

See attached

# 5.2 Catch Basin Retrofits Screen Covers and Inserts by Council Districts

#### **CATCH BASIN RETROFITS**

CATCH BASIN RETROFITS						
	Inserts			Screen Covers		
Council District	Phase I	Phase III		Phase I & II Phase III		
	(COMPLETED)			(COMPLETED)		
	Installed	Planned	Installed	Installed	Planned	Installed*
1	1,174	200	0	960	960	960
2	0	10	0	505	1,436	1,436
3	0	10	0	1,230	1,790	1,790
4	580	500	0	890	1,454	1,454
5	98	20	0	1,186	2,673	2,673
6	0	0	0	380	1,162	1,162
7	0	0	0	960	1,306	1,306
8	1,370	50	0	1,526	1,611	1,611
9	1,300	500	0	1,936	1,040	1,040
10	809	100	0	1,200	1,716	1,716
11	71	10	0	399	2,581	2,581
12	0	20	0	985	2,294	2,294
13	570	320	0	790	941	941
14	1,480	220	0	1,125	1,642	1,642
15	168	40	0	228	1,581	1,581
TOTALS						
TOTALS	7,620	2,000	0	14,300	24,219	24,219

