

# **Proposition O – Clean Water Bond Program**

# **May 2015 Monthly Report**



## **Argo Drain Sub-basin Facility MOU Signing Ceremony at LAX**

#### **Administrative Oversight Committee**

Miguel Santana, City Administrative Officer, Chair Barbara Romero, Board of Public Works Sharon Tso, Chief Legislative Analyst Marcie L. Edwards, Department of Water & Power Greg Good, Office of the Mayor

#### **Citizens Oversight Advisory Committee**

Adi Liberman, Chair Francine Diamond Mark Gold Alina Bokde Miguel Luna Cynthia McClain-Hill Craig A. Perkins M. Teresa Villegas

PREPARED BY
BUREAU OF ENGINEERING
PROP O CLEAN WATER DIVISION





#### **Distribution List**

Miguel Santana, City Administrative Officer Office of the City Administrative Officer (CAO)

Kevin James, President Board of Public Works

Sharon Tso, Chief Legislative Analyst
Marcie L. Edwards, General Manager

Office of the Chief Legislative Analyst (CLA)
Department of Water and Power (DWP)

Barbara Romero, Deputy Mayor Mayor's Office Greg Good Mayor's Office

Adi Liberman, Chair

Francine Diamond

Mark Gold

Alina Bokde

Miguel Luna

Citizens Oversight Advisory Committee

Cynthia McClain-Hill
Craig A. Perkins
Citizens Oversight Advisory Committee
Craig A. Perkins
Citizens Oversight Advisory Committee
Citizens Oversight Advisory Committee

Monica Rodriguez, Vice President

Matt Szabo, President Pro Tempore

Michael R. Davis, Commissioner

Heather Repenning, Commissioner

Carvel on Moore, City Engineer

Board of Public Works

Board of Public Works

Board of Public Works

Board of Public Works

Gary Lee Moore, City Engineer Bureau of Engineering (BOE)

John L. Reamer, Jr., Director Bureau of Contract Administration (BCA)

Nazario Sauceda, Director Bureau of Street Services

Enrique C. Zaldivar, Director Bureau of Sanitation (BOS)

Victoria Santiago, Director

Board of Public Works, Office of Accounting
Michael A. Shull, General Manager

Department of Recreation & Parks (RAP)

Kenneth R. Redd, Deputy City Engineer BOE Adel H. Hagekhalil, Assistant Director BOS

Edward Jordan, Assistant City Attorney City Attorney's Office

David H. Hirano CAO
Alma Gibson CAO
Rafael E. Prieto CLA
Blayne A. Sutton-Wills CLA
David Pettijohn DWP
Shahram Kharaghani BOS
Kendrick K. Okuda BOE

Comments or suggestions regarding the Proposition O Monthly Report may be directed to Kendrick K. Okuda, BOE Proposition O Implementation Program Manager, at 213-485-1165 or email at <a href="mailto:Kendrick.Okuda@lacity.org">Kendrick.Okuda@lacity.org</a>

This report is available for viewing online at the Bureau of Engineering website: http://eng.lacity.org/projects/prop\_o/report2015.htm



#### **TABLE OF CONTENTS**

Sec.	tion			Page
1.0	Exec	utive S	ummary	
			am Summary	4
			COAC, AOC, and Other	4
			Key Issues	
			Proposition O Awards	5 5 7
			Project Community Meetings Schedule	7
	1.2	Bond		8
	1.3	Projec	ct Status Summary	9 9
		1.3.1	Projects in Planning	9
		1.3.2	COAC & AOC Project Funding Recommendations	10
			1.3.2.1 COAC & AOC Project Recommendations	10
			Projects in Implementation	11
		1.3.4	Project and Program Budget Summary	12
			1.3.4.1 Project Budget Summary	12
			1.3.4.2 Program Budget Summary	13
			1.3.4.3 Project Funding Summary	14
2.0	<u>Sche</u>			
	2.1	•	ct Schedules	15
0 0		_	am Master Schedule	16
3.0	Budg		at us. A stual Fun an ditura	47
4.0	3.1	_	et vs. Actual Expenditure	17
4.0		ct State		22
	4.1 4.2	•	ct Status Report ct Optimization Status	34
5.0	Appe	•	of Optimization Status	34
5.0	5.1		of Catch Basin Retrofits Screen Covers and Inserts by Council District	s 35
			cil District Map	36
	5.3		of Proposition O Projects Approved for Implementation	37
			· · · · · · · · · · · · · · · · · · ·	٥.

#### 1.0 EXECUTIVE SUMMARY

#### 1.1 Program Summary

In November 2004, voters of the City of Los Angeles passed the Proposition O – Clean Water Bond, authorizing \$500 million of general obligation bonds for projects to protect public health by cleaning up pollution in the City's rivers, lakes, and beaches. The projects are intended to assist the City of Los Angeles in meeting Federal Clean Water Act requirements. Proposition O – Clean Water Bond will also fund improvements to protect water quality, provide flood protection, increase water conservation, provide habitat protection, and create open space.

This monthly progress report summarizes the status of activities and progress of the Proposition O – Clean Water Bond program, for May 2015.

# 1.1.1 <u>Citizens Oversight Advisory Committee (COAC), Administrative Oversight Committee (AOC), and Other highlights</u>

- The May 18, 2015 COAC meeting was canceled; there were no urgent matters needing action.
- The May 28, 2015 AOC meeting was canceled; there were no urgent matters needing action.



#### 1.1.2 Key Issues

#### • Temescal Canyon Park BMP Ph II & Penmar Water Quality Improvement Ph II Projects

- o **Issue:** Dept. of Recreation and Parks (RAP) consideration to establish project easements and to obtain project approval from the Board of RAP.
- Status: Prop O staff presented Board Reports for project approval, construction right-ofentry and establishment of permanent easements to the RAP Facility Repair & Maintenance Commission Task Force on March 4, 2015. The Task Force approved the reports to be scheduled for the full RAP Board.
- Action: Prop O staff is working with RAP staff to schedule the reports for full Board.
   Prop O staff is also working with BOE's Real Estate Division to begin preparation of the easements required by the reports, after they are approved by the RAP Board.

#### 1.1.3 Prop O Awards

#### Elmer Avenue Green Street Project

National Association of Clean Water Agencies 2011 Operations and Environmental Performance Award

Institute for Sustainable Infrastructure Envision Platinum Award

#### • South Los Angeles Wetlands Park

Construction Management Association of America – Southern California Chapter 2013 Project Achievement Award – Parks less than \$10M

Institute for Sustainable Infrastructure Envision Platinum Award

American Council of Engineering Companies - 2014 Engineering Excellence Awards Competition National Recognition Award

#### • Echo Park Lake Rehabilitation Project

Engineering News Record - California 2013 California Best Projects (Southern California) – Water/Environment

American Public Works Association – Southern California Chapter 2013 BEST Project Award - Drainage, Water and Wastewater

American Society of Civil Engineers – Metro Los Angeles Branch 2013 Outstanding Public Civil Engineering Project – (Water) over \$10M

American Society of Civil Engineers – Los Angeles Section 2013 Outstanding Government Civil Engineering Project



#### Prop O Awards cont'd

California Water Environment Association - Los Angeles Basin Section 2013 Engineering Achievement Award

Southern California Development Forum 2013 Urban Design and Planning Award

National Association of Clean Water Agencies 2014 Operations and Environmental Performance Award

American Society of Civil Engineers - Region 9 2013 Outstanding Parks & Recreation Project

American Academy of Environmental Engineers and Scientists 2014 Grand Prize for Environmental Sustainability

Construction Management Association of America – Southern California Chapter 2014 Project Achievement Award – Public Works Project

California Preservation Foundation 2014 California Preservation Design Award - Rehabilitation Category

American Society of Civil Engineers - National 2015 Outstanding Civil Engineering Achievement Award Finalist

California Stormwater Quality Association (CASQA) 2014 Outstanding Sustainable Stormwater BMP Project

American Society of Landscape Architects - Southern California Chapter 2014 Quality of Life Design Award - Honor Award, Recreation and Parks

American Society of Landscape Architects - Southern California Chapter 2014 Quality of Life Design Award - Award of Excellence

#### Santa Monica Bay Low Flow Diversion Upgrades

American Public Works Association – Southern California Chapter 2013 BEST Project Award – Storm Water Quality

#### Rory M. Shaw Wetlands Park

Institute for Sustainable Infrastructure Envision Platinum Award



#### 1.1.4 Project Community Meetings Schedule

The following is a list of Proposition O project meetings with the public that occurred in May and are planned for the month of June.

	COMMUNITY MEETINGS									
Date	Time	Project	Group	CD	Location					
05/12/15	6:00 p.m.	Machado Lake Ecosystem Rehabilitation	Ken Malloy Harbor Regional Park Advisory Board	15	Harbor Gateway Chamber of Commerce 1400 W. 240 <sup>th</sup> St. Harbor City, CA 90710					
05/13/15	6:00 p.m.	Albion Riverside Park	Public Meeting and Local Volunteer Neighborhood Oversight Committee (LVNOC)	1	Downey Recreation Ctr. 219 S Avenue 18 Los Angeles, CA 90031					
5/20/15	10:00 a.m.	Santa Monica Bay LFD Upgrades Pkg 3 Ph 2	PCH Taskforce	11	Pacific Palisades Library 861 Alma Real Dr. Pacific Palisades, CA 90272					
06/20/15	10:00 a.m.	Machado Lake Phase I	Ribbon Cutting Ceremony	15	25500 Waterman Way Harbor City, CA 90710					



#### 1.2 Bond Sales

The following table is a summary of the bond sales that fund Proposition O.

PROPOSIT	TION O BOND SALE	SUMMARY	
General Obligation Bonds Approved by	Voters		\$500,000,000
Total Bond Sales to Date			\$439,500,000
Fund 16F July 13, 2005 City Council Approved Bond Sale (Ord. 176839 CF 05-1408)		\$37,000,000	
Bond Interest Earnings (As of Apr 30) Bond Interest Balance (As of Mar 31)	\$3,089,304 \$3,029		
Fund 16M July 21, 2006 City Council Approved Bond Sale (Ord. 177733 CF 06-0600-S37)		\$8,000,000	
Bond Interest Earnings (As of Apr 30) Bond Interest Balance (As of Mar 31)	\$900,020 \$5,179		
Fund 16Q July 22, 2008 City Council Approved Bond Sale (Ord. 180090 CF 08-1706)		\$101,000,000	
Bond Interest Earnings (As of Apr 30) Bond Interest Balance (As of Mar 31)	\$6,334,047 \$108,306		
Fund 16T July 21, 2009 City Council Approved Bond Sale (Ord. 180808 CF 09-1674)		\$176,500,000	
Bond Interest Earnings (As of Apr 30) Bond Interest Balance (As of Mar 31)	\$11,328,084 \$602,203		
Fund 16V July 28, 2011 City Council Approved Bond Sale (Ord. 181755 CF 11-0841)		\$117,000,000	
Bond Interest Earnings (As of Apr 30) Bond Interest Balance (As of Mar 31) Total Bond Interest Earnings to Date	\$5,512,933 \$1,151,250 \$27,164,388		
(As of Apr 30)	ψΔ1,104,300		
<b>General Obligation Bonds Remaining</b>	to be Sold		\$60,500,000

#### 1.3 Project Status Summary

The following table summarizes the projects that are being considered. The projects will be presented to the AOC & COAC for approval.

		Prop O	<b>Funds From</b>					
		•	Other		Date presented to the COAC & AOC			
Applicant	Prop O Funding Request	Set Aside Funds Request	Sources (if applicable)	Total Project Funding Needed	COAC	AOC		
Mountains creation and onservation Authority	\$8,561,390	\$0	\$0	\$10,156,479	7/14	7/14		
BOS	\$33,460,603	\$0	\$0	\$34,206,816	TBD	TBD		
BOS	\$58,300,000	TBD	TBD	\$58,300,000	TBD	TBD		
BOS	\$1,000,000	\$0	\$0	\$1,000,000	5/13	TBD		
BOS	\$3,162,958	\$0	\$0	\$3,162,958	TBD	TBD		
1	<b></b>			<b>*</b>				
V C	Mountains creation and onservation Authority  BOS  BOS  BOS	Mountains creation and onservation Authority  BOS \$33,460,603  BOS \$58,300,000  BOS \$1,000,000	Mountains creation and onservation Authority  BOS \$33,460,603 \$0  BOS \$58,300,000 TBD  BOS \$3,162,958 \$0  TOTALS	Mountains creation and onservation Authority         \$8,561,390         \$0         \$0           BOS         \$33,460,603         \$0         \$0           BOS         \$58,300,000         TBD         TBD           BOS         \$1,000,000         \$0         \$0           BOS         \$3,162,958         \$0         \$0           TOTALS	Mountains creation and snservation Authority  BOS \$33,460,603 \$0 \$0 \$34,206,816  BOS \$58,300,000 TBD TBD \$58,300,000  BOS \$1,000,000 \$0 \$0 \$1,000,000  BOS \$3,162,958 \$0 \$0 \$3,162,958	Mountains creation and onservation Authority         \$8,561,390         \$0         \$10,156,479         7/14           BOS         \$33,460,603         \$0         \$0         \$34,206,816         TBD           BOS         \$58,300,000         TBD         TBD         \$58,300,000         TBD           BOS         \$1,000,000         \$0         \$1,000,000         5/13           BOS         \$3,162,958         \$0         \$3,162,958         TBD           TOTALS		

<sup>\*</sup>Grant Funding has not been secured

<sup>\*\*</sup>Funding from other sources have not yet been identified

#### 1.3.2 COAC & AOC Funding Recommendations (Pending Mayor Approval)

The following table summarizes the projects approved and recommended by COAC and AOC for funding. The projects will be presented to the City Council and Mayor for approval.

	PROJECTS RECOMMENDED FOR FUNDING BY COAC AND AOC													
Project		Prop O Funding		Prop O Set Aside Other Funds Sources (if		-	Funding endations	Date Recommended						
Title	Applicant	Request	Request	applicable)	Funding Needed	COAC	AOC	by COAC & AOC						
	TOTALS													

#### 1.3.2.1 COAC & AOC Project Recommendations (Pending Funding Approval)

The following table summarizes the projects approved by COAC and AOC, without funding authority.

	PROJECTS RECOMMENDED BY COAC AND AOC											
Project Title	Applicant	Prop O Funding Request	Prop O Set Aside Funds Request	Funds From Other Sources (if applicable)	Total Project Funding Needed	Month/Year Recommended by COAC & AOC						
Boyle Heights Joint Use Community Center	City of LA, Council District 14	\$2,291,000	\$0	\$528,000	\$2,819,000	July 2007						
	TOTALS											
	\$2,291,000 \$0 \$528,000 \$2,819,000											



### Proposition O - Clean Water Bond

1.3.3 Projects in Implementation (Approved by City Council & Mayor)

1.3.3 Projects in Implementation (Approved by City Council & Mayor) PROJECTS IN IMPLEMENTATION									
11100201	Council/Mayor	ATION	Current Total	Potential Funds					
Project Title	_	Prop O Set Aside	Project Budget	From Other					
Projects in Pre-Design	- <del> </del>		gee						
Aliso Creek-Limekiln Creek Restoration	\$1,595,089	\$0	\$10,156,479	\$0					
Argo Drain Sub-basin Facility	\$30,122,000	\$0	\$37,122,000	\$7,000,000					
Land Acquisition Projects									
Taylor Yard River Park - Parcel G2 Land Acquisition	\$0	\$12,400,000	TBD	TBD					
Projects in Design									
Albion Riverside Park	\$11,455,000	\$0	\$17,139,355	\$5,684,355					
Rory M. Shaw Wetlands Park	\$7,800,000	\$0	\$22,000,000	\$14,200,000					
Projects in Bid & Award									
Penmar Water Quality Improvement Phase II	\$5,830,200	\$0	\$5,830,200	\$2,112,985					
Temescal Canyon Park Stormwater BMP Phase II	\$4,398,565	\$0	\$4,398,565	\$0					
Projects in Construction									
Avalon Green Alley South	\$1,602,642	\$0	\$1,602,642	\$891,344					
Broadway Neighborhood Stormwater Greenway	\$4,626,502	\$0	\$4,626,502	\$2,939,361					
Catch Basin Inserts & Opening Screen Covers Ph IV	\$6,160,000	\$0	\$6,160,000	\$0					
Machado Lake Ecosystem Rehabilitation	\$110,457,563	\$0	\$111,886,560	\$1,428,997					
Machado Lake Phase I (Wilmington Drain)	\$21,049,911	\$0	\$21,049,911	\$13,063,974*					
Santa Monica Bay Low Flow Diversion Upgrade P3 Ph2	\$14,194,469	\$0	\$14,194,469	\$0					
Projects in Post Construction		·							
Albion Dairy Park – Demolition & Remediation	\$6,956,400	\$0	\$6,956,400	\$4,077,476					
Elmer Avenue Phase II: Elmer Paseo	\$829,000	\$0	\$1,275,000	\$446,000					
Temescal Canyon Park Stormwater BMP Phase I	\$14,247,435	\$0	\$14,947,435	\$0					
Projects Completed	. , ,		. , ,						
Albion Dairy Park – Land Acquisition	\$17,537,311	\$0	TBD	TBD					
Catch Basin Inserts and Coverings Phase I	\$14,702,886	\$0	\$14,702,886	\$600,000					
Catch Basin Opening Screen Covers Phase II	\$9,630,788	\$0	\$9,630,788	\$0					
Catch Basin Opening Screen Covers Phase III	\$44,500,000	\$0	\$44,500,000	\$0					
Cesar Chavez Ground Water Improvement	\$2,527,873	\$0	\$9,841,230	\$6,801,230					
Echo Park Lake Rehabilitation	\$45,296,789	\$0	\$45,296,789	\$599,875					
Glenoaks/Sunland Stormwater Capture	\$508,696	\$0	\$508,696	\$0					
Grand Blvd. Tree Wells	\$713,039	\$0	\$713,039	\$350,000					
Hansen Dam Wetlands Restoration	\$2,220,702	\$0	\$2,517,702	\$297,000					
Imperial Highway Sunken Median Stormwater BMP	\$1,301,724	\$0	\$1,301,724	\$0					
Inner Cabrillo Beach Bacterial Water Qlty. Improvement	\$8,000,000	\$0	\$16,000,000	\$8,000,000					
La Cienega/Fairfax Stormwater BMP (CANCELED)	\$668,159	\$0	\$668,159	\$0					
Los Angeles Zoo Parking Lot	\$6,240,455	\$0	\$6,240,455	\$0					
Mar Vista Recreation Center Stormwater BMP	\$4,556,186	\$0	\$4,556,186	\$2,077,838					
Oros Green Street	\$198,924	\$0	\$784,251	\$586,651					
Peck Park Canyon Enhancement	\$6,190,000	\$0	\$7,896,193	\$1,706,193*					
Penmar Water Quality Improvement Phase I	\$17,754,800	\$0	\$17,754,800	\$0					
Rosecrans Recreation Ctr Stormwater Enhancements	\$4,829,119	\$0	\$6,754,033	\$1,924,914					
Santa Monica Bay Low Flow Diversion Upgrades P1	\$4,613,087	\$0	\$4,613,087	\$5,128,183**					
Santa Monica Bay Low Flow Diversion Upgrades P2	\$2,032,341	\$0	\$2,032,341	**					
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 3	\$14,079,108	\$0	\$14,079,108	\$6,826,018					
Santa Monica Bay Low Flow Diversion Upgrades P4	\$3,891,062	\$0	\$3,891,062	**					
South Los Angeles Wetlands Park (Site Readiness)	\$12,378,202	\$0	\$25,847,153	\$13,468,951					
Strathern Pit Multiuse - Land Acquisition	\$10,000,000	\$0	\$28,000,000	\$18,000,000					
Westchester Stormwater BMP (RENAMED "ARGO")	\$2,574,787	\$0	\$2,574,787	\$0					
Westminster Dog Park Stormwater BMP	\$687,888	\$0	\$687,888	\$0 \$0					
Westside Park Rainwater Irrigation	\$4,556,504	\$0	\$8,304,589	\$3,192,038					
TOTALS	\$483,515,206	\$12,400,000	\$559,042,464	\$114,403,383					
TOTALS	Ψ <del>1</del> 00,010,200	Ψ12,700,000	9000,07£,70 <del>1</del>	Ψ11 <del>-</del> 7, <del>7</del> 00,000					

<sup>\*</sup>Estimated non-Prop O funding that may be available. \*\*American Recovery and Reinvestment Act (ARRA) funding for Pkg. 2 is bundled with Pkg. 1. Prop 50-CBI funding for Pkg. 4 is bundled with Pkg. 1.



#### 1.3.4 Project and Program Budget Summary

#### 1.3.4.1 Total Project Budget Summary

The following table is a summary of the Proposition O project funding.

PROJECT BUDGET SUMMARY											
Potential Funds From Other Total Project Description Prop O Funding Prop O Set Aside Sources* Budget											
Projects In Planning– Prop O Funding Request	\$0	\$0	\$0	\$0							
Projects Recommended by AOC	\$0	\$0	\$0	\$0							
Projects In Implementation	\$483,515,206	\$12,400,000	\$114,403,383	\$559,042,464							
	TOTA	LS									
\$483,515,206 \$12,400,000 \$114,403,383 \$559,042											
Prop O Total Project Obligation	\$495,9	15,206									

<sup>\*</sup>Estimated grant funds/reimbursements that may be available

#### 1.3.4.2 Program Budget Summary

The table on the following pages gives an updated program budget summary for Proposition O.

#### 1.3.4.3 Project Funding Summary

The table on the following pages gives an updated project funding summary for Proposition O.

Project Tally Flak - Devillation & Revision(Co.)   \$ 6,000,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000   \$ 6,000			Council / Mo	10° A	nnroyed					Comment
Alban Charp Pail - Demotition & Remonstror	Project Title	Or		- /	Approved	Future Needs				
Alson Formatis Peak	Albion Dairy Park - Demolition & Remediation	\$	6,956,400							6,956,400
Sept   Description   Sept	, '						\$	(22,689)		17,537,311
Auston Green Aley South  Ask Whay 1. Lands (Free Confinence Recentation   \$ 1,002,046   \$ 1,002,046   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000   \$ 1,005,000		_								
Also Vales   Limenia Chemic Confidence Restauration   \$ 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,660,000   \$ 3 1,66	ŭ ,								_	
South Heapt John User Communic Center Improvements   \$   \$   \$   \$   \$   \$   \$   \$   \$										1,595,089
Carle Resear Incenter and Covering Present   COMPLETED \$ 17,000,000   \$ 2,000,110   \$ 1,000,000   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$ 5,000,120   \$		\$	-						\$	-
Carb Bastin Opening Screen Content Plateal II - COMPLETED									_	4,626,502
Cach Basin Cipernig Science Cover Place III - COMPLETED \$ 4,45,00,000 \$ 8,100,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,000 \$ 8,000,	ů						_		_	
Cach Besin Internia A Opening Science Courte Floate IV							Ψ	(505,212)	_	44,500,000
Son Park Lake Rehabilitation - COMPLETED   \$ 8, 82,203.13   \$ 8,08,065.08   \$ 4,508,775   \$ 22,000		\$							\$	6,160,000
Elemet Averuse Prisonal II: Famer Prosect		_					_		_	2,527,873
Commontation Computer COMPLETED   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,000   \$ 0,000,							\$	(38,966,524)		
Harmsen Dani Wellands Restancion - COMPLETED										508,696
Impart   Highway Surken Median Stormwater BMP - CAMPLETED   \$ 2,723,403   \$ 1,142,1679   \$ 1,309,1724							\$	(362,888)	_	713,039
mort Caffrido Beach Bacterial Water Quality Improvement F-COMPLETED   \$ 0,000,000   \$ 1,000,000		_						(4.404.070)	_	2,220,702
La Compage Farinax   Stormward PMP - CANCELED   \$ 7,667,888   \$ 6,989,720   \$ 688,195   \$ 688,195   \$ 68,195   \$ 688,195   \$ 13,001.243   \$ 7,767,880   \$ 688,195   \$ 12,049,911   \$ 1							\$	(1,421,679)		
Michardo Lake Frosent (Wilmington Drain)							\$	(6,999,728)	-	668,159
Michardon Lake Ecosystem Rehabilation			13,904,243						\$	6,240,455
Mar Visita Recreation Centries Estimovater SMM* - COMPLETED \$ 4,5561.86							^	40.000		21,049,911
Total - Front   Street - COMPLETED   \$ , 386,000   \$ , (197,078) \$   18,920							\$	10,933,666		
Pack Park Caryon Enhancement - COMPLETED \$ 5,199,000 \$ \$ 5,190,000 \$ \$ 1,7754,800 \$ \$ 1,7754,800 \$ \$ 1,7754,800 \$ \$ 1,7754,800 \$ \$ 1,7754,800 \$ \$ 1,7754,800 \$ \$ 1,7754,800 \$ \$ 1,7754,800 \$ \$ 1,7754,800 \$ \$ 1,7754,800 \$ \$ 1,7754,800 \$ \$ 1,7754,800 \$ \$ 1,7754,800 \$ \$ 1,7754,800 \$ \$ 1,7754,800 \$ \$ 1,7754,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,800,800 \$ 1,754,8							\$	(187,076)	_	198,924
Pennar Valer Quality Improvement Phase II	Peck Park Canyon Enhancement - COMPLETED	\$	6,190,000					, · , · <del>-</del> /	\$	6,190,000
Roy M. Shew Wellands Palik Roy M. Shew Wellands Palik Rosecarian Recordantic Content Stomwater Enhancements - COMPLETED \$ 4,829,119 \$ 2,023,210,200 \$ 4,613,087 Santa Monica Bay Low Flow Diversion Upgrades, Ptg. 2 - COMPLETED \$ 3,300,111 \$ \$ (2,201,200) \$ 4,613,087 Santa Monica Bay Low Flow Diversion Upgrades, Ptg. 2 - COMPLETED \$ 3,300,111 \$ \$ (1,547,770) \$ 2,003,241 Santa Monica Bay Low Flow Diversion Upgrades, Ptg. 3 - COMPLETED \$ 3,300,111 \$ \$ (6,54,928) \$ 1,047,700 \$ 2,003,241 Santa Monica Bay Low Flow Diversion Upgrades, Ptg. 3 - COMPLETED \$ 20,634,036 \$ \$ (6,54,928) \$ 1,047,700 \$ 1,079,100 \$ 2,003,241 Santa Monica Bay Low Flow Diversion Upgrades, Ptg. 3 - Flow Flow Flow Flow Flow Flow Flow Flow		_								17,754,800
Rosectars Recreation Centrel Stormwater Enhancements - COMPLETED \$ 4,829,119 \$ 2,201,209 \$ 4,613,877 \$ \$ 2,201,209 \$ 4,613,877 \$ \$ 2,201,209 \$ 4,613,877 \$ \$ 2,201,200 \$ 4,613,877 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ 4,613,877 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ 4,613,877 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ 4,613,877 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ 4,613,877 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ \$ 2,203,241 \$ \$ 2,201,200 \$ 2,203,241 \$ \$ 2,203,241 \$ \$ 2,203,241 \$ \$ 2,203,241 \$ \$ 2,203,241 \$ \$ 2,203,241 \$ \$ 2,203,241 \$ \$ 2,203,241 \$ \$ 2,203,241 \$ \$ 2,203,241 \$ \$ 2,203,241 \$ \$ 2,203,241 \$ \$ 2,203,241 \$ \$ 2,203,241 \$ \$ 2,203,241 \$ \$ 2,203,241 \$ \$ 2,203,241 \$ \$ 2,203,241 \$ \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,241 \$ 2,203,2			-,,						_	
Santa Monica Bay Low Flow Diversion Upgrades, Plag. 1 - COMPLETED   \$ 6,814,977   \$ (2,201,290) \$ 4,613,067   Santa Monica Bay Low Flow Diversion Upgrades, Plag. 2 - COMPLETED   \$ 3,300,111   \$ (1,347,705) \$ (2,003,241) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2,047,045) \$ (2			, ,						_	, ,
Santa Monica Bay Low Flow Diversion Upgrades, Pig. 3 - COMPLETED   \$ 20.634,038   \$ (6.554,928) \$ 14,079,000   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460   \$ 14,194,460							\$	(2,201,290)		4,613,087
Santa Monica Biru Low Flow Diversion Upgrades, Pig., 3 Phase 2   \$ 14.194.469   \$ (2.399.442   \$ 3.89.164   \$ 3.80.800   \$ (2.399.442   \$ 3.89.164   \$ 3.80.800   \$ (2.399.442   \$ 3.89.164   \$ 3.80.800   \$ (2.399.442   \$ 3.89.164   \$ (3.99.442   \$ 3.89.164   \$ (3.99.442   \$ 3.89.164   \$ (3.99.442   \$ 3.89.164   \$ (3.99.442   \$ 3.89.164   \$ (3.99.442   \$ 3.89.164   \$ (3.99.442   \$ 3.89.164   \$ (3.99.442   \$ 3.89.164   \$ (3.99.442   \$ 3.89.164   \$ (3.99.442   \$ 3.89.164   \$ (3.99.442   \$ (3.99.442   \$ 3.89.164   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (3.99.442   \$ (		_					_			2,032,341
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 4 - COMPLETED \$ 6,290,504 \$ (2,399,442) \$ 3,891,662 South Los Anales Vetlands Park (includes) Site Readless) - COMPLETED \$ 10,000,000 \$ 12,300,000 \$ 12,300,000 \$ 12,300,000 \$ 12,300,000 \$ 12,400,000 \$ 10,000,000 \$ 12,400,000 \$ 10,000,000 \$ 12,400,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$ 10,000,000 \$	, , , , ,						\$	(6,554,928)		
South Los Angeles Wellands Park (includes Sile Readiness) - COMPLETED \$ 16,678,202 \$ \$ (4,300,000) \$ 12,378,202 \$ \$ (1,000,000) \$ 1,000,000 \$ 12,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,000 \$ 1,000,0							\$	(2.399.442)	-	
Taylor Yard River Park - Parcel G2 Land Acquellon	South Los Angeles Wetlands Park (includes Site Readiness) - COMPLETED	_							_	12,378,202
Tamescal Carryon Park Stormwester Phase     \$ 14,247,435   \$ 1,427,435   \$ 1,4247,435   \$ 1,4247,435   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,4381,555   \$ 1,43	<u>'</u>	\$	10,000,000						_	10,000,000
Temescal Carryon Park Stormwater Phase II   \$ 4.398,565   \$ 4.398,565   \$ 4.398,565   \$ 4.398,565   \$ 4.398,565   \$ 4.398,565   \$ 4.398,565   \$ 6.301,472,131   \$ 2.574,787   \$ 887,888   \$ 32.722,000   \$ (30,147,213) \$ 2.574,787   \$ 887,888   \$ (75,9867) \$ 887,888   \$ 6.904,559   \$ (2.348,085) \$ (55,9867) \$ 887,888   \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$ (25,348,085) \$		•	14 247 425	\$	12,400,000				_	
Westindsted Dig Park Stormwater BMP - CMPLETED   \$ 1,438,755   \$ (2,348,065) \$ 2,574,787   \$ 887,888   \$ Westindsted Dog Park Stormwater BMP - CMPLETED   \$ 6,904,569   \$ 1,238,755   \$ (2,348,065) \$ 4,556,504   \$ 12,400,000 \$ \$ (2,348,065) \$ 4,556,504   \$ 12,400,000 \$ \$ (2,348,065) \$ 4,556,504   \$ 12,400,000 \$ \$ (2,348,065) \$ 4,556,504   \$ 12,400,000 \$ \$ (2,348,065) \$ 4,556,504   \$ 12,400,000 \$ \$ (2,348,065) \$ 4,556,504   \$ 12,400,000 \$ \$ (2,348,065) \$ 4,556,504   \$ 12,400,000 \$ \$ (2,348,065) \$ 4,556,504   \$ 12,400,000 \$ \$ (2,348,065) \$ 4,556,504   \$ 12,400,000 \$ \$ \$ (2,348,065) \$ 4,556,504   \$ 12,400,000 \$ \$ \$ (2,348,065) \$ 4,556,504   \$ 12,400,000 \$ \$ \$ (2,348,065) \$ 4,556,504   \$ 12,400,000 \$ \$ \$ (2,348,065) \$ 4,556,504   \$ 12,400,000 \$ \$ \$ (2,348,065) \$ 4,556,504   \$ 12,400,000 \$ \$ \$ (2,348,065) \$ 4,556,504   \$ 12,400,000 \$ \$ \$ (2,348,065) \$ 4,556,504   \$ 12,400,000 \$ \$ \$ (2,348,065) \$ 4,556,504   \$ 12,400,000 \$ \$ \$ (2,348,065) \$ 4,556,504   \$ 12,400,000 \$ \$ \$ (2,348,065) \$ 4,556,504   \$ 12,400,000 \$ \$ \$ (2,348,065) \$ 4,556,504   \$ 12,400,000 \$ \$ \$ (2,348,065) \$ 4,566,504   \$ 12,400,000 \$ \$ \$ (2,348,065) \$ 4,566,504   \$ 12,400,000 \$ \$ \$ (2,348,065) \$ 4,566,504   \$ 12,400,000 \$ \$ \$ (2,348,065) \$ 4,566,504   \$ 12,400,000 \$ \$ \$ (2,348,065) \$ 4,566,504   \$ 12,400,000 \$ \$ \$ (2,348,065) \$ 4,566,504   \$ 12,400,000 \$ \$ \$ \$ \$ \$ \$ (2,348,065) \$ \$ (2,348,065) \$ \$ (2,348,065) \$ \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348,065) \$ (2,348									_	
Vestside Park Rainwater Irrigation - COMPLETED   \$ 6,904,599   \$ (2,348,085) \$ 4,556,504	Westchester Stormwater BMP - RENAMED "ARGO"		32,722,000					(30,147,213)		2,574,787
Total - Project Budget   \$ 581,433,961   \$ 12,400,000   \$ - \$ (97,918,754)   \$ 495,915,206		_					•	,	_	687,888
City Staff - Program Related Budget (as of November 2014)   Office of Accounting		_		•	40 400 000	•				
Stream of Contract Administration   S		el a	361,433,961	Þ	12,400,000	ъ -	Þ	(97,910,754)	Đ	495,915,200
Bureau of Engineering   \$ 7.490.358   \$ 1,6987.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.893   \$ 16.087.89	Office of Accounting	\$	1,906,709						\$	1,906,709
Bureau of Sanitation			-						_	-
Related Costs									_	
Subtotal   \$ 33,562,799   \$ - \$ - \$ - \$   \$ 33,562,799										8,077,839
Program Development/Implementation	Subtota			\$	-	\$ -	\$	-		33,562,799
Full Proposal Development		-								
Subtotal   \$ 960,000   \$ - \$ - \$ (136)   \$ 959,864							\$	(136)		
Optimization				\$	-	\$ -	\$	(136)		959,864
Arbitrage \$ 2,000,000 \$ \$ 2,000,000 \$ \$ 2,000,000 \$ \$ 2,000,000 \$ \$ 2,000,000 \$ \$ \$ 2,000,000 \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	General Costs (As of June 24, 2015)									-
Controller-ITA	Optimization	\$	1,616,524						_	1,616,524
Subtotal   \$ 2,700   \$ 2,000,000   \$ -   \$ -   \$ 3,619,224		•	2.700	\$	2,000,000					
Total - Prop O Budget   \$ 615,956,760   \$ 12,400,000   \$ - \$ (97,918,890)   \$ 534,057,093				\$	2,000,000	\$ -	\$	-		3,619,224
Sample	Total - Prop O Budget	et \$	615,956,760	\$			\$	(97,918,890)	\$	534,057,093
Bond Proceeds - First Sale   \$ 37,000,000   \$ 37,000,000     Bond Proceeds - First Sale Interest   \$ 3,089,147   \$ 3,089,147     Bond Proceeds - Second Sale   \$ 8,000,000   \$ 8,000,000     Bond Proceeds - Second Sale Interest   \$ 899,279   \$ 8,000,000     Bond Proceeds - Second Sale Interest   \$ 899,279   \$ 8,000,000     Bond Proceeds - Third Sale   \$ 101,000,000   \$ 101,000,000     Bond Proceeds - Third Sale Interest   \$ 6,318,288   \$ 6,318,288     Bond Proceeds - Fourth Sale Interest   \$ 16,500,000   \$ 176,500,000     Bond Proceeds - Fourth Sale Interest   \$ 11,241,990   \$ 117,419,90     Bond Proceeds - Firth Sale   \$ 117,000,000   \$ 117,000,000     Bond Proceeds - Firth Sale Interest   \$ 117,000,000   \$ 117,000,000     Bond Proceeds - Firth Sale Interest   \$ 117,000,000   \$ 117,000,000     Bond Proceeds - Firth Sale Interest   \$ 117,000,000   \$ 117,000,000     Bond Proceeds - Firth Sale Interest   \$ 117,000,000   \$ 117,000,000     Bond Proceeds - Firth Sale Interest   \$ 117,000,000   \$ 117,000,000     Bond Proceeds - Firth Sale Interest   \$ 117,000,000   \$ 117,000,000     Bond Proceeds - Firth Sale Interest   \$ 117,000,000   \$ 117,000,000     Bond Proceeds - Firth Sale Interest   \$ 117,000,000   \$ 117,000,000     Bond Proceeds - Firth Sale Interest   \$ 117,000,000   \$ 117,000,000     Bond Proceeds - Firth Sale Interest   \$ 117,000,000   \$ 117,000,000     Bond Proceeds - Firth Sale Interest   \$ 117,000,000   \$ 117,000,000     Bond Proceeds - Firth Sale Interest   \$ 117,000,000   \$ 117,000,000     Bond Proceeds - Firth Sale Interest   \$ 117,000,000   \$ 117,000,000     Bond Proceeds - Firth Sale Interest   \$ 117,000,000   \$ 117,000,000     Bond Proceeds - Firth Sale Interest   \$ 117,000,000   \$ 117,000,000     Bond Proceeds - Firth Sale Interest   \$ 117,000,000   \$ 117,000,000     Bond Proceeds - Firth Sale Interest   \$ 117,000,000   \$ 117,000,000     Bond Proceeds - Firth Sale Interest   \$ 117,000,000   \$ 117,000,000     Bond Proceeds - Firth Sale Interest   \$ 117,000,000   \$ 117,000,000     Bond Proceeds -	POTENTIA	AL FU	JNDING SOUR	CES						
Bond Proceeds - First Sale Interest   \$ 3,089,147   \$ 3,089,147   Bond Proceeds - Second Sale   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$ 8,000,000   \$										
Bond Proceeds - Second Sale   \$ 8,000,000   \$ 8,000,000     Bond Proceeds - Second Sale Interest   \$ 899,279   \$ 899,279     Bond Proceeds - Third Sale   \$ 101,000,000   \$ 101,000,000     Bond Proceeds - Third Sale Interest   \$ 6,318,288   \$ 6,318,288     Bond Proceeds - Fourth Sale   \$ 176,500,000   \$ 176,500,000     Bond Proceeds - Fourth Sale Interest   \$ 11,241,990   \$ 11,241,990     Bond Proceeds - Fifth Sale Interest   \$ 11,241,990   \$ 11,241,990     Bond Proceeds - Fifth Sale Interest   \$ 117,000,000   \$ 117,000,000     Bond Proceeds - Fifth Sale Interest   \$ 5,345,059   \$ 5345,059     Bond Proceeds - Future Sales   \$ 60,500,000   \$ 60,500,000     Bond Proceeds - Fourth Sale Interest   \$ 18,270,046   \$ 18,270,046     Less Set-Aside for Future Arbitrage Payments   \$ 2,000,000   \$ 7,000,000     Sewer Construction and Maintenance (SCM)   \$ 7,000,000   \$ 7,000,000     Total - Funding Sources   \$ 484,663,809   \$ 2,000,000   \$ 7,000,000   \$ 7,000,000     Total - Prop O Budget   \$ (534,057,093)     PROP O PROGRAM BUDGET CONTINGENCY   \$ 20,106,715										37,000,000
Bond Proceeds - Second Sale Interest   \$ 899,279   \$ 899,275				<u> </u>			_			
Bond Proceeds - Third Sale   \$ 101,000,000   \$ 101,000,000			899,279							899,279
Bond Proceeds - Fourth Sale   \$ 176,500,000   \$ 176,500,000	Bond Proceeds - Third Sale	\$	101,000,000		-				\$	101,000,000
Bond Proceeds - Fourth Sale Interest   \$ 11,241,990   \$ 11,241,990   \$ 11,241,990   \$ 11,241,990   \$ 11,241,990   \$ 117,000,000   \$ 117,000,000   \$ 117,000,000   \$ 117,000,000   \$ 117,000,000   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,241,090   \$ 13,										
Bond Proceeds - Fifth Sale   \$ 117,000,000   \$ 117,000,000							-			
Bond Proceeds - Fifth Sale Interest   \$ 5,345,059   \$ 5,345,059   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000   \$ 60,500,000										117,000,000
Bond Proceeds - Secured Grants Received   \$ 18,270,046   \$ 18,270,046   \$ 18,270,046   \$ 18,270,046   \$ 18,270,046   \$ 2,000,000   \$ 2,000,000   \$ 2,000,000   \$ 2,000,000   \$ 2,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,000   \$ 3,000,0		\$								5,345,059
Less Set-Aside for Future Arbitrage Payments       \$ 2,000,000       \$ 2,000,000         Sewer Construction and Maintenance (SCM)       \$ 7,000,000       \$ 7,000,000         Total - Funding Sources       \$ 484,663,809       \$ 2,000,000       \$ 67,500,000       \$ - \$ 554,163,809         Total - Prop O Budget       \$ (534,057,093)         PROP O PROGRAM BUDGET CONTINGENCY       \$ 20,106,715		•	10 270 040			\$ 60,500,000				
Sewer Construction and Maintenance (SCM)   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.00   \$ 7,000,000.		Ф	10,270,046	\$	2,000.000					2,000,000
Total - Funding Sources \$ 484,663,809 \$ 2,000,000 \$ 67,500,000 \$ - \$ 554,163,809  Total - Prop O Budget \$ (534,057,093  PROP O PROGRAM BUDGET CONTINGENCY \$ 20,106,715	, ,	L		Ė	, ,	\$ 7,000,000.00				7,000,000
Total - Prop O Budget \$ (534,057,093  PROP O PROGRAM BUDGET CONTINGENCY \$ 20,106,715	Total - Funding Sources	s \$	484,663,809	\$	2,000,000	\$ 67,500,000	\$	-	\$	554,163,809
PROP O PROGRAM BUDGET CONTINGENCY \$ 20,106,715						Tota	I - P	rop O Budget	\$	(534,057,093)
					PROP O PR					20,106,715
	Bond Proceeds - Secured Grants Anticipated	\$	8,094,674							8,094,674

		Original Prop O Funding (with	Other Direct	Potential	
Project Title	Budget	set asides)	Funding	Reimbursements Source	Status
			\$ -	\$ 500,000 Brownsfield	Grant received
Albion Dairy Park - Demolition & Remediation	\$ 6,956,400	\$ 6,956,400	\$ -	\$ 3,000,000 Demolition escrow account	Demolition escrow check received for \$3,000,000
,			\$ 571,320	Sprint Nextel and Swiss II lease paym 20,952 City Clerk	Rental reimbursement of \$20,952 approved
Albion Dairy Park - Land Acquisition - COMPLETED	TBD	\$ 17,537,311	\$ -	\$ - N/A	N/A
·		11,001,011	\$ -	\$ 5,000,000 Prop 84	1971
Albion Riverside Park	\$ 17,139,355	\$ 11,455,000	\$ 684,355		
Aliso Creek-Limekiln Creek Restoration	\$ 10,156,479	\$ 1,595,089	\$ -	\$ -	
Argo Drain Sub-basin Facility	\$ 37,122,000	\$ 30,122,000	\$ -	\$ 7,000,000 LAWA	MOU Draft has been sent to City Council
Avalon Green Alley South	\$ 1,602,642		\$ -	\$ 891,344 Prop 84	Grant secured
Broadway Neighborhood Stormwater Greenway	\$ 4,626,502		\$ -	\$ 2,939,361 Prop 84	Grant secured
Catch Basin Inserts and Coverings Phase I - COMPLETED	\$ 14,702,886		\$ -	\$ 600,000 Prop 40	Grant completed
Catch Basin Opening Screen Covers Phase II - COMPLETED  Catch Basin Opening Screen Covers Phase III - COMPLETED	\$ 9,630,788 \$ 44,500,000		\$ - \$ -	\$ - N/A \$ - N/A	N/A N/A
Catch Basin Inserts & Opening Screen Covers Phase IV	\$ 6,160,000			\$ - N/A	N/A
Caton Baom moone a opening coron covers i nace iv	ψ 0,100,000	0,100,000	\$ 5,250,000		Secured
One of the same One of the same of the sam	¢ 0.044.000	¢ 0.507.070	\$ 750,000		Secured
Cesar Chavez Ground Water Improvement - COMPLETED	\$ 9,841,230	\$ 2,527,873	\$ 387,230	\$ - UDAG	Secured
			\$ 414,000	\$ - CIEP	Secured
Echo Park Lake Rehabilitation - COMPLETED	\$ 45,896,664	\$ 45,296,789	\$ 599,875		Funding of \$494,978.61 has been received
Elmer Avenue Phase II: Elmer Paseo	\$ 1,275,000		\$ 446,000		Secured
Glenoaks/Sunland Stormwater Capture - COMPLETED	\$ 508,696		\$ -	\$ - N/A	N/A
Grand Blvd. Tree Wells - COMPLETED Hansen Dam Wetlands Restoration - COMPLETED	\$ 713,039 \$ 2,517,702		\$ 297,000	\$ 350,000 Prop 50-SMBRP \$ - Caltrans - FTIP	Grant completed Secured by MRCA for Design
Imperial Highway Sunken Median Stormwater BMP - COMPLETED	\$ 1,301,724		\$ 297,000	\$ - Califais - FTIP	N/A
Inner Cabrillo Beach Bacterial Water Quality Improvement - COMPLETED	\$ 16,000,000		\$ 8,000,000	\$ - Port of Los Angeles	Secured
La Cienega Fairfax Stormwater BMP - CANCELED	\$ 668,159		\$ -	\$ - N/A	Project canceled
Los Angeles Zoo Parking Lot - COMPLETED			\$ -	\$ - N/A	N/A
			\$ -	\$ 5,068,856 Prop 50-IRWMP	Secured
Machado Lake-Phase I (Wilmington Drain)	\$ 21,049,911	\$ 21,049,911	\$ -	\$ 8,166,474 LA County Flood Control District	Final Agreement Pending
			\$ 10,000		Secured
			\$ 780,000		Funding of \$780,000 received and grant completed
Machado Lake Ecosystem Rehabilitation	\$ 111,886,560	\$ 110,457,563	\$ 296,997		Grant completed
			\$ 352,000	\$ - Quimby \$ 1,777,838 Act	Secured Grant reimbursement of \$1,777,838 received
Mar Vista Recreation Center Stormwater BMP - COMPLETED	\$ 4,556,186	\$ 4,556,186	\$ - \$ -	\$ 300,000 Prop 50-SMBRP	Grant completed
Oros Green Street - COMPLETED	\$ 784,251	\$ 198,924	\$ 586,651		Secured
			\$ 1,586,193		\$1,586,193 in grant funding authorized for payment
Peck Park Canyon Enhancement - COMPLETED	\$ 7,896,193	\$ 6,190,000	\$ 120,000		\$120,000 in grant funding paid; grant completed
Penmar Water Quality Improvement (Phase I) - COMPLETED	\$ 17,754,800	\$ 17,754,800	\$ -	\$ - N/A	N/A
Penmar Water Quality Improvement (Phase II)	\$ 5,830,200	\$ 5,830,200	\$ -	\$ 2,112,985 Prop 84	Grant Secured
Rory M. Shaw Wetlands Park	\$ 22,000,000	\$ 7,800,000	\$ 14,200,000		Secured
Rosecrans Recreation Center Stormwater Enhancements - COMPLETED	\$ 6,754,033	\$ 4,829,119	\$ 568,690		Secured
			\$ 1,356,224		Prop O K to find funding or down scope project
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 1 - COMPLETED	\$ 4,613,088	\$ 4,613,087	\$ -	\$ 4,361,106 American Recovery & Reinvestment Act (ARRA)	Grant completed; ARRA funding for Pkg. 2 is bundled with Pkg. 1
Canta Monica Bay Low Flow Diversion opgrades, Fkg. 1 - Comi LETED	Ψ,015,000	4,013,007	\$ -	\$ 767,077 Prop 50-CBI	Grant completed
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 2 - COMPLETED	\$ 2,032,342	\$ 2,032,341	\$ -	\$ - Act	ARRA funding for Pkg. 2 is bundled with Pkg. 1
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 3 - COMPLETED	\$ 12,079,108	\$ 14,079,108	\$ -	\$ - N/A	N/A
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 3 Phase 2	\$ 14,194,469			\$ 6,826,018 SCM Fund	Secured
Santa Monica Bay Low Flow Diversion Upgrades, Pkg. 4 - COMPLETED	\$ 3,891,062	\$ 3,891,062	\$ -	\$ - Prop 50-CBI	Prop 50-CBI funding for Pkg. 4 is bundled with Pkg. 1
			\$ -	\$ 3,808,583 Prop 50-IRWMP	grant anticipated.
			\$ 2,011,937		Grant of \$2,011,937 paid and grant completed
			\$ 1,282,721 \$ 3,739,707		Grant funding of \$1,282,721 paid and grant completed Funding of \$3,277,193 paid
South Los Angeles Wetlands Park (includes Site Readiness) - COMPLETED	\$ 25,847,153	\$ 12,378,202	\$ 1,000,000		Grant funding of \$1,000,000 paid and grant completed
Count Los Angeles Wellands Fair (includes one Readiness) - Comit ELTED	Ψ 25,047,155	12,576,202	\$ 500,000		Grant funding of \$1,000,000 paid and grant completed  Grant funding of \$500,000 paid and grant completed
			\$ -	\$ 858,525 MTA for remediation	Reimbursement of \$858,525 received and completed
			\$ -	\$ 67,501 MTA - lease payment	Lease payment of \$67,501 received and completed
			\$ -	\$ 199,977 EPA - Brownfields grant	Grant completed
Strathern Pit Multiuse - Land Acquisition - COMPLETED	\$ 28,000,000				Secured
Taylor Yard River Park - Parcel G2 Land Acquisition	TBD	\$ 12,400,000	TBD	TBD TBD	TBD
Temescal Canyon Park Stormwater BMP (Phase I)	\$ 14,947,435	\$ 14,247,435	\$ -	\$ - N/A	N/A
Temescal Canyon Park Stormwater BMP (Phase II)	\$ 4,398,565	\$ 4,398,565	\$ -	\$ - N/A \$ - N/A	N/A N/A
Westchester Stormwater BMP - RENAMED "ARGO"  Westminster Dog Park Stormwater BMP - COMPLETED	\$ 2,574,787 \$ 687,888	\$ 2,574,787 \$ 687,888	\$ - \$ -	\$ - N/A \$ - N/A	N/A N/A
Westimister Duy Fair Stuffiwater Divir - CUNIFLETED	ψ 001,008	Ψ 001,888	\$ -	\$ 2,000,000 Prop 50-SMBRP	Grant completed
Westside Park Rainwater Irrigation - COMPLETED	\$ 8,304,589	\$ 4,556,504	\$ 900,000		Secured
	, ,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,	,,	\$ 292,038		Secured
			OTALS	· · · · · · · · · · · · · · · · · · ·	<u> </u>
	\$ 557,642,341	\$ 495,915,206	\$ 64,982,938	\$ 56,616,597	




#### 2.0 SCHEDULE

**2.1** <u>Project Schedules</u>
The following table summarizes the schedule status for projects in the Program Schedule Update.

The following table summarizes the schedule status for projects in the P	rogram Sch	<u>edule Up</u>	
Description	Ahead	On	Behind
Projects in Pre-Design			
Aliso Creek-Limekiln Creek Restoration			<b>✓</b>
Argo Drain Sub-basin Facility		<b>√</b>	
Land Acquisition Projects			
Taylor Yard River Park-Parcel G2 Land Acquisition*		ACTIVE	
Projects in Design		AOIIVE	
Albion Riverside Park			
Rory M. Shaw Wetlands Park*	+	· /	
Projects in Bid & Award		<u> </u>	
Penmar Water Quality Improvement Phase II			<b>√</b>
Temescal Canyon Park Stormwater BMP Phase II			
Projects in Construction			<u> </u>
Avalon Green Alley South	T		<b>√</b>
Broadway Neighborhood Stormwater Greenway			· ·
Catch Basin Inserts & Opening Screen Covers Phase IV*		<b>✓</b>	•
Machado Lake Ecosystem Rehabilitation			
Machado Lake Phase I (Wilmington Drain)	<b>✓</b>	,	
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 3 Phase II	·		
Projects in Post Construction	· ·		
Albion Dairy Park – Demolition & Remediation			
Elmer Avenue Phase II: Elmer Paseo			
Temescal Canyon Park Stormwater BMP Phase I			
Projects Completed			
Albion Dairy Park – Land Acquisition*			
Catch Basin Inserts and Coverings Phase I			
Catch Basin Opening Screen Covers Phase II			
Catch Basin Opening Screen Covers Phase III*			
Cesar Chavez Ground Water Improvement* (a.k.a. Sheldon Arleta)			
Echo Park Lake Rehabilitation			
Glenoaks/Sunland Stormwater Capture			
Grand Blvd. Tree Wells			
Hansen Dam Wetlands Restoration			
Imperial Highway Sunken Median Stormwater BMP			
Inner Cabrillo Beach Bacterial Water Quality Improvement*			
Los Angeles Zoo Parking Lot			
Mar Vista Recreation Center Stormwater BMP			
Oros Green Street			
Peck Park Canyon Enhancement			
Penmar Water Quality Improvement Phase I			
Rosecrans Recreation Center Stormwater Enhancements*			
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 1			
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 2			
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 3			
Santa Monica Bay Low Flow Diversion Upgrades Pkg. 4		<u></u>	
South Los Angeles Wetlands Park		<u></u>	
Strathern Pit Multiuse – Land Acquisition*			<u> </u>
Westminster Dog Park Stormwater BMP			
Westside Park Rainwater Irrigation			
*Schedule not controlled by Prop O			

<sup>\*</sup>Schedule not controlled by Prop O

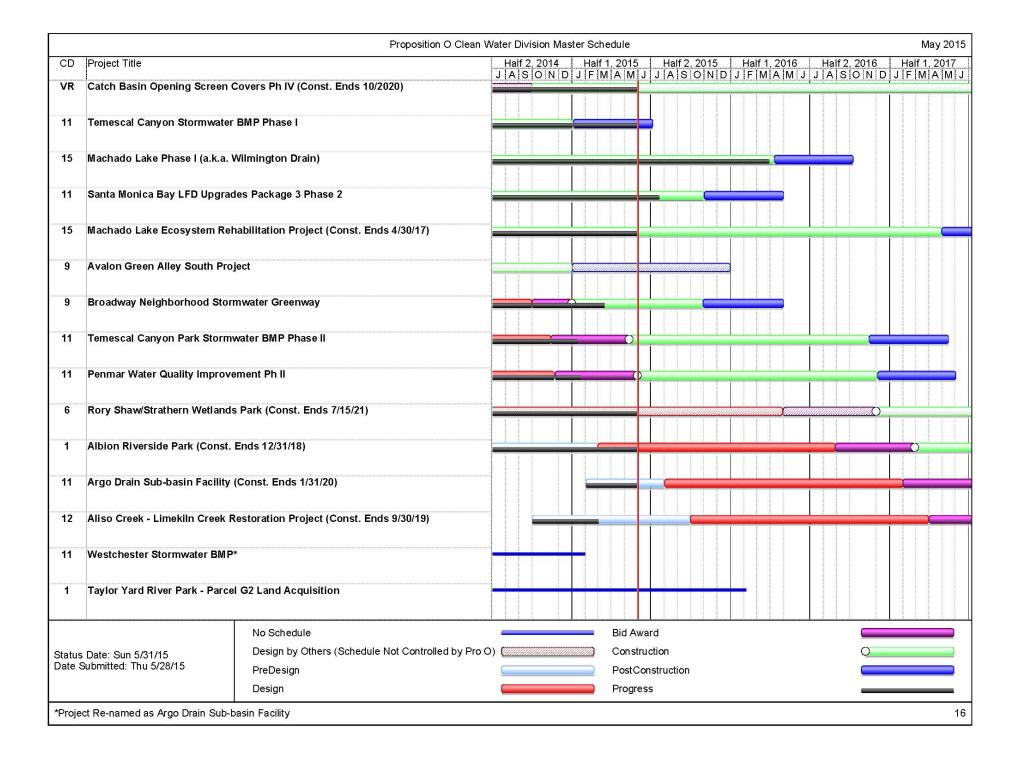



#### 3.0 PROP O PROGRAM BUDGET

### 3.1 Budget vs. Actual Expenditure

Project		Original Prop O Budget	Current Prop O Budget	April Expenditures	Prop O Expenditures as of April 30, 2015
Albion Dairy Park Demolition & Remediation	Land Asquisition	ΦO	<b>#</b> 0	ФО.	to.
Remediation	Land Acquisition Pre-Design/Design/	\$0	\$0	\$0	\$0
Funding Category 3	Construction Management	\$816,400	\$816,400	\$983	\$2,199,380
	Construction Cost	\$3,140,000	\$6,140,000	\$0	\$4,093,136
	Sub-total	\$3,956,400	\$6,956,400	\$983	\$6,292,516
Albion Dairy Park Land Acquisition	Land Acquisition Pre-Design/Design/	\$17,560,000	\$17,537,311	\$0	\$17,471,528
Funding Category 2	Construction Management	\$0	\$0	\$0	\$65,686
PRE-CLOSEOUT	Construction Cost	\$0	\$0	\$0	\$0
	Sub-total	\$17,560,000	\$17,537,311	\$0	\$17,537,214
Albion Riverside Park Improvements	Land Acquisition Pre-Design/Design/	\$0	\$0	\$0	\$0
Funding Category 2	Construction Management	\$2,907,000	\$2,907,000	\$11,348	\$420,952
	Construction Cost	\$8,548,000	\$8,548,000	\$0	\$0
		\$11,455,000	\$11,455,000	\$11,348	\$420,952
Aliso Creek-Limekiln Creek Restoration	Land Acquisition Pre-Design/Design/	\$0	\$0	\$0	\$0
Funding Category 2	Construction Management	\$1,595,089	\$1,595,089	\$141	\$32,732
	Construction Cost	\$0	\$0	\$0	\$0
	-	\$1,595,089	\$1,595,089	\$141	\$32,732
Argo Drain Sub-basin Facility					
	Land Acquisition	\$0	\$0	\$0	\$0
Funding Category 1, 2, & 4	Pre-Design/Design/ Construction Management	\$3,622,200	\$3,622,000	\$8,427	\$8,427
	Construction Cost	\$26,500,000	\$26,500,000	\$0	\$0
	•	\$30,122,200	\$30,122,000	\$8,427	\$8,427
Avalon Green Alley South	Land Acquisition	\$0	\$0	\$0	\$0
Avaion Green Alley South	Pre-Design/Design/	ΦΟ	Φυ	Φ0	\$0
Funding Category 2 and 4	Construction Management	\$481,913	\$481,913	\$3,818	\$9,642
	Construction Cost	\$1,120,729	\$1,120,729	\$0	\$0
	Sub-total	\$1,602,642	\$1,602,642	\$3,818	\$9,642
Broadway Neighborhood Stormwater					
Greenway	Land Acquisition	\$200,000	\$200,000	\$0	\$473,945
Funding Category 2 and 4	Pre-Design/Design/ Construction Management	\$1,331,046	\$1,331,046	\$19,460	\$468,964
r anang category z ana r	Construction Cost	\$3,095,456	\$3,095,456	\$0	\$0
	Sub-total	\$4,626,502	\$4,626,502	\$19,460	\$942,909
Catch Basin Inserts and Coverings Ph					
I	Land Acquisition	\$0	\$0	\$0	\$0
Funding Cotogony 1	Pre-Design/Design/	<b>#0.400.000</b>	<b>#500.047</b>	00	<b>#</b> 500.047
Funding Category 1	Construction Management Construction Cost	\$2,100,000 \$14,900,000	\$560,017 \$14,142,869	\$0 \$0	\$560,017 \$14,142,869
COUNCIL/MAYOR APPROVED CLOSE-OUT	Sub-total	\$17,000,000	\$14,702,886	<b>\$0</b>	\$14,702,886
Catch Basin Opening Screen Covers Ph					
II	Land Acquisition	\$0	\$0	\$0	\$0
	Pre-Design/Design/				
Funding Category 1	Construction Management	\$0	\$383,822	\$0	\$383,822
COUNCIL/MAYOR APPROVED CLOSE-OUT	Construction Cost Sub-total	\$10,000,000 <b>\$10,000,000</b>	\$9,246,965 <b>\$9,630,788</b>	\$0 \$0	\$9,246,965
	Sub-total	φ10,000,000	φ <del>9</del> ,030,768	ΦU	\$9,630,788

Project		Original Prop O Budget	Current Prop O Budget	April Expenditures	Prop O Expenditures as of April 30, 2015
Catch Basin Opening Screen Covers P					
III	Land Acquisition Pre-Design/Design/	\$0	\$0	\$0	\$0
Funding Category 1 & 4	Construction Management	\$2,475,000	\$2,475,000	\$9,003	\$5,363,278
	Construction Cost	\$42,025,000	\$42,025,000	\$0	\$38,067,224
	Sub-total	\$44,500,000	\$44,500,000	\$9,003	\$43,430,502
Catch Basin Opening Screen Covers P	h				
IV	Land Acquisition	\$0	\$0	\$0	\$0
	Pre-Design/Design/				
Funding Category 1 & 4	Construction Management Construction Cost	\$0	\$3,400,000	\$82,943	\$924,703
	Construction Cost	\$0 \$0	\$2,760,000 <b>\$6,160,000</b>	\$0 \$82,943	\$924,703
0 0b 0 d W-t		φυ	\$0,100,000	\$02,943	ψ <b>324,703</b>
Cesar Chavez Ground Water	Land Acquisition	<b>#</b> 0	ФО.	ФО.	ΦO.
Improvement	Pre-Design/Design/	\$0	\$0	\$0	\$0
Funding Category 2	Construction Management	\$1,234,950	\$712,248	\$0	\$712,248
	Construction Cost	\$1,805,050	\$1,815,625	\$0	\$1,815,625
COUNCIL/MAYOR APPROVED CLOSE-OUT	Sub-total	\$3,040,000	\$2,527,873	\$0	\$2,527,873
Echo Park Lake Rehabilitation	Land Acquisition	\$0	\$0	\$0	\$0
Funding Catagony 1 2 2 8 4	Pre-Design/Design/	<b>#10 500 701</b>	<b>#</b> 40,000,000	<b>#</b> 400	<b>#40.500.000</b>
Funding Category 1, 2, 3, & 4	Construction Management Construction Cost	\$19,569,791 \$64,693,522	\$13,600,000 \$31,696,789	\$136 \$0	\$10,560,220 \$26,065,517
	Sub-total	\$84,263,313	\$45,296,789	\$136	\$36,625,737
_	- Jub-total	φ04,203,313	\$43,230,703	ψ130	ψ30,023,131
Elmer Avenue Phase II: Elmer Paseo	Land Acquisition	\$0	\$0	\$0	\$0
Funding Category 3	Pre-Design/Design/ Construction Management	¢249.000	\$318,900	\$36	\$274,561
Tunding Category 3	Construction Cost	\$318,900 \$510,100	\$510,900 \$510,100	\$0 \$0	\$469,042
	Sub-total	\$829,000	\$829,000	\$36	\$743,603
Glenoak/Sunland Stormwater Capture		· · ·		·	. ,
•	Land Acquisition	\$0	\$0	\$0	\$0
From Nove Octobrom 0	Pre-Design/Design/	\$168,696	\$168,696	•	***
Funding Category 3	Construction Management Construction Cost		\$340,000	\$0 \$0	\$33,487 \$0
	Sub-total	\$340,000 \$508,696	\$508,696	\$0 \$0	\$33,487
		<b>\$300,030</b>	4300,030	Ψ	\$33,407
Grand Blvd. Tree Wells	Land Acquisition	\$0	\$0	\$0	\$0
Funding Catagon 4	Pre-Design/Design/	40.40.007	4000 505	•	<b>*</b>
Funding Category 1	Construction Management Construction Cost	\$248,927 \$827,000	\$330,595 \$382,444	\$0 \$0	\$196,021 \$382,444
COUNCIL/MAYOR APPROVED CLOSE-OUT	Sub-total	\$1,075,927	\$713,039	\$0	\$578,465
	Sub-total	\$1,075,927	φ <i>τ</i> 13,039	ψU	\$376,403
Hansen Dam Wetland	Land Association	•		•	40
Restoration	Land Acquisition	\$0	\$0	\$0	\$0
Funding Category 3	Pre-Design/Design/ Construction Management	\$637,302	\$637,302	\$0	\$467,303
gg, -	Construction Cost	\$1,583,400	\$1,583,400	\$0	\$1,345,488
PRE-CLOSEOUT	Sub total				
	Sub-total	\$2,220,702	\$2,220,702	\$0	\$1,812,791
Immedial Hung Combon Mr. "					
Imperial Hwy Sunken Median	Land Acquisition	<b>#</b> 0	40	00	^^
Stormwater BMP	Land Acquisition Pre-Design/Design/	\$0	\$0	\$0	\$0
Funding Category 1	Construction Management	\$505,700	\$537,188	\$0	\$537,188
	Construction Cost	\$2,217,703	\$764,536	\$0	\$764,536
COUNCIL/MAYOR APPROVED CLOSE-OUT			_		_

Project		Original Prop O Budget	Current Prop O Budget	April Expenditures	Prop O Expenditures as of April 30, 2015
Inner Cabrillo Beach Bacterial Water Quality Improvement	Land Acquisition	N/A	N/A	N/A	N/A
addity improvement	Pre-Design/Design/	IV/A	14/7	N/A	19/74
Funding Category 1	Construction Management	\$1,043,478	\$1,043,478	\$0	\$14,455
	Construction Cost	\$6,956,522	\$6,956,522	\$0	\$6,906,550
	Sub-total	\$8,000,000	\$8,000,000	\$0	\$6,921,005
La Cianaga/Fairfay Ctarmyyatar DMD					
La Cienega/Fairfax Stormwater BMP (Canceled)	Land Acquisition	\$0	\$0	\$0	\$0
(Gancelea)	Pre-Design/Design/	ΨΟ	ΨΟ	ΨΟ	ΨΟ
Funding Category 1	Construction Management	\$2,050,388	\$668,159	\$0	\$668,159
CANCELED	Construction Cost	\$5,617,500	\$0	\$0	\$0
CANCELED	Sub-total	\$7,667,888	\$668,159	\$0	\$668,159
LA Zoo Parking Lot	Land Acquisition	\$0	\$0	\$0	\$0
	Pre-Design/Design/				
Funding Category 1 & 3	Construction Management	\$2,774,743	\$1,726,283	\$0	\$1,726,283
COUNCIL/MAYOR APPROVED CLOSE-OUT	Construction Cost	\$11,129,500	\$4,514,172	\$0	\$4,514,172
	Sub-total	\$13,904,243	\$6,240,455	\$0	\$6,240,455
Machado Lake - Phase I (Wilmington					
Drain)	Land Acquisition	\$0	\$0	\$0	\$0
- " o	Pre-Design/Design/			*	*
Funding Category 1 & 3	Construction Management Construction Cost	\$5,298,626	\$5,298,626	\$53,441	\$6,634,026
	Sub-total	\$15,751,285 <b>\$21,049,911</b>	\$15,751,285 <b>\$21,049,911</b>	\$94,825 <b>\$148,266</b>	\$14,960,724 \$21,594,750
	Sub-total	\$21,049,911	\$21,049,911	\$140,200	\$21,394,730
Machado Lake Ecosystem	Lond Annuinition	•		•	<b>^</b>
Rehabilitation	Land Acquisition Pre-Design/Design/	\$0	\$0	\$0	\$0
Funding Category 1 & 3	Construction Management	\$23,113,996	\$20,369,499	\$238,551	\$11,631,665
	Construction Cost	\$76,409,901	\$90,088,064	\$3,020,166	\$23,980,919
	Sub-total	\$99,523,897	\$110,457,563	\$3,258,717	\$35,612,583
Mar Vista Recreation Center					
Stormwater BMP	Land Acquisition	\$0	\$0	\$0	\$0
	Pre-Design/Design/				
Funding Category 1	Construction Management	\$1,130,482	\$1,130,482	\$300	\$1,686,392
	Construction Cost	\$3,425,704	\$3,425,704	\$0 \$200	\$2,482,436 \$4,168,827
	Sub-total	\$4,556,186	\$4,556,186	\$300	\$4,168,827
Oros Green Street	Land Acquisition	\$0	\$0	\$0	\$0
Funding Category 4	Pre-Design/Design/ Construction Management	\$300,000	\$1,325	\$0	\$1,325
	Construction Cost	\$86,000	\$1,323 \$197,600	\$0 \$0	\$197,600
COUNCIL/MAYOR APPROVED CLOSE-OUT	Sub-total	\$386,000	\$198,924	\$0	\$198,924
Peck Park Canyon Enhancement	Land Acquisition	\$0	\$0	\$0	\$0
- II	Pre-Design/Design/				
Funding Category 3	Construction Management Construction Cost	\$714,662	\$714,662	\$0	\$2,882,848
	-	\$5,475,338 \$6,400,000	\$5,475,338 \$6,100,000	\$0 \$0	\$2,578,129 \$5,460,977
	Sub-total	\$6,190,000	\$6,190,000	\$0	\$5,460,977
Penmar Water Quality Improvement					
Phase I	Land Acquisition	\$0	\$0	\$0	\$0
Funding Category 2 & 4	Pre-Design/Design/ Construction Management	\$3,946,800	\$4,600,000	\$0	\$4,390,881
	Construction Cost	\$16,808,000	\$13,154,800	\$0 \$0	\$12,928,225
	Sub-total	\$20,754,800	\$17,754,800	\$0	\$17,319,106

Project		Original Prop O Budget	Current Prop O Budget	April Expenditures	Prop O Expenditures as of April 30, 2015
Penmar Water Quality Improvement	Lond Annual Man				
Phase II	Land Acquisition	\$0	\$0	\$0	\$0
Funding Category 4	Pre-Design/Design/ Construction Management	\$538,200	\$1,582,000	\$3,706	\$430,120
· anamy caregory ·	Construction Cost	\$2,292,000	\$4,248,200	\$0	\$0
	Sub-total	\$2,830,200	\$5,830,200	\$3,706	\$430,120
Rory M. Shaw Wetlands Park	Land Acquisition	\$0	\$0	\$0	\$0
Nory III. Onaw Westands Fark	Pre-Design/Design/	Ψ	ΨΟ	Ψ	Ψ
Funding Category 2	Construction Management	\$0	\$0	\$0	\$8,918
	Construction Cost	\$7,800,000	\$7,800,000	\$0	\$0
	Sub-total	\$7,800,000	\$7,800,000	\$0	\$8,918
Rosecrans Recreation Center	Land Association	•	•	•	•
Stormwater Enhancements	Land Acquisition	\$0	\$0	\$0	\$0
Funding Category 3 & 4	Pre-Design/Design/ Construction Management	\$1,106,427	\$1,106,427	\$0	\$144,737
PRE-CLOSEOUT	Construction Cost	\$3,722,692	\$3,722,692	\$0	\$2,833,498
	Sub-total	\$4,829,119	\$4,829,119	\$0	\$2,978,235
0 / 11 / 12   12   13   14   15   15   15   15   15   15   15		· · · · · · · · · · · · · · · · · · ·			, , , , , , , , ,
Santa Monica Bay Low Flow Diversion	Land Acquisition	\$0	<b>\$</b> 0	<b>¢</b> 0	¢4 222 406
Upgrades P 1	Pre-Design/Design/	\$0	\$0	\$0	\$1,233,496
Funding Category 1	Construction Management	\$1,864,976	\$1,413,342	\$0	\$3,193,291
PRE-CLOSE-OUT	Construction Cost	\$4,949,401	\$3,199,746	\$0	ψο, του, 20 τ
	Sub-total	\$6,814,377	\$4,613,087	\$0	\$4,426,787
Santa Monica Bay Low Flow Diversion				<u></u>	.,,,
Upgrades P 2	Land Acquisition	\$0	\$0	\$0	\$852,235
069.4400.	Pre-Design/Design/	Ψ°	Ψ*	Ψ.	<b>4002,200</b>
Funding Category 1	Construction Management	\$925,077	\$858,394	\$0	\$1,173,948
PRE-CLOSE-OUT	Construction Cost	\$2,455,034	\$1,173,948	\$0	
	Sub-total	\$3,380,111	\$2,032,341	\$0	\$2,026,183
Santa Monica Bay Low Flow Diversion					
Upgrades P 3	Right of Way	\$2,000,000	\$2,000,000	\$11,170	\$506,265
	Pre-Design/Design/				
Funding Category 1	Construction Management	\$5,378,778	\$3,627,036	\$0	\$3,640,026
PRE-CLOSEOUT	Construction Cost	\$13,255,258	\$8,452,072	\$0	\$8,446,053
	Sub-total	\$20,634,036	\$14,079,108	\$11,170	\$12,592,344
Santa Monica Bay Low Flow Diversion					
Upgrades P 3 Phase 2	Right of Way	\$0	\$250,795	\$0	\$0
For the Cotton of A	Pre-Design/Design/	<b>^</b>	<b>04 700</b> 400	0005.050	<b>*</b> 4 <b>*** *** ** ** ** ** **</b>
Funding Category 1	Construction Management Construction Cost	\$0	\$1,790,120	\$285,356	\$1,804,702
	Sub-total	\$0 <b>\$0</b>	\$12,153,554 <b>\$14,194,469</b>	\$582,159 <b>\$867,514</b>	\$7,665,026 \$9,469,728
	3ub-total	Ψ0	Ψ14,134,403	4007,314	ψ3,403,720
Santa Monica Bay Low Flow Diversion	Land Acquisition				
Upgrades P 4	·	\$0	\$0	\$0	\$0
Funding Catagony 1	Pre-Design/Design/ Construction Management	£4.704.004	<b>#4.424.020</b>	<b>(</b> C)	£4 207 774
Funding Category 1 PRE-CLOSEOUT	Construction Cost	\$1,721,601	\$1,434,020 \$2,457,043	\$0 \$0	\$1,367,771
THE OLOGEOUT	Sub-total	\$4,568,903 <b>\$6,290,504</b>	\$2,457,042 <b>\$3,891,062</b>	\$0 <b>\$0</b>	\$2,457,042 \$3,824,813
	Oub-total	ψ0,230,304	Ψ0,031,00Z	Ψ	ψ5,02-7,013
South Los Angeles Wetlands Park					
(includes Site Readiness)	Land Acquisition	\$2,011,937	\$0	\$0	\$5,973,306
( )	Pre-Design/Design/	Ψ=,σ,σσι	40	40	ψο,σ. ο,σσσ
Funding Category 3	Construction Management	\$4,466,265	\$6,591,664	\$0	\$3,856,068
DDE OLOGEOUT	Construction Cost	\$10,200,000	\$5,786,538	\$0	
PRE-CLOSEOUT	Sub-total	\$16,678,202	\$12,378,202	\$0	\$9,829,374

Project		Original Prop O Budget	Current Prop O Budget	April Expenditures	Prop O Expenditures as of April 30, 2015
Strathern Pit Multiuse -Land Acquisition	•	\$10,000,000	\$10,000,000	\$0	\$0
Funding Category 2	Pre-Design/Design/ Construction Management	Φ0	<b>#</b> 0	<b>#</b> 0	<b>#0.770</b>
runding Category 2	Construction Cost	\$0 \$0	\$0 \$0	\$0 \$0	\$2,770 \$0
	Sub-total	\$10,000,000	\$10,000,000	\$0	\$2,770
	Land Acquisition	\$12,440,000	\$12,400,000	\$0	\$0
Taylor Yard River Park - Parcel G2	Pre-Design/Design/	, ,,,,,,,,,	, , , , , , , , , , , , , , , , , , , ,	•	•
Land Acquisition	Construction Management	\$0		\$2,943	\$48,034
Funding Category 3 & 4	Construction Cost	\$0	\$0	\$0	\$0
	Sub-total	\$12,440,000	\$12,400,000	\$2,943	\$48,034
	Land Acquisition	\$0	\$0	\$0	\$0
Temescal Canyon Park Stormwater BMP Phase I	Pre-Design/Design/ Construction Management	\$2,842,626	\$5,122,699	\$5,405	\$5,053,101
Funding Category 3 & 4	Construction Cost	\$12,104,809	\$9,124,736	\$5,405 \$0	\$8,636,389
3	Sub-total	\$14,947,435	\$14,247,435	\$5,405	\$13,689,490
Townson Convey Book Starmwater			-		
Temescal Canyon Park Stormwater BMP Phase II	Land Acquisition	\$0	\$0	\$0	\$0
J 1 11000 11	Pre-Design/Design/	Ψ	Ψ	Ψ	Ψ
Funding Category 3 & 4	Construction Management	\$703,374	\$803,374	\$5,445	\$517,588
	Construction Cost	\$2,995,191	\$3,595,191	\$0	\$0
	Sub-total	\$3,698,565	\$4,398,565	\$5,445	\$517,588
Westchester Stormwater BMP					
(Renamed Argo)	Land Acquisition	\$0	\$0	\$0	\$0
- "	Pre-Design/Design/		*	****	*****
Funding Category 1, 2, & 4	Construction Management Construction Cost	\$2,574,787 \$0	\$2,574,787 \$0	\$11,804 \$0	\$2,621,122 \$0
	Sub-total	\$2,574,787	\$2,574,787	\$11,804	\$2,621,122
	- Cub total	42,014,101	Ψ2,014,101	Ψ11,004	<b>V</b> 2,021,122
Westminster Dog Park Stormwater BM	P Land Acquisition	\$0	\$0	\$0	\$0
Westimister bog i ark stormwater bin	Pre-Design/Design/	ΨΟ	ΨΟ	ΨΟ	ΨΟ
Funding Category 4	Construction Management	\$279,755	\$432,928	\$0	\$270,351
COUNCIL/MAYOR APPROVED CLOSE-OUT	Construction Cost	\$1,159,000	\$254,960	\$0	\$254,960
COUNCIL/MATOR APPROVED CLOSE-001	Sub-total	\$1,438,755	\$687,888	\$0	\$525,311
	Land Acquisition	\$0	\$0	\$0	\$0
Westside Park Rainwater Irrigation	Pre-Design/Design/	04.447.045	<b>44</b> 570 000	•	<b>A</b> 4 000 400
Project	Construction Management Construction Cost	\$1,147,945 \$5,756,644	\$1,572,362 \$2,984,142	\$0 \$0	\$1,280,429 \$3,276,180
Funding Category 1	-				
PRE-CLOSEOUT	Sub-total	\$6,904,589	\$4,556,504	\$0	\$4,556,609
PROJECTS SUBTOTAL		\$510,250,279	\$495,915,206	\$4,443,138	\$303,280,736
Consultant Cost - Program Related Budg	get				
Project Optimization			\$1,616,524	\$75,102	\$608,278
Program Development			\$599,864	\$0	\$599,684
Full Proposal Development			\$360,000	\$0	\$360,000
City Staff - Program Related Budget					
Office of Accounting			\$1,906,709	\$13,459	\$1,286,344
Bureau of Engineering Bureau of Sanitation			\$7,490,358	\$42,033 \$127,012	\$3,703,722
Related Costs			\$16,087,893 \$8,077,839	\$137,912 **	\$11,446,624 **
			, -,,-30		
Arbitrage			\$2,000,000	\$0	\$7,340
Controller			\$2,700	\$0	\$2,700
PROGRAM TOTAL			\$534,057,093	\$4,711,644	\$321,295,429

Expenditures are estimates, and will be adjusted to conform with approved modified indirect labor rated. Estimated expenditures are shown to assist in monitoring of expenses, and are not intended to be financial statements.



#### **4.0 PROJECT STATUS REPORT**

#### 4.1 Project Status Report

A brief status report for each project is provided on the following pages. The report identifies key project information, the planned scope of work, progress date, updated construction costs and percentage complete for all Proposition O projects.

The Percentage Complete at the far right hand column of the diagram uses a color-coding system to designate the current phase of each project.

Turquoise Pre-Design

Yellow Right of Way Acquisition/ Land Acquisition

Red Design

Violet Bid and Award
Green Construction
Blue Post Construction

Progress for each project is tracked by a color-coded pie chart. The color-coding system shows work completed in the darker shade of each color and the lighter shade denotes work to be completed. For example, if a project is in design the pie chart begins as light red. As progress is made, a darker red will indicate the approximate percentage of design work completed to date.






· · · · · · · · · · · · · · · · · · ·	O - Clean Water Bond Program			Monthly	Progress Report - May 2015
ROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION COST	PERCENT COMPLETE
go Drain Sub-basin cility s Angeles World Airport	CD 11 - Mike Bonin  Designer: AECOM  Contractor: TBD  Proj. Mgr.: Salem Garawi  Contact #: 213-847-0345 Concept Report approved by the COAC	Capture and treat stormwater runoff from three existing storm drains through the project BMP elements, including Trash Net System, Underground Detention Tank and Underground Infiltration Facility.	Project is in the pre-design phase.	Notice to Proceed:  Contract Duration: City Engineer's Est. (Class A): Contract Award Amount: \$0 Contract Award + Contingency (24%) CO's to date (#,%): Award Amount +	
And described the final position of the second control of the seco	Mar 2007  Proposed project layout.	Funding: Prop O		CO's Issued \$0  Master Sch. Constr.  Completion Date: JAN 2020	Pre Land Design Bid & Const Award
oion Dairy Park - emolition & Remediation	CD 1 - Gilberto Cedillo	Demolition of the buildings and improvements of an industrial	Project is in the close-out phase.	Notice to Proceed: 7/11/2011 Contract Duration: 661 City Engineer's Est.	
39 N. Albion Street	Designer: Malcolm Pirnie  Contractor: National Demolition	facility, remediation and abatement of all hazardous materials and soils onsite, and the importation of clean soil to leave		(Class A): \$2,468,100 Contract Award Amount: \$1,269,555 Contract Award +	
	Proj. Mgr.: Iftekhar Ahmed  Contact #: 213-485-5875	the property in a level, graded condition.		Contingency (241%) \$4,469,555 CO's to date (24, 223%): \$2,827,281 Award Amount +	
	No Concept Report prepared Photo of project site after remediation.	Funding: Prop O & Brownsfield		CO's Issued \$4,096,836  Master Sch. Constr.  Completion Date: APR 2013	Pre Land Design Bid & Const Award
oion Dairy Park - Land quisition	CD 1 - Gilberto Cedillo	Acquire a parcel of land adjacent to the LA River as part of LA River	The Purchase and Sale Agreement was executed on	Prop O Acquisition Cost: \$17,474,154	
39 N. Albion Street	Designer: N/A	Revitalization Master Plan.	10/2/09. Escrow closed on		
	Contractor: N/A Proj. Mgr.: Kendrick Okuda Contact #: 213-485-1165 Concept Report approved by the COAC Jan 2009	COMPL	10/23/09 Park land acquisition is		100%
bion Riverside Park	Photo of project site.	Funding: Prop O		Acquisition Date:  Notice to Proceed:	Pre Land Design Bid & Const Award
39 Albion Street	CD 1 - Gilberto Cedillo Designer: Tetra Tech	This project will install a series of storm water best management practices. Storm water will be	Project is in design phase.	Contract Duration: City Engineer's Est. (Class A):	
OS AIDIOII SHEEL	Contractor: N/A  Proj. Mgr.: Iftekhar Ahmed  Contact #: 213-485-5875  Concept Report approved by the COAC Oct 2012	diverted from nearby storm drains and utilized/treated with bioswales, bioretention basins, an infiltration tank, and a storage tank.		Contract Award Amount: Contract Award + Contingency (%) CO's to date(, %): Award Amount + CO's Issued	18%
	Rendering of project site.	Funding: Prop O, Prop. 84, & Prop. K		Master Sch. Constr. Completion Date:	Pre Land Design Bid & Const Award





Proposition (	osition O - Clean Water Bond Program				N	Monthly Progress Report - May 2015
PROJECT	CONTACT	ΓS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION CO	OST PERCENT COMPLETE
Aliso Creek-Limekiln Creek					Notice to Proceed:	
Restoration	CD - 12	Mitchell Englander	Construction of BMP's to reduce	Project is in the pre-design phase.	Contract Duration:	
	Designer:	N/A	contaminants to Aliso/ Limekiln Creeks, and the Los Angeles		City Engineer's Est. (Class A):	
			River to assist the City in meeting		Contract Award	
	Contractor:	N/A	TMDL requirements. BMPs		Amount: Contract Award +	
國際學院	Proj. Mgr.:	Andy Flores	include LFD systems, bioswales, vegetated basin, open space		Contingency (%)	
自己的人类原	Contact #:	213-485-4496	restoration of upland and riparian		CO's to date(#,%):	
		ort approved by the COAC	habitat.		Award Amount + CO's Issued	500/
	Nov 2013				Master Sch. Constr.	59%  Pre Land Design Bid & Const Post
	Photo of pro	oject site.	Funding: Prop O		Completion Date:	Design Acquire Award Const
Avalon Green Alley South					Notice to Proceed:	
	CD 9 - Cu	rren Price, Jr.	Construction of stormwater BMPs	Project is in the construction	Contract Duration:	
Alley nw of 54th and San Pedro.	Designer:	The Trust for Public Land	in an alley located in the South Los Angeles area to capture,	phase.	City Engineer's Est. (Class A):	
AND ALLEY	Comtractors	Las Assalas Essissasias	infiltrate, and retain stormwater		Contract Award Amount:	
* * * * * * *	Contractor:	Los Angeles Engineering	runoff from the tributary area: permeable pavers, dry wells, and		Contract Award +	\$0
	Proj. Mgr.:	Iftekhar Ahmed	rainwater harvesting for plant		Contingency (%)	\$0
	Contact #:	213-485-5875	irrigation.		CO's to date(#, %):	\$0
	Concept Rep May 2013	ort approved by the COAC			Award Amount + CO's Issued	\$0 42%
	·				Master Sch. Constr.	Pre Land Design Bid & Const Post Design Acquire Award Const
Droadway Naighbarbaad	Rendering of	of alley improvements.	Funding: Prop O & Prop 84  Construction of stormwater BMPs		Completion Date:	DEC 2014
Broadway Neighborhood Stormwater Greenway		<b>-</b>	of residential BMPs: dry wells,	<del>-</del>	Notice to Proceed:	
Olominator Oroomiay	CD 9 - Cu	rren Price, Jr.	rain gardens, & infiltration	The construction order was issued to Mike Prlich on 4/08/15. A	Contract Duration: City Engineer's Est.	
Vicinity of 48th St & Broadway	Designer:	Carollo	trenches; neighborhood BMPs: sub-surface infiltration basins &	groundbreaking ceremony is being	(Class A):	
	Contractor:	Mike Prlich & Sons, Inc.	dry wells; & a sub-regional facility consisting of a infiltration gallery.	planned. The contractor is expected to begin construction in	Contract Award Amount: Contract Award +	\$0
	Proj. Mgr.:	John Saldin	Estimated construction cost is	May.	Contingency (%)	\$0
	Contact #:	213-485-1411	\$2.6 million.		CO's to date(#, %):	\$0
	Concept Rep May 2013	ort approved by the COAC			Award Amount + CO's Issued	so 30%
	1710y 2010				Master Sch. Constr.	Pre Land Design Bid & Const Post
	Photo of pro	oposed rain garden.	Funding: Prop O & Prop 84		Completion Date:	DEC 2014 Design Acquire Award Const
Cabrito Paseo					Notice to Proceed:	
Walkway/Bike Path	CD 6 - Nu	ry Martinez	Implement stormwater best	Project is on hold due to funding	Contract Duration:	
btwn Marson St. and Raymer St.	Designer:	TBD	management practices including: installation of bioswales, trash	issues. The Los Angeles Neighborhood Land Trust	City Engineer's Est. (Class A):	\$3,095,456
16:10:10:11:61:11:10	Contractor:	TRD	capture devices, tree wells to aid _	(LANLT) is unable to secure	Contract Award Amount:	\$0
			in filtration, and a "SIMART" irrigation system.	additional \$3 million in funds needed to completerthe project.	Contract Award +	
	Proj. Mgr.:	Iftekhar Ahmed		LAN <del>LT requested to withdraw hei</del> r	Contingency (%)	\$0
	Contact #:	213-485-5875		request for project funding.	CO's to date(#, %):	\$0
	Feb 2011	ort approved by the COAC			Award Amount + CO's Issued	\$0
			Funding: Prop O, Kaiser		Master Sch. Constr.	Pre Land Design Bid & Const Post Award Const
	Proposed p	roject site plan.	Foundation, & LANLT		Completion Date:	DEC 2014



Proposition (	O - Clean Water Bond Program			Monthly P	rogress Report - May 2015
PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION COST	PERCENT COMPLETE
Catch Basin Inserts and Covers Phase I	CD: All  Designer: Bureau of Sanitation	Install 8,000 inserts and 6,000 screens in the high trash generation areas, in the City, to	This project is complete.	Notice to Proceed:  Contract Duration:  City Engineer's Est. (Class A): \$14,900,000	
Silvina Silvin	Contractor: Various Proj. Mgr.: Alfredo Magallanes	achieve 20% trash reduction in the Ballona Geekand Los Angeles River Watersheds		Contract Award Amount: N/A Contract Award + Contingency (%) N/A	
	Contact #: 213-485-3958 Concept Report approved by the COAC Jun 2005			CO's to date(#, %): N/A Award Amount + CO's Issued N/A Master Sch. Constr.	re Land Design Bid & Const Post Award Const
Cotob Boois Opening	Photo of catch basin insert.	Funding: Prop O & Prop 40		Completion Date: SEP 2007	
Catch Basin Opening Screen Covers Phase II	CD: All	Install approximately 6,400 screens in medium trash	This project is complete.	Notice to Proceed: Contract Duration: City Engineer's Est.	
Citywide	Designer: Bureau of Sanitation	generation areas, in the City, to increase trash reduction from 20%		(Class A): \$9,400,000 Contract Award	
	Contractor: Various Proj. Mgr.: Alfredo Magallanes	(accomplished in Phase 1) to 30% trash reduction in Ballona Creek and LA River Watersheds.		Amount: N/A Contract Award + Contingency (%) N/A	
	Contact #: 213-485-3958 Concept Report approved by the COAC Aug 2006	60MIL		CO's to date(#, %): N/A Award Amount + CO's Issued N/A	100%
	Photo of catch basin screen cover.	Funding: Prop O		Master Sch. Constr. Completion Date: OCT 2007	esign Acquire Award Const
Catch Basin Opening				Notice to Proceed: 6/1/2008	
Screen Covers Phase III	CD: All	Retrofit of approximately 24,219	This project is complete.	Contract Duration: 730	
Citywide	Designer: Bureau of Sanitation	catch basins with opening screen covers and 2,600 inserts. Includes City-owned catch basins		City Engineer's Est. (Class A): \$42,025,000 Contract Award	
	Contractor: TBD  Proj. Mgr.: Alfredo Magallanes	nor covered in Phases I & II, as well as all/State and County catch basins within the City.		Amount: N/A Contract Award + Contingency (%) N/A	
	Contact #: 213-485-3958 Concept Report approved by the COAC		/	CO's to date(#, %): N/A Award Amount +	
	Feb 2007  Photo of catch basin screen cover.	Funding: Prop O		CO's Issued N/A  Master Sch. Constr.  Completion Date: DEC 2016	re Land Acquire Design Bid & Const Post Const Const
Catch Basin Opening				Notice to Proceed:	
Screen Covers Phase IV	CD: All	Retrofit of catch basins with opening screen covers and	Project is in the construction phase.	Contract Duration: 2112 City Engineer's Est.	
Citywide	Designer: Bureau of Sanitation	inserts. Includes City-owned	για <b>ο</b> σ.	(Class A): \$2,700,000	
	Contractor: TBD	catch basins not covered in Phases I, II, & III as well as all State and County catch basins		Contract Award Amount: N/A Contract Award +	
	Proj. Mgr.: Alfredo Magallanes	within the City.		Contingency (%) N/A	
	Contact #: 213-485-3958 Concept Report approved by the COAC Nov 2013			CO's to date(#, %): N/A Award Amount + CO's Issued N/A	12% te Land Design Bid & Const Post
	Photo of catch basin screen cover.	Funding: Prop O		Master Sch. Constr.  Completion Date: OCT 2020	esign Acquire Design Award Const Const



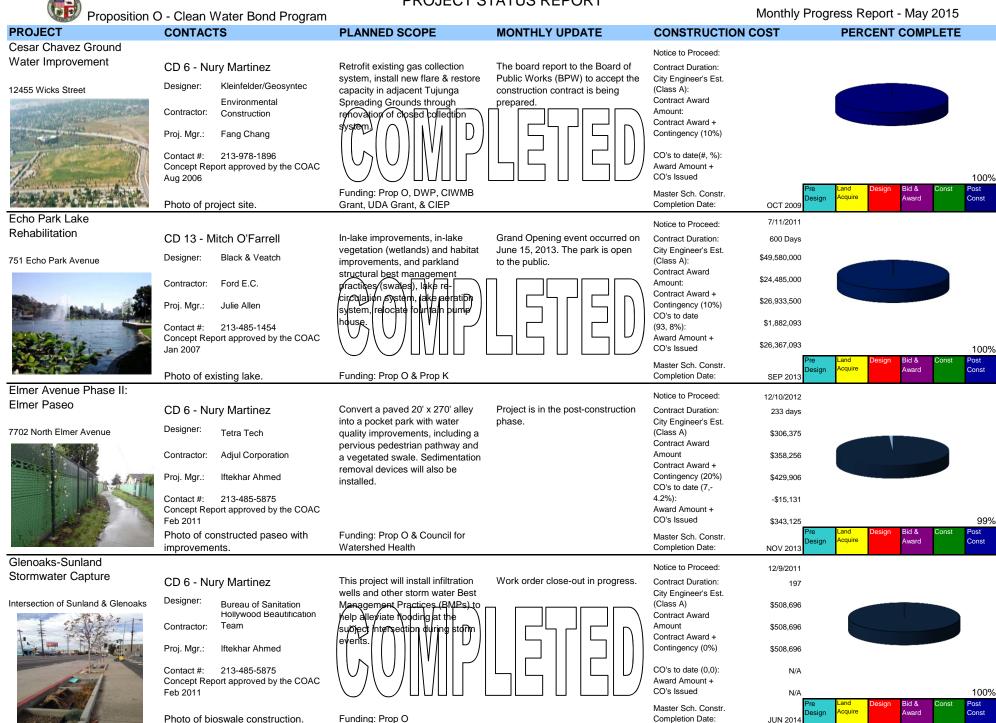




**PROJECT CONTACTS** Grand Blvd. Tree Wells CD 11 - Mike Bonin Designer: **PSOMAS** Intersection Grand & Riviera Contractor: Proj. Mgr.: Andy Flores

#### Monthly Progress Report - May 2015



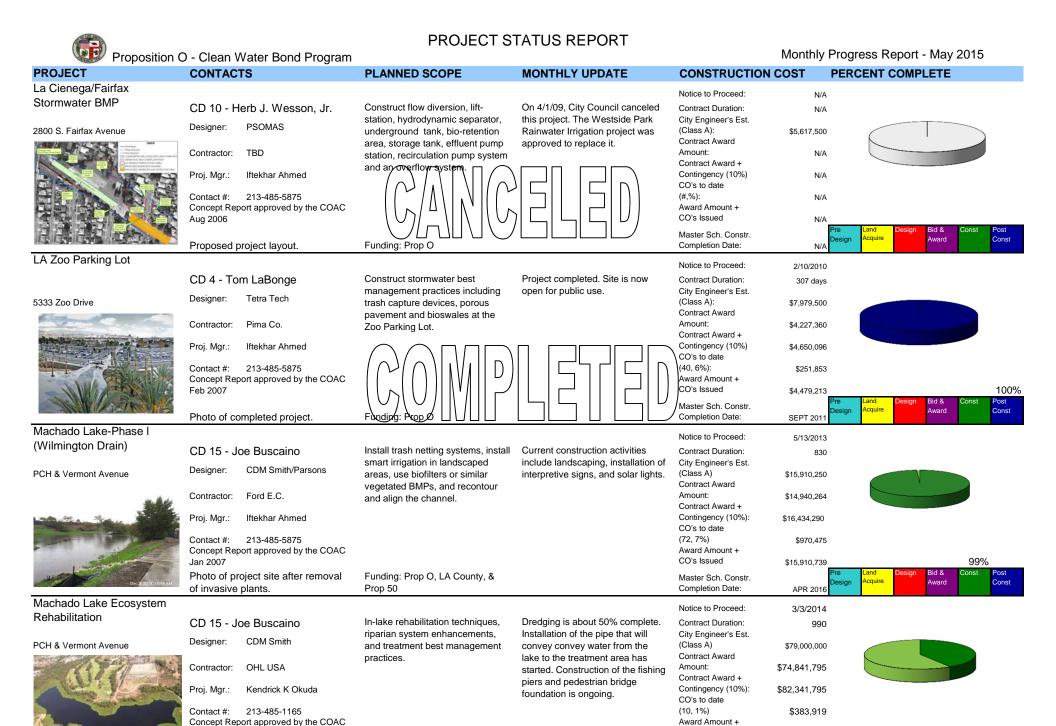

Funding: Prop O, Coastal

Conservancy, Quimby, & Prop K

Jan 2007

Photo of existing lake.

CO's Issued

Master Sch. Constr.


Completion Date:

\$75,225,714

APR 201

#### 28

41%

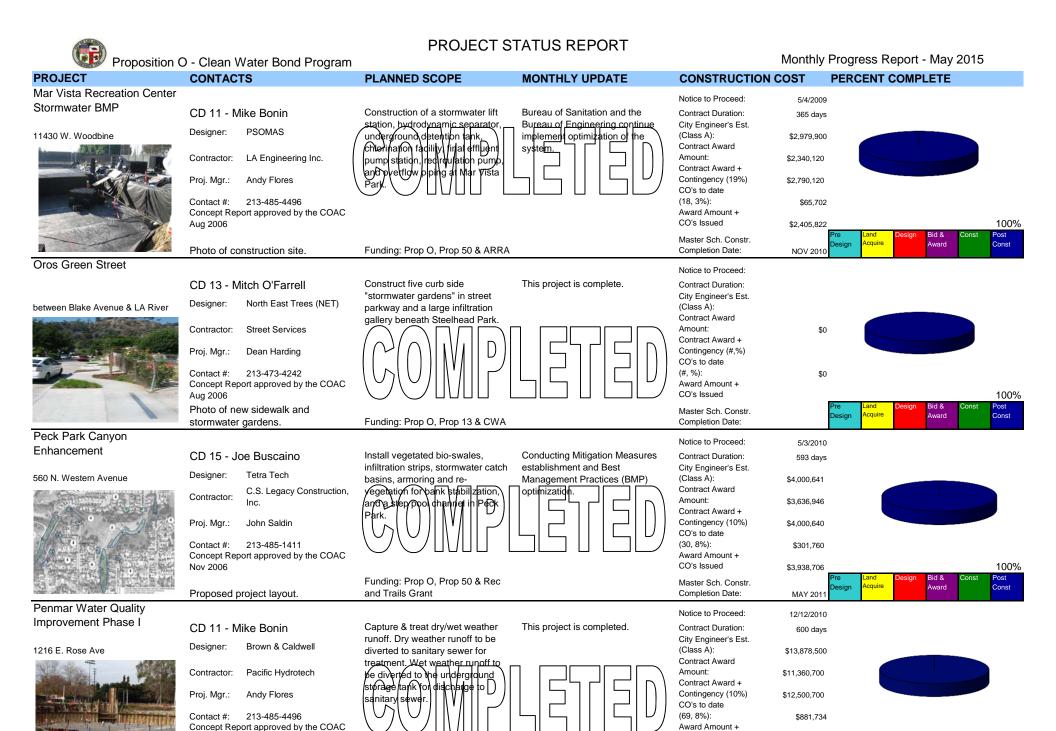

Mar 2007

Photo of construction site.

Funding: Prop O

CO's Issued

Master Sch. Constr.


Completion Date:

\$12,242,434

**DEC 201** 



100%



Proposition 9	O - Clean Water Bond Program	PROJECT S	TATUS REPORT	Month	nly Progress Report - May 2015
PROJECT	CONTACTS	PLANNED SCOPE	MONTHLY UPDATE	CONSTRUCTION COST	PERCENT COMPLETE
Penmar Water Quality Improvement Phase II	CD 11 - Mike Bonin	Phase II of the Penmar Water Quality Improvement Project	This project is in the bid & award phase.	Notice to Proceed: Contract Duration: City Engineer's Est.	
1216 E. Rose Ave	Designer: Carollo Engineers	proposes the construction of an onsite stormwater treatment /	рпаве.	(Class A): \$2,275 Contract Award	,000
San	Contractor: TBD	disinfection system. The treated stormwater is to be used for		Amount: Contract Award +	\$0
The control of the co	Proj. Mgr.: Katie Doherty  Contact #: 213-847-0395  Concept Report approved by the COAC	landscape irrigation.		Contingency (10%) CO's to date (#, %): Award Amount +	\$0 \$0
Programme Control of the Control of	Mar 2007  Proposed project layout.	Funding: Prop O, Prop 84		CO's Issued  Master Sch. Constr.  Completion Date: DEC 2	\$0 32%  Pre Design Design Bid & Const Post Acquire Design Bid & Award Const Post Const Post Design D
Rory M. Shaw Wetlands				Notice to Proceed:	
Park	CD 6 - Nury Martinez	The Strathern Pit Multiuse Project will convert a 30-acre landfill to a	Project continues in the design phase.	Contract Duration: City Engineer's Est.	
8175 & 8216 Fair Avenue	Designer: LA County  Contractor: N/A	wetlands park facility to provide enhanced water quality, flood protection, habitat creation,		(Class A): Contract Award Amount:	\$0
No Street Programme Progra	Proj. Mgr.: Andy Flores	groundwater recharge, recreational and water reuse.		Contract Award + Contingency (10%) CO's to date	\$0
Particular Control of	Contact #: 213-485-4496 Concept Report approved by the COAC Oct 2006			(#,%): Award Amount + CO's Issued	\$0 \$082%
	Proposed project site plan.	Funding: Prop O & LA County		Master Sch. Constr. Completion Date: JUL 2	Pre Land Design Acquire Design Bid & Const Post Const
Rosecrans Rec. Center Stormwater Enhancements	25.5	L II IIOMAA D.T.II	B :	Notice to Proceed: 1/17/2	2011
	CD 15 - Joe Buscaino  Designer: Withers & Sandgren	Install "SMART" irrigation system, bioswales, vegetated retention	Project is complete.	Contract Duration: 640 c City Engineer's Est.	
15000 S. Vermont Avenue	Contractor: Horizon Construction Intl.	basins, infiltration basins, synthetic soccer field, decemposed granite		(Class A): \$3,500 Contract Award Amount: \$3,195	
	Proj. Mgr.: Ray Araujo	pathway, and landsdaping.		Contract Award + Contingency (10%) \$3,515	
THE PARTY OF THE P	Contact #: 213-473-9717 Concept Report approved by the COAC		5L   L L	CO's to date (4, 2%): \$32 Award Amount +	,151
	Nov 2006 Photo of completed construction			CO's Issued \$3,237 Master Sch. Constr.	Pre Land Design Bid & Const Post
OMBI ED III	site.	Funding: Prop O & Prop K		Completion Date: OCT 2	Design Acquire Award Const
SMBLFD Upgrades Pkg 1	CD 11 Mike Benin	Upgrade Marquez, Bay Club,	Project is complete.	Notice to Proceed: 7/6/2  Contract Duration: 366 of	
PCH Several Locations	CD 11 - Mike Bonin  Designer: PSOMAS	Thornton, Venice Pavilion, and Imperial Low Flow Diversion	r roject is complete.	Contract Duration: 366 of City Engineer's Est. (Class A): \$3,714	
1 Off Geveral Educations	Contractor: LA Engineering, Inc.	systems to divert both summer and winter div-weather flows, in		Contract Award Amount: \$3,024	
	Proj. Mgr.: Andy Flores	order to comply with the bacterial		Contract Award + Contingency (10%) \$3,327	,000
	Contact #: 213-485-4496 Concept Report approved by the COAC	regulations.	\  \  \  \  \  \  \  \  \  \  \  \  \  \	CO's to date (26, 6%): \$121 Award Amount +	,970
	Aug 2006			CO's Issued \$3,146	,515 100%

Funding: Prop O, Prop 50 & ARRA

Photo of Marquez Ave. LFD.

Master Sch. Constr.

JUL 2010

Completion Date:

#### PROJECT STATUS REPORT




Photo of channel at diversion site.

Funding: Prop O & Prop 50

Master Sch. Constr.

**APR 201** 

Completion Date:





Master Sch. Constr.


JAN 201


Completion Date:

Photo of playground and new

Funding: Prop O

restrooms.



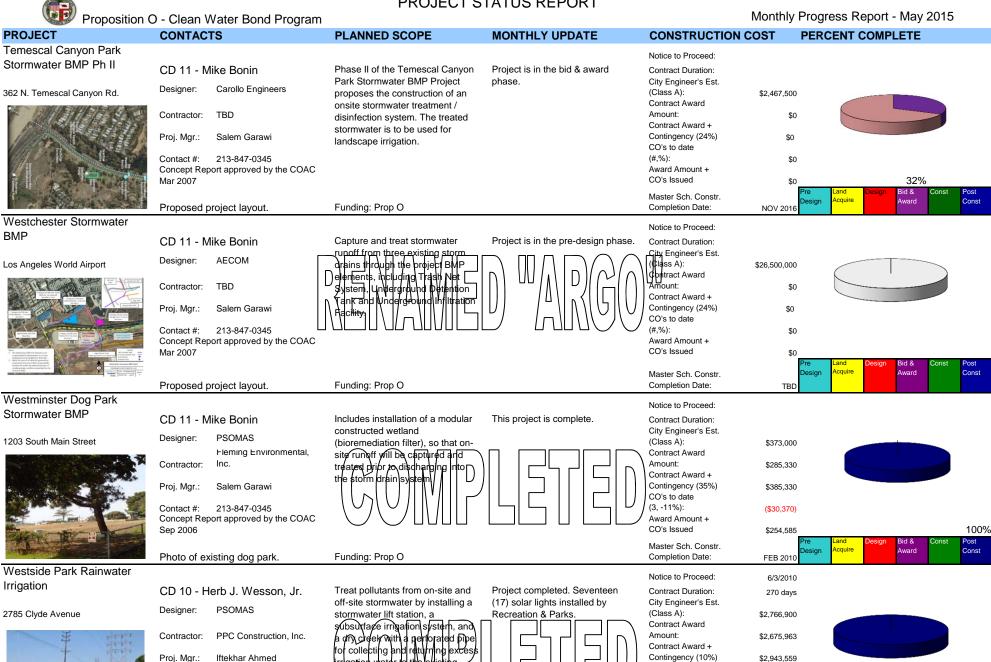

Funding: Prop O, Prop 50, Prop K,

Quimby

213-485-5875

Concept Report approved by the COAC

Photo of completed park.

Contact #:

Mar 2009

CO's to date (37, 22%):

Award Amount + CO's Issued

Master Sch. Constr.

Completion Date:

\$600,216

\$3,276,179

AUG 201

100%

#### 4.2 Project Optimization Status

The table below gives an overview of the optimization scope and status for completed Prop O projects. The optimization tasks for these projects are mandated either by regulatory agency permit requirement, site condition or stakeholders' request.

	Project	Optimization scope	Status
2	Hansen Dam Wetlands Restoration Mar Vista Recreation Center Stormwater BMP Ph 2	Mitigation measures implementation and habitat restoration. Project will prepare annual reports for the regulatory agencies for a period of 5 years.  Optimization of existing BMP is to include stormwater beneficial reuse of the harvested water. The goal is to provide stormwater irrigation for the planter boxes adjoining the tennis courts and to the grass areas west of the tennis courts and south of parking lot along Sawtelle Boulevard. Items to be constructed include pump system, irrigation system, pavement, planter curbing, and installation plantings. The irrigation system will operate as a dual reuse/potable water system. When reuse stormwater is not available for irrigation, the system will automatically use potable water.	The last annual report will be submitted in January 2017.  The Bureau of Sanitation and the Department of Recreation and Parks have agreed on an expanded project scope which will also include stormwater irrigation of the grass areas west of the tennis courts and south of parking lot along Sawtelle Boulevard. Notice to Proceed will be issued this month to an Engineering Firm for preparation of the required plans for construction.



#### **5.0 APPENDIX**

PROJECT PHASE	STATUS				
	Complete				
Phase I	7,620 catch basin inserts 7,900 catch basin curb opening screens covers				
	<ul> <li>Installations coverage addressed the City's high trash generation areas.</li> </ul>				
	Complete				
Phase II	6,400 catch basin curb opening screen covers				
	Installation coverage addressed only a portion of the City's medium trash generation area.				
	Complete				
	24,187 catch basin curb opening screen covers				
Phase III	<ul> <li>Installation coverage addressed the low and medium trash generation areas in the Los Angeles and Ballona Creek watersheds.</li> </ul>				
	• Completed a special study, <i>The Quantification of the City of LA's Institutional Measures for Trash TMDL Compliance</i> . The study resulted in demonstrating the City's institutional measures having a 13.5% effectiveness in the prevention of trash discharges into the storm drain system.				
	In Progress				
	1,600 catch basin inserts (PLANNED)  1,000 catch basin curb opening screen covers (PLANNED)				
	Completed the field evaluation of 250 catch basins in the Machado Lake watershed for feasibility of curb opening screen covers or insert installation.				
	<ul> <li>Completed the field evaluation of 1,150 catch basins in the Dominguez Channel watershed for feasibility of curb opening screen covers or insert installation.</li> </ul>				
Phase IV	• Completed the field evaluation of 1,200 catch basins in the Santa Monica Bay watershed for feasibility of curb opening screen covers or insert installation.				
Phase IV	• Commenced a special study, <i>Evaluation of an Alternative Curb Opening Screen Cover for Trash TMDL Compliance</i> . It is anticipated study would support a more cost effective alternative for future installations. Final study report to be completed by June 2015.				
	Machado Lake watershed catch basin retrofits tentative start date of July 2015.				
	A Request for Proposal is under LASAN review to establish a contract for the fabrication and installation of curb opening screen covers. Anticipate installation start date late Summer or early Fall 2015.				
	Construction ending date: September 2017				

#### 5.2 Council District Map

See attached

# **5.3** Map of Proposition O Projects Approved for Implementation See attached

